

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

MIT NO 31-096494

BUILDING PERMIT

FOR Single Family Dwelling Remodel
Additions Misc Residential ConstructionLOG NO & AREA T220 DATE 1-3-90 CONST VAL \$ 61600ADDRESS OF CONSTRUCTION 7501 ELLA WY OWNER PLASTER DEVE CO PHONE 385-5031LOT(s) 47 BLOCK 1 SUBDIVISION RIDGEVIEW WEST UNIT 3 ZONE _____PROPOSED CONSTRUCTION SINGLE FAMILY USE RESIDENCETHIS PERMIT FOR BLDG ☒ A/C ☐ ELEC ☒ PLBG ☒ OTHER PERMITS REQD FENCE ☐ OFF SITE ☐ SWIM POOL ☐FLOOR AREA BSMT _____ 1ST 1013 2ND 1073 GARAGE 597 PORCH 36 TOTAL 2719CONTRACTOR PLASTER DEVE. CO., INC. STATE LICENSE NO 017957 CITY LICENSE NO G11-D48-2-14322ARCHITECT _____ ENGINEER VTNMASTER PLUMBER/
CONTRACTOR _____ MASTER ELECTRICIAN/
CONTRACTOR _____

OTHER INSPECTIONS AND FEES

- 1 Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
- 2 Re inspection fee during normal business hours assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30.00 per hour
- 3 Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour)
- 4 Additional plan review required by changes, additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours)

CONDITIONS OF THE PERMIT

- 1 I agree to call the City Building Department for inspections before concrete is poured before rough wiring, electrical plumbing framing is covered. Also for air conditioning drywall and sheathing inspection.
- 2 I agree that when the job is completed that I will call for final inspection before occupancy.
- 3 I agree to perform all construction in accordance with City Ordinances and Building Codes.
- 4 The Contractor's signature below denotes authority from the owner to sign in his behalf and that the owner is aware of all requirements of this application and permit. Separate permits must be taken out for work outlined above this agreement.
- 5 I have read and understand the contents of this application and permit. I hereby state that the information I have supplied on this application is true and correct.
- 6 Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way.
- 7 24 HOUR MINIMUM NOTICE REQUIRED FOR INSPECTIONS.

BY PLASTER DEVELOPMENT CO., INC.

I HEREBY DECLARE THAT I AM THE LEGAL OWNER OF THE ABOVE PROPERTY

OWNER

BY CW BRUBAKER

AGENT

I hereby certify that I have reviewed this application and the proposed plans and have found that the proposed development meets the requirements of the City of Las Vegas Flood Hazard Reduction Ordinance for the issuance of this Development Permit.

LAND DEVELOPMENT AND FLOOD CONTROL ENGINEER

PLANNING DEPT

BUILDING DEPT

SPECIAL CONDITIONS

PLANS ON FILE
PER PLOT PLAN
ACCENT
46C

PLUMBING		FEE	ELECTRICAL		FEE
WATER DISTRIBUTION	6.00		RECEPTACLE _____ SWITCH _____	40	
SEWER SYSTEM NEW OR MODIFICATION	10.00		EACH LIGHT FIXTURE OR SOCKET _____	30	
FIXTURES WATER SOFTENER HW HEATER	2.00		SPECIAL OUTLET APPLIANCE ETC	70	
GARBAGE DISPOSAL WASHER	2.00		SERVICE/PANEL SUB/3.00 200A/6.00 400A/12.50		
FUEL PIPING	6.00		AC UNIT OR MOTORS	3.00	
IRRIGATION SYSTEM	8.00		2310 2432 TOTAL		
MISC			MISC		
2310 2433 TOTAL			2310 2431 ISSUANCE FEE		
AIR CONDITIONING		FEE	7143 2973 SEWER CONNECTION		
NEW UNIT 3 TON = 9.00 OVER = 16.50			2310 2431 PLAN REVIEW FEE		
FURNACE TO 100,000/9.00 OVER/11.00			2310 2431 BLDG PERMIT FEE		
VAPORATIVE COOLER	6.50		TOTAL FEES		
VENTILATION FAN	2.35				
2310 2435 TOTAL					

RECEIPT
0000
SEWR 12750 00
FLCK 300 00
SFD 10425 00
CHCA 29475 00
8510A000 14 41

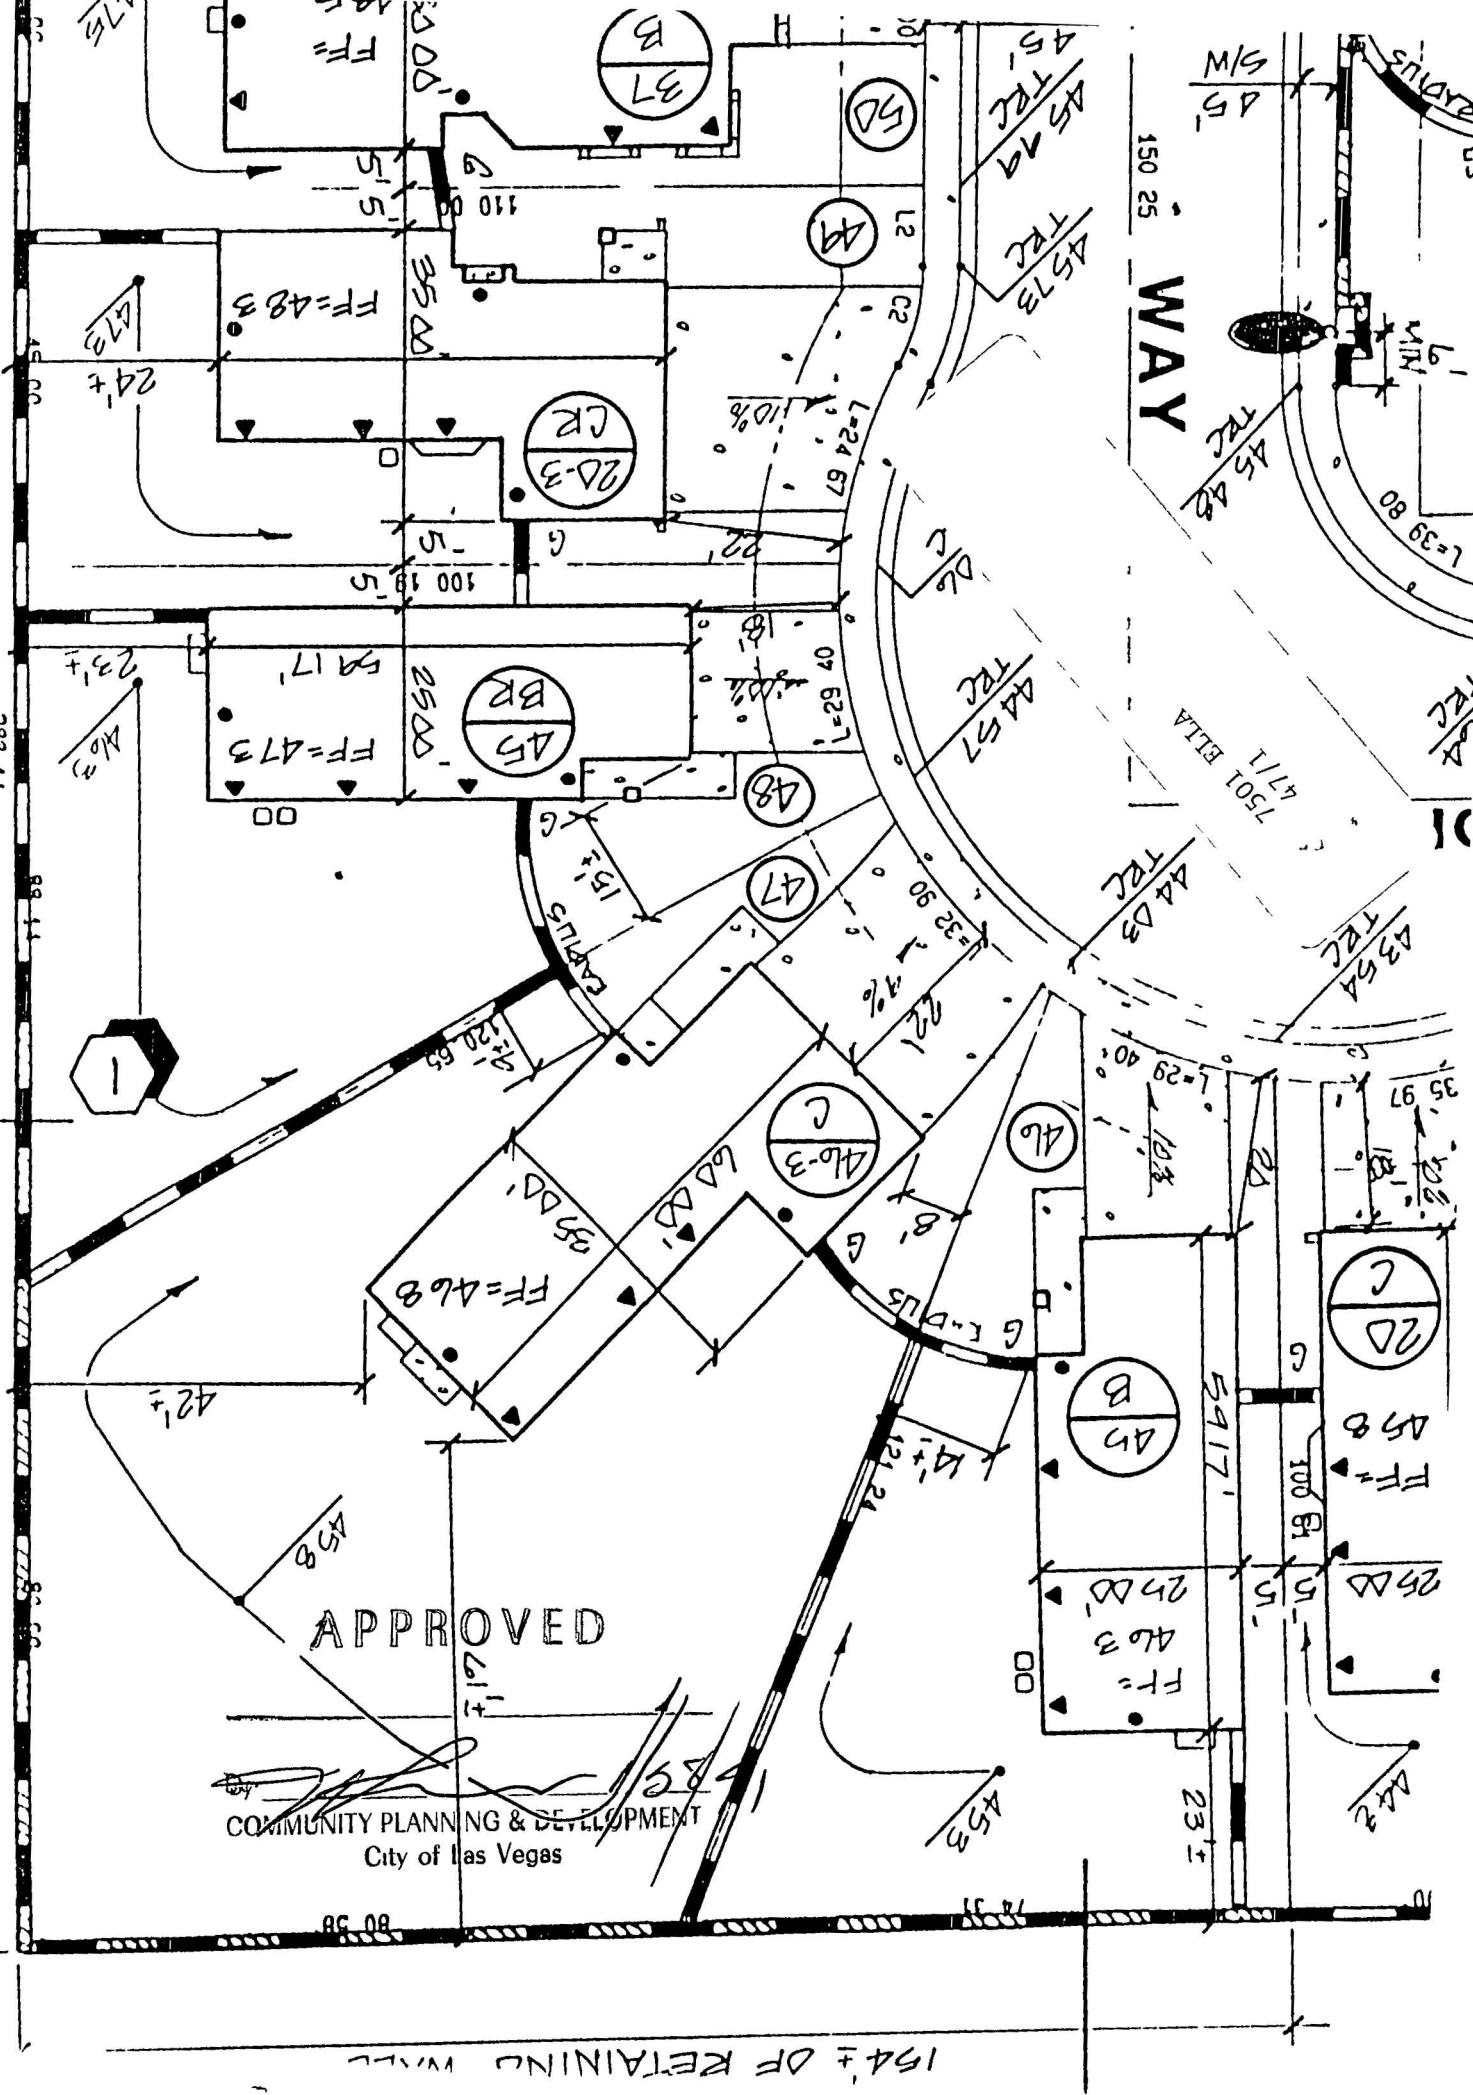
02/04/91

Permit Expires 180 Days After Abandonment of Work

PERMIT NO _____
MUST BE MACHINE VALIDATED

664960-16 1000 W 775 105L

125' ± Δ = RETAINING WALL



CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6254

PERMIT NO

91-097082

PLUMBING PERMIT

LOG NO & AREA

P-220 91

DATE January 10, 1991

CONST VAL \$

final 3-22-91

ADDRESS OF

CONSTRUCTION 7501 Ella Way

OWNER Plaster Development Inc.

PHONE 873-5558

CONTRACTOR Hynds Plumbing & Heating Co.

STATE

LICENSE NO 1021

CITY

LICENSE NO 01660

LOT(s) 47

BLOCK 1

SUBDIVISION Ridgeview Unit 3 - Accent 43

ZONE

PROPOSED CONSTRUCTION Plumbing

USE

S.D

PLUMBING
PERMIT NOApproval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10.00
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
1	Bathtub Shower Lavatory Toilet Urinal	EA 2 00	2.00
1	Floor Drain Floor Sink Wash Tray Sink	EA 2 00	2.00
2	Garbage Disposal Clothes Washer Dishwasher (residential)	EA 2 00	4.00
	Garbage Disposal (commercial)	EA 8 00	
	Clothes Washer Dishwasher (commercial)	EA 2 00	
	Clothes Dryer (gas) (venting)	00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
1	Hot Water Heater (Gas or Electric)	EA 2 00	2.00
SEWER SYSTEM			
1	New Replacement Modification or Any Drainage Work	10 00	10.00
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
	Irrigation Single Family Dwelling	8 00	
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation		

UNITS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
3	Medium Pressure System (Plan Check)	2 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Addtional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTION

RECEIPT

0005

LPG 1888 00

CHEK 1888 00

8794A000 10 38

FIXTURES X 02/02/91

FEE

2310 2403

PERMIT

FEE

TOTAL

FEES \$164.00

PERMIT NO

MUST BE MACHINE VALIDATED

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

Hynds Plumbing & Heating Co.

99

SIGNED

CONTRACTOR

MASTER CARD NO

BY

Registered Master Plumber Spec Cont or Owner

BUILD NO DEPT

DATE

CITY OF LAS VEGAS, NEVADA

PERMIT NO - 097443

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

ELECTRICAL PERMIT

LOG NO & AREA

P220

24911-3

CONST VAL \$

ADDRESS OF

CONSTRUCTION 7501 ELLA WAY

OWNER

SIGNATURE RIDGEVIEW 3

CONTRACTOR BEST ELECTRIC

STATE

LICENSE NO

0019488

CITY

LICENSE NO

C1184122758

HOWARD DUNN LOT/BLK 47/1

PLAN 46C

M1-212

PHONE 367-0050

(PRINT NAME OF MASTER ELECTRICIAN)

PROPOSED CONSTRUCTION

Single Family Dwellings

USE

finished 3-22-91

ELECTRIC

PERMIT NO

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	0.00
0	Supplemental Fee	4 50	0.00
APPLIANCE CHARGE			
Residential or General Commercial			
76	Receptacle 47 Switch 29	40	30.40
22	Each Light Fixture Socket or Exit Light Smoke Detector or Exhaust Fan	30	6.60
9	EACH OUTLET FOR SPECIAL PURPOSE Dishwasher Garbage Grinder Trash Compactor GFI Clothes Washer Dryer Electric Range Ovens Water Heater Space Heater Blast Coil Heater (PER KW) Mercury Lamp Quartz Lamp Sodium Lamp 20AMP Sign Circuit	70	6 30
	X Ray Unit	10 00	
	Area Lighting (First 3 000 Watts)	8 00	
	Each Additional 1 000 Watts	3 00	
MOTORS (1 H P AND OVER) TRANSFORMERS ELEVATORS WELDERS GENERATORS CHILLERS SIGNS AND A/C UNITS (OVER 5 TONS)			
	First H P or Ton For each Unit	3 00	
	First KVA For Each Unit	3 00	
	Each Additional H P Ton or KVA up to 50	50	
	Each Additional H P Ton or KVA over 50	35	
10	Temporary power or Pole	6 00	60.00
ELECTRIC SERVICE OR MAIN DISCONNECT			
1	Up to 200 AMP	6 00	6.00
0	400 AMP And 600 AMP	12 50	0.00
	Over 600 AMP To 1200 AMP	25 00	
	Over 1200 AMP	50 00	
	Each Additional Meter Socket	50	
0	Sub Panel Motor Control Center Disconnect Switch Transfer Switch (Each)	3 00	0.00
	Swimming Pool (Residential)	20 00	
	Swimming Pool (Semi Public)	30 00	
	Spas	8 00	
	Recreational Vehicle Spaces (Each)	3 00	

UNITS	DESCRIPTION	FEE	TOTAL
	Busways Trolley or Plug in (Ea 100 Ft)	3 00	
	Gas Pumps Dispensers (Each)	3 00	
2	Permanent A/C Unit (5 Tons or Less)	3 00	6 00
0	Each Air Handler	1 00	0 00
RESIDENTIAL LOW VOLTAGE INSTALLATIONS			
	Speaker Outlets (Each)	30	
	Signal or Alarm Outlets (Each)	30	
	Amplifiers	2 00	
	Control Panel	50	
2	TV Master System	30	0 60
2	Telephone or Computer Outlet	30	0 60
OTHER INSPECTIONS AND FEES INCLUDES ISSUANCE FEES WHEN APPLICABLE			
	Inspections outside of normal business hours (minimum charge — three hours)	30 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30 00 EACH	30 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — one half hour) After work hours — \$30 00 per hour — minimum 1 hour	30 00 per hour	
	Starter Permit	50 00	
CONTRACT PRICE OR COST OF INSTALLATION			
	Commercial —Burglar Alarms		
	—Music Systems		
	—Data Processing		
	—Communication		
	Conduit Only—Contract Price		
	All Misc Electric		

Electrical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule

2310 2432 02/13/01

RECEIPT

*0000**
 ELEC 1892 00
 CHECK 1872 00
 0011A000 00 EL

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED HOMEOWNER CONTRACTOR

PERMIT

FEE \$126 50

LESS

STARTER PERMIT

TOTAL

FEES

PERMIT NO

MUST BE MACHINE VALIDATED

Permit Expires 180 Days After Abandonment of Work

CITY OF LAS VEGAS, NEVADA

PERMIT 99 - 097473

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

071

AIR CONDITIONING PERMIT

LOG NO & AREA

P-220 '91



24865-1

CONST VAL \$

ADDRESS OF
CONSTRUCTION

7501 ELLA WAY

OWNER PLASTER DEV

PHONE 565-8751

CONTRACTOR CARL'S A/C & S/M INC

STATE
LICENSE NO 8370CITY
LICENSE NO 230-2-10793

LOT(s) 47 BLOCK 1 SUBDIVISION RIDGEVIEW UNIT 3 ACCENT 43

ZONE

PROPOSED CONSTRUCTION COMPLETE INSTALLATION OF A/C AND DUCTWORK

USE

fueled 3-22-91

Approval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For the issuance of each permit	15 00	15 00
	For issuing each supplemental permit	4 50	
UNIT FEE SCHEDULE			
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance up to and including 100 000 Btu/h	9 00	
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance over 100 000 Btu/h	11 00	
	For the installation or relocation of each floor furnace including vent	9 00	
	For the installation or relocation of each suspended heater recessed wall heater or floor mounted unit heater	9 00	
	For the installation relocation or replacement of each appliance vent installed and not included in an appliance permit	4 50	
	For the repair of alteration of or addition to each heating appliance refrigeration unit cooling unit absorption unit or each heating cooling absorption or evaporative cooling system including installation of controls regulated by this code	9 00	
2	For the installation or relocation of each boiler or compressor to and including three tons or each absorption system to and including 100 000 Btu/h	9 00	18 00
	For the installation or relocation of each boiler or compressor over three tons to and including 15 tons or each absorption system over 100 000 Btu/h and including 500 000 Btu/h	16 50	
	For the installation or relocation of each boiler or compressor over 15 tons to and including 30 tons or each absorption system over 500 000 Btu/h to and including 1 000 000 Btu/h	22 50	
	For the installation or relocation of each boiler or compressor over 30 tons to and including 50 tons or for each absorption system over 1 000 000 Btu/h to and including 1 750 000 Btu/h	33 50	
	For the installation or relocation of each boiler or refrigeration compressor over 50 tons or each absorption system over 1 750 000 Btu/h	56 00	

UNITS	DESCRIPTION	FEE	TOTAL
	For each air handling unit to and including 10 000 cubic feet per minute including ducts attached thereto Note This fee shall not apply to an air handling unit which is a portion of a factory assembled appliance cooling unit evaporative cooler or absorption unit for which a permit is required elsewhere in this code	6 50	
	For each air handling unit over 10 000 cfm	11 00	
	For each evaporative cooler other than portable type	6 50	
5	For each ventilation fan	4 50	11 75
	COMMERCIAL RESIDENTIAL	2 35	
	For each ventilation system which is not a portion of any heating or air conditioning system authorized by a permit	6 50	
	For the installation of each hood which is served by mechanical exhaust including the ducts for such hood	6 50	
	For each fire damper installed in an existing system	4 50	
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge — three hours)	25 00 per hour	
	Re inspect on fee assessed under provisions of TABLE 3 A of the Uniform Building Code — \$15 00 EACH	15 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — two hours)	30 00 per hour	
	Mechanical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Gas piping which is directly related and necessary to the repair or replacement of heating air conditioning or refrigeration systems not exceeding 500 000 BTU/H	6 00	

2310-2435

 RECEIPT
 0002
 A/C 1248 85
 PHEX 1248 85
 001-4010 08 57

02/13/91

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED

CONTRACTOR

MASTER CARD NO

PERMIT FEE 15 00

BY

Spec Contractor or Owner

TOTAL FEES \$44,75

BUILDING DEPT

DATE

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

CITY OF LAS VEGAS, NEVADA

PERMIT NO 91-104324

DEPARTMENT OF BUILDING AND SAFETY
PHONE 383 6251DEVELOPMENT PERMIT
FOR Swimming Pool or Spa

LOG NO & AREA m-2999 DATE _____ CONST VAL \$ 6400

ADDRESS OF CONSTRUCTION 7501 E11A WY OWNER Marty Pollinger PHONE 363-4476

CONTRACTOR Designer Pools STATE LICENSE NO 31702 CITY LICENSE NO 045285

LOT(s) 47 BLOCK 1 SUBDIVISION Redwood West 13 ZONE _____

PLUMBING CONTRACTOR _____ ELECTRICAL CONTRACTOR Joseph A. [Signature]

CIRCLE TYPE OF POOL THAT APPLIES PRIVATE Pool SEMI PUBLIC PUBLIC SPA

MATERIALS OF CONSTRUCTION REINFORCED GUNITE REINFORCED CONCRETE OTHER finished 5-29-91

SQUARE FEET OF SURFACE POOL 500 SPA 40 VOLUME IN GALLONS 15,000

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

I state that I am familiar with the effective ordinances of the City of Las Vegas Nevada and the effective Statutes of the State of Nevada covering construction and use of the above type I agree to perform said construction in conformity therewith I further agree that issuance of a permit on the above application will not excuse me from conforming with the said Ordinances and Statutes despite any errors on the part of the building inspector or engineer in checking plans and application herewith

All swimming pools must be fenced before the pool is filled with water No electrical lines shall cross over a pool Applicants must have separate plot plans showing location of power pole proposed or existing fencing and location of swimming pool I agree to repair any utility line if damaged during excavation work I have read and understand the contents of above application I hereby state that the same are true and correct

SIGNED [Signature] CONTRACTOR

BY [Signature] AGENT/OWNER

PLANNING DEPT [Signature] DATE 4-29-91

BUILDING DEPT [Signature] DATE 4-29-91

- 1 Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
- 2 Re Inspection fee during normal business hours assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30.00 each
- 3 Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour)
- 4 Additional plan review required by changes additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours)

DESCRIPTION			FEE	TOTAL
ISSUANCE FEE			10 00	10
SEWER CONNECTION FEE (to 30 000 GALLONS)			63 60 00	63
BUILDING PERMIT POOL & OR SPA				77
PLUMBING PERMIT	PRIVATE POOL OR SPA	PREFORMED SPA	10 00	
		OTHERWISE	20 00	20
	PUBLIC OR SEMI PUBLIC POOL OR SPA	PREFORMED SPA	20 00	
		OTHERWISE	30 00	05/01/91
	FUEL PIPING FOR POOL HEATER		6 00	164
ELECTRICAL PERMIT	SPA		8 00	184
	SWIMMING POOL	RESIDENTIAL	20 00	20
		PUBLIC SEMI PUBLIC	30 00	
	ELECTRICAL SERVICE CHANGE		6 00	
MISC				
TOTAL FEES				204 00

RECEIPT

0002
 POOL 87 00
 SEWR 63 00
 FLPS 26 00
 ELEC 28 00
 CHEK 204 00
 3518A000 14 44

05/01/91

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

{91-096494}

INSTALLATION CARD

JOB ADDRESS

MAGNAWALL 1-KOTE
REINFORCED STUCCO SYSTEM

1-KOTE STUCCO PRODUCTS

ICBO Evaluation Service Inc. Report No 4776

Date of Job Completion _____

PLASTERING CONTRACTOR


Name NICHOLS CONSTRUCTION, INC

Address 625 CABALLO
LAS VEGAS, NV 89119

Approved Contractor Number as Issued by
the Plastering Manufacturing 25

Phone (702) 361-3341

This is to certify that the plastering system on the building exterior at the above address has been installed in accordance with the evaluation report specified above and the manufacturer's instructions


Signature of authorized representative of plastering contractor

_____ Date

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

☐ PERMIT NUMBER 91104824		INSPECTION NUMBER	
JOB ADDRESS 7501 Ella Way			
LOT NO	BLOCK NO Larry	SUBDIVISION NAME	
FIRE DEPT MAP NO Designer Pools	JOB PHONE 3634476	CALL IN DATE 5-1-91	CALL IN TIME 7 254P
INSPECTOR NO 86	INSPECTOR NAME		
INSPECTION REQUESTED preguisite n g elec			
gas OK sticker at final			
☐ PARTIAL INSPECTION	☐ PARTIAL APPROVAL (P)	PARTIAL DESCRIPTION	
☒ APPROVED (A)	☐ STOP WORK (S)	☐ COMMENTS (C)	☐ TEMPORARY APPROVAL (T) - UNTIL
☐ REJECTED (R)		☐ HOLD (H)	
☐ REFEE (F)		☐ PERMIT REQUIRED	
INSPECTOR SIGNATURE M Haler		INSPECTION DATE 3 MAY 91	
☐ PROJECT COMPLETE	BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)		
IF YOU HAVE ANY QUESTIONS ON THIS INSPECTION YOU MAY CALL THE INSPECTOR FROM 7 00 A M 7 15 A M OR 2 45 P M 3 00 P M AT			

FOR ADDITIONAL ASSISTANCE CALL 386-6251
SEE REVERSE SIDE FOR INSPECTION TYPES

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS



**PERMIT
NUMBER**

91104824

**INSPECTION
NUMBER**

JOB ADDRESS

7501 Ella Way

LOT NO

BLOCK NO

SUBDIVISION NAME

Came

FIRE DEPT MAP NO

JOB PHONE

CALL IN DATE

CALL IN TIME

SCHEDULE DATE

Designa Peals

3-21-91

9-936A

INSPECTOR NO

INSPECTOR NAME

71

**INSPECTION
REQUESTED**

preplaster, fence & gates

POOL LITES WILL NOT WORK
GATE MUST BE SELF CLOSING AND
SELF LATCHING

☐ PARTIAL
INSPECTION

☐ PARTIAL
APPROVAL (P)

PARTIAL DESCRIPTION

☐ APPROVED
(A)

☐ STOP
WORK (S)

☐ COMMENTS
(C)

☐ TEMPORARY
APPROVAL (T) - UNTIL

☐ HOLD
(H)

☒ REJECTED (R)

REINSPECTION REQUIRED CALL *799 2071

☐ REFEE (F)

REINSPECTION FEE REQUIRED PAY AT CITY HALL
3RD FLOOR 400 E STEWART STREET

☐ PERMIT
REQUIRED

**INSPECTOR
SIGNATURE**

[Signature]

INSPECTION DATE

22 MAY 91

☐ **PROJECT
COMPLETE**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

IF YOU HAVE ANY QUESTIONS ON THIS INSPECTION YOU MAY
CALL THE INSPECTOR FROM 7 00 A M 7 15 A M OR 2 45 P M 3 00 P M AT

FOR ADDITIONAL ASSISTANCE CALL *386-6251
SEE REVERSE SIDE FOR INSPECTION TYPES

* EFFECTIVE JULY 1 1991
PHONE PREFIX WILL BE 229

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

☐ PERMIT NUMBER		91-104824		☐ INSPECTION NUMBER			
JOB ADDRESS 7501 Ella Way							
LOT NO 363 4476		BLOCK NO Larry		SUBDIVISION NAME			
FIRE DEPT MAP NO Design: Pools		JOB PHONE		CALL IN DATE 6-19-91		CALL IN TIME 9-1154A	
SCHEDULE DATE		INSPECTOR NO 83					
INSPECTOR NAME		INSPECTION REQUESTED gas test for heater					
☐ PARTIAL INSPECTION		☐ PARTIAL APPROVAL (P)		PARTIAL DESCRIPTION			
☒ APPROVED (A)		☐ STOP WORK (S)		☐ COMMENTS (C)		☐ TEMPORARY APPROVAL (T) — UNTIL	
☐ HOLD (H)							
☐ REJECTED (R)		REINSPECTION REQUIRED CALL *799 2071					
☐ REFEE (F)		REINSPECTION FEE REQUIRED PAY AT CITY HALL 3RD FLOOR 100 E STEWART STREET					
☐ PERMIT REQUIRED							
INSPECTOR SIGNATURE <i>JW Long</i>				INSPECTION DATE 6-20-1			
☐ PROJECT COMPLETE		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)					
IF YOU HAVE ANY QUESTIONS ON THIS INSPECTION YOU MAY CALL THE INSPECTOR FROM 7 00 A M 7 15 A M OR 2 45 P M 3 00 P M AT							

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELI WAY			PERMIT NO -
LOT NO	MAP NO 873-7665	INSPECTOR	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 29 MAY 91

GFI ok

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☒ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 Elmway			PERMIT NO.	
LOT NO 47	MAP NO.	INSPECTOR 65	DATE	
SUBDIVISION NAME Ridgeview			PHONE	
INSPECTOR SIGNATURE Lowman			INSPECTION DATE 1-27-91	

← REMOVE ANY ROCKS/CONCRETE FROM DITCHES, IF LARGER THAN PLASTIC PIPES!

(46C)

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**
☐ **PERMIT REQUIRED**
☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☒ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☒ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☒ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 Ella Way			PERMIT NO	
LOT NO 47	MAP NO	INSPECTOR 65	DATE 1/23/91	
SUBDIVISION NAME Kessler, Ridgeview			PHONE	
INSPECTOR SIGNATURE J. Brunner			INSPECTION DATE 1-24-91	

- WASTE FOOTINGS, NOT INSPECTED
- BLOW TRASH OFF, POOR AREAS
- KEEP ALL LADDER & CHAIRS UP TO KICK HEIGHT, ESP. IN TRANSITION AREAS
- KEEP POP OUT REBAR AWAY FROM CONTACT W/ DIRT
- FIRST PUST FIES NOT POURED ~~now~~ NOW!

(466)

☐ PARTIAL INSPECTION DESCRIPTION					
☐ APPROVED		☐ PERMIT REQUIRED		☐ STOP WORK	
☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071					
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☒ B 3	<u>PRE SLAB</u>	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY INSPECTION & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)			

FOR ASSISTANCE CALL 386-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELLA WAY			PERMIT NO 96494
LOT NO 47/1	MAP NO	INSPECTOR 65	DATE 2/12/91
SUBDIVISION NAME PLASTER - Ridgeview			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 2/12/91

OK - SHEAR

NOT REQD. - HOLD PWS

OK - ANC, BOLTS

NEED DRWS! - BOUND. NAILS

- NEED to SEE TRUSS CALC'S ?

- explain BOUNDARY NAILING ?

- USING A-35'S FOR 3RD CAR GAR.

OSB SHEAR TO GABLE TRUSS, NAIL EVERY HOLE!

- NAIL HORIZ JOINT GAR/HSE OSB, SHEAR, 4" O.C.

- PUT NUTS, WSHRS, ON FRT POST ANC. BOLTS

☐ PARTIAL INSPECTION DESCRIPTION

SUPPORT FLR TRUSS END 46

☒ **APPROVED - MOVE FRT POSTS OVER EXTERIOR WALLS, OUTSIDE**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOUND LAYOUT / REAR ZONING	☐ P-1	ON SITE SEWER	☐ X-1	UNDERGROUND HYDRO
☐ B-2	STEM WALL / FIRM & REBAR	☐ P-2	ON SITE WATER	☐ X-2	UNDERGROUND FINAL FLOW
☐ B-3	PRE SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☒ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	☒ PRE GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	☒ PRE PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION	BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)
--	---

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELLA			PERMIT NO 959 96494
LOT NO 4771	MAP NO	INSPECTOR 65	DATE 2/22/91
SUBDIVISION NAME Plaster-Ridgeway			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 2/22/91

- CHECK IF ADPL PLUG KEPT,
- AT FRG. ENT. ? OVER 6' FROM FRG. ENT.
- CHECK DRYS IN FRG UPPER TUB
- + SHOWER ?
- REPLACE FLEX LINE TO LOWER
- EXT FAN, UTIL RM

(46 plr)

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☒ P 5	<u>TOP OUT WATER/GAS WASTE</u>	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☒ M 1	<u>ROUGH VENT</u>	☒ E 2	<u>ROUGH ELECTRICAL</u>
☐ B 10	<u>POOL</u> PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	<u>POOL</u> PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELLA			PERMIT NO 96494
LOT NO 471	MAP NO	INSPECTOR 65	DATE 2/25/91
SUBDIVISION NAME PLASTER - RODGENSEN			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 2/25/91

- RE-ATTACH FLEX DUCT TO LOWER BATH EXH. FAN
- BLOCK OVER W/ 2"X's, ANY JOINTS IN BOT. PLATE, OUTSIDE WALLS, IF NOT UNDER STUDS
- REPAIR, OR REPLACE BAD 2"X6" WALL STUD, TOP OF STAIRS
- COVER F/P FWE ABOVE REAR ROOF TRUSSES
- SET UPPER FRT. TUB
- NSED ADDL. WALL STUD, UNDER UPPER FRT DBL GIRDER - ROOF (46 pl.)

☐ PARTIAL INSPECTION DESCRIPTION

☒ **FINISH F/WL BETWEEN STAIR STRINGERS**

☒ **APPROVED** ☐ PERMIT REQUIRED ☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☒ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

[illegible]

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELIA			PERMIT NO 96494		
LOT NO 47/1		MAP NO		INSPECTOR 65	
SUBDIVISION NAME Plaster-Ridgeview				DATE 2/27/91	
INSPECTOR SIGNATURE 				INSPECTION DATE 2/27/91	

— REPAIR OR REPLACE DAMAGED 2"X6" WALK STUD, BATH, AT TOP OF STAIRS

— FILL UPPER FRT TUB, W/ WTR FOR LEAK TEST

— NEED ADDN. WALK STUDS UNDER UPPER DBL ROOF GIRDERS!

— F/BLK UNDER FRT UPPER TUB

— STOP USING LESS THAN 12" WIDE OSB FOR SHEAR OR SHEATH!

— PUT NAIL PLATE OVER FRESH LINE, UPPER, MID-WALK

— USE FACTORY SUPPORT, UPPER H.W.

☐ PARTIAL INSPECTION DESCRIPTION
FLUE JOINT, NO TIE WIRES! (46 plan)

☐ APPROVED		☐ PERMIT REQUIRED		☐ STOP WORK	
-----------------------------------	--	--	--	------------------------------------	--

☒ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B 1	FOOTING / UNDER SLAB / FORMS & REBAR	☐ P 1	ON SITE WATER	☐ X 2	UNDER GROUND FINAL / FLOW
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	BUILDING SEWER (YARD LINES)	☐ X 3	SPRINKLER SYSTEM HYDRO
☐ B 3	PRE SLAB	☐ P 3	UNDERSLAB PLUMBING	☐ X 4	FIRE ALARM
☐ B 4	ROOF SHEATHING	☐ P 4	TOP OUT WATER GAS WASTE	☐ X 5	OTHER
☒ B 5	FRAMING	☐ P 5	FINAL GAS TEST	☐ X 6	FINAL FIRE
☐ B 6	DRYWALL NAILING	☐ P 6	FINAL PLUMBING		
☐ B 7	EXTERIOR LATH / STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 8	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 9	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 10	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 11	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 12	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C OF O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELLA WAY			PERMIT NO 96494
LOT NO 47	MAP NO	INSPECTOR 65	DATE
SUBDIVISION NAME RIDGEVIEW, PLASTER			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i>			INSPECTION DATE 2-28-91

- FILL UPPER FRT TUB W/ WTR, FOR LEAK TEST!

- USE FACTORY TYPE CLAMP SUPPORT ON H.W. FLUE, UPPER FRT.

"SUPER" WILL CHECK ABOVE (2) ITEMS, BEFORE DRY WALL TO BE HUNG IN AREAS NOTED!

☐ PARTIAL INSPECTION DESCRIPTION					
☒ APPROVED		☐ PERMIT REQUIRED		☐ STOP WORK	
☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071					
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL -- FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☒ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)			

FOR ASSISTANCE CALL 388 6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELIA			PERMIT NO. 789 96494
LOT NO. 47/1	MAP NO.	INSPECTOR G5	DATE 3/4/91
SUBDIVISION NAME Plaster - Ridgeview			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 3/4/91

FINISH SHEAR NAILING, STAIR
INTERIOR, HORIZ EDGE, 4" O.C.

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☒ B 7	<u>DRYWALL NAILING</u>	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELLA		PERMIT NO 96494	
LOT NO 47/1	MAP NO	INSPECTOR 65	DATE 3/13/91
SUBDIVISION NAME Plaster - Ridgeview			PHONE
INSPECTOR SIGNATURE Yanbu			INSPECTION DATE 3/13/91

— FOR TEMP TESTS, ONLY!

— INSUL ENDS OF ALL WIRING

— ISSUED E-TAG # 30197

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED** ☐ PERMIT REQUIRED ☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☒ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELIA		PERMIT NO. 96494	
LOT NO 47/1	MAP NO.	INSPECTOR 65	DATE 3/14/91
SUBDIVISION NAME P L A S T E R - R I D G E V I E W			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 3/14/91

- ISSUED & TAG #17505

☐ PARTIAL INSPECTION DESCRIPTION

☒ APPROVED ☐ PERMIT REQUIRED ☐ STOP WORK **(46 plan)**

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071


INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☒ F 6	FINAL GAS TEST #16	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELLA			PERMIT NO 96494
LOT NO 47/1	MAP NO	INSPECTOR 65	DATE 3/22/91
SUBDIVISION NAME Plaster-Ridgeview			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 3/22/91

— SEAL GAR. LID, AT D.O., LOW
VOLT WIRING (2)
— ADD STRAP (1) A/C WIRING FLEX
— SEAL GAR LID, H.W. FIVE
— " " GAS LINE
— " " S.W. PIPES
— MISSING (1) FRT ENT. CEILING LIGHT
— " (1) LV RM " "
— " (2) STAIRS, WALL "
— " PLANK COVER, UNDERSTAIRS CLOSET
— " KIT SINK, CLEAN-OUT!

☐ PARTIAL INSPECTION DESCRIPTION

(46 plan)

☒ **APPROVED** ☐ **PERMIT REQUIRED** ☐ **STOP WORK**

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071					
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☒ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☒ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION** BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7501 ELLA		PERMIT NO 96494	
LOT NO 47/1	MAP NO	INSPECTOR 65	DATE 4/15/91
SUBDIVISION NAME Plaster-Dodgeview			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i>			INSPECTION DATE 4/15/91
E - 97443			
P - 97082			
A/C - 97473			
OTHER PERMITS:			
- FIX SIDEWALK, DAMAGED!			
- SEAL AROUND H.W. FLUE, AT GARAGE			
☐ PARTIAL INSPECTION DESCRIPTION			
☒ APPROVED ☐ PERMIT REQUIRED ☐ STOP WORK			
☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING
☐ B 8	EXTERIOR LATH/STUCCO		
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT
☐ B 10	FOOT PRE GUNITE	☐ M 2	HOOD
☐ B 11	FOOT PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL
☐ B 12	BUILDING FINAL		
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH
		☐ X 2	UNDERGROUND HYDRO
		☐ X 3	UNDERGROUND FINAL/FLOW
		☐ X 4	SPRINKLER SYSTEM HYDRO
		☐ X 5	FIRE ALARM
		☐ X 6	OTHER
		☐ X 7	FINAL FIRE
		☐ E 1	UNDERGROUND ELECTRICAL
		☐ E 2	ROUGH ELECTRICAL
		☐ E 3	LOW VOLTAGE ELECTRICAL
		☐ E 4	SIGN INSPECTION
		☐ E 5	FINAL ELECTRICAL
		☐ E 6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C OF O ISSUANCE (Commercial Only)	

FOR ASSISTANCE CALL 386-8251
