

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 88956	
LOT NO.	MAP NO. 5-957a	INSPECTOR 59	DATE 11-6-90
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i>			INSPECTION DATE 11/7/90

Ref

Plumbing not complete

band all mtl within 5' of

pool edges

☐ PARTIAL INSPECTION - DESCRIPTION:

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☒ P-5	TOP OUT-WATER/GAS WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☒ E-2	ROUGH ELECTRICAL
☒ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 85956	
LOT NO.	MAP NO. 5-500	INSPECTOR 59	DATE 11-7-90
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE B. J. [Signature] 11/8/90			INSPECTION DATE

first inspection & rough gas

tighten lugs @ window banding

APV subject to above

☐ PARTIAL INSPECTION - DESCRIPTION.

☒ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS <i>9720 Terrace Green</i>			PERMIT NO. <i>85956</i>
LOT NO	MAP NO	INSPECTOR <i>59</i>	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE <i>B. J. [Signature]</i>			INSPECTION DATE <i>2/20/11</i>

bonding lugs ~~are~~ have been tightened

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☒ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER:
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☒ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 368-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green Ave.		PERMIT NO. 85956	
LOT NO	MAP NO 1 1:03P	INSPECTOR 59	DATE 2-20-91
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i> 2/21/91			INSPECTION DATE
<i>alarm</i> <i>Ref gate locked - unable to get in back yard to inspect.</i>			
☐ PARTIAL INSPECTION - DESCRIPTION:			
☐ APPROVED		☐ PERMIT REQUIRED	
☐ STOP WORK		☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 793-2071	

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRY WALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☒ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 85956	
LOT NO.	MAP NO. 2-350P	INSPECTOR 59	DATE 2-21-91
SUBDIVISION NAME Lakes			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i> 2/25/1			INSPECTION DATE
<i>recall gate unlocked please try latch</i> <i>Pool Lites - OK</i> <i>Note: you can't have elec recept closer than 10 ft to pool edge - please blank off @ house - pads for equipment must be 3" above finish grade</i> <i>OK to plaster but must comply with above + Recall insp</i>			
☒ PARTIAL INSPECTION - DESCRIPTION: <i>will leave gas tag @ BII Approval</i>			
☐ APPROVED		☐ PERMIT REQUIRED	
☐ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071		☐ STOP WORK	

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2 ^a	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5 ^a	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☒ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 85956
LOT NO	MAP NO 2 8:38A	INSPECTOR 59
SUBDIVISION NAME Lakes		DATE 3-13-91
INSPECTOR SIGNATURE 		PHONE 3651682
		INSPECTION DATE

Call 1/2 hr. prior for instructions
Final on pool

Note: make certain pads for equip is
about 3" above finish grade

left jobsite @
10:57 a.m.

GT# 17011

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☒ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☒ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	<u>POOL</u> PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☒ B-11	<u>POOL</u> PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☒ E-5	FINAL ELECTRICAL
☐ B-13	CERT. OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☒ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 85956	
LOT NO	MAP NO 2 8:38A	INSPECTOR 59	DATE 3-13-91
SUBDIVISION NAME Lakes			PHONE 3651682
INSPECTOR SIGNATURE 			INSPECTION DATE 3/14/91

Call 1/2 hr. prior for instructions
Final on pool

Note: make certain pads for equip is
about 3" above finish grade
lift jobsite @
10:57 a.m.

GTF# 17011

☐ PARTIAL INSPECTION - DESCRIPTION:

☐ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 793-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER:
☐ B-6	INSULATION	☒ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☒ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	<u>POOL</u> PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☒ B-11	<u>POOL</u> PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	<u>SIGN</u> INSPECTION
☐ B-12	BUILDING FINAL			☒ E-5	FINAL ELECTRICAL
☐ B-13	CERT. OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☒ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 306-3251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO 89827	
LOT NO	MAP NO 11-1121A	INSPECTOR 59	DATE 11-27-90
SUBDIVISION NAME Waterford			PHONE
INSPECTOR SIGNATURE <i>B. G. [Signature]</i>			INSPECTION DATE 11/28/90

Retaining Wall

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC.	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 88956	
LOT NO.	MAP NO. 5-957d	INSPECTOR 59	DATE 11-6-90
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 11/7/0

Reg

Plumbing not complete
band all mtl within 5' of
pool edge

☐ PARTIAL INSPECTION - DESCRIPTION:

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071


INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☒ P-5	TOP OUT-WATER (GAS) WASTE	☐ X-6	OTHER.
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRY WALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☒ E-2	ROUGH ELECTRICAL
☒ B-10	<u>POOL</u> PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	<u>POOL</u> PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT. OF OCC	☐ X-1	KICKER / FLUSH*	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 393-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 89827	
LOT NO	MAP NO	INSPECTOR 59	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 	11/30/0		INSPECTION DATE
Retaining wall			
☐ PARTIAL INSPECTION - DESCRIPTION:			
☒ APPROVED		☐ PERMIT REQUIRED	☐ STOP WORK
☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING
☐ B-8	EXTERIOR LATH/STUCCO		
☒ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT
☐ B-10	<u>POOL</u> PRE-GUNITE	☐ M-2	HOOD
☐ B-11	<u>POOL</u> PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL
☒ B-12	BUILDING FINAL		
☐ B-13	CERT OF OCC.	☐ X-1	KICKER / FLUSH
☒ FINAL INSPECTION		☐ X-2	UNDERGROUND HYDRO
		☐ X-3	UNDERGROUND FINAL/FLOW
		☐ X-4	SPRINKLER SYSTEM HYDRO
		☐ X-5	FIRE ALARM
		☐ X-6	OTHER
		☐ X-7	FINAL FIRE
		☐ E-1	UNDERGROUND ELETTRICAL
		☐ E-2	ROUGH ELECTRICAL
		☐ E-3	LOW VOLTAGE ELECTRICAL
		☐ E-4	SIGN INSPECTION
		☐ E-5	FINAL ELECTRICAL
		☐ E-6	TEMP POWER
BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O. ISSUANCE (Commercial Only)			

FOR ASSISTANCE -CALL: 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO. 88956	
LOT NO.	MAP NO. 6-500	INSPECTOR 59	DATE 11-7-90
SUBDIVISION NAME			PHONE

INSPECTOR SIGNATURE > B. [Signature]	INSPECTION DATE 11/8/90
---	-----------------------------------

"first inspection & rough gas"

Tighten lugs @ window banding

Apv Subject to above

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER.
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVAL

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

ADDRESS 9720 Terrace Green			PERMIT NO. 85956
LOT NO	MAP NO	INSPECTOR 59	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 2/20/11

bonding lugs ~~are~~ have been Tightened

☐ PARTIAL INSPECTION - DESCRIPTION.

☒ **APPROVED**

 ☐ **PERMIT REQUIRED**

 ☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☒ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 393-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green Ave.			PERMIT NO. 85956		
LOT NO	MAP NO 1 1:03P	INSPECTOR 59	DATE 2-20-91		
SUBDIVISION NAME			PHONE		
INSPECTOR SIGNATURE B. J. Waters			INSPECTION DATE 2/21/91		
<i>address</i> <i>Ref gate locked - unable to get in back yard to inspect</i>					
☐ PARTIAL INSPECTION - DESCRIPTION					
☒ APPROVED		☐ PERMIT REQUIRED		☐ STOP WORK	
☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071					
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☒ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O. ISSUANCE (Commercial Only)			

FOR ASSISTANCE -CALL: 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9720 Terrace Green		PERMIT NO 85956	
LOT NO.	MAP NO 2 - 350 P	INSPECTOR 59	DATE 2-21-91
SUBDIVISION NAME Lakes			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE
<i>recall gate unlatched please try latch</i>			
<i>Pool lites - OK</i>			
<i>Note: you can't have elec recept closer than 10 ft to pool edge - please blank off @ house - pads for equipment must be 3" above finish grade - OK to plaster but must comply with above + Recall insp</i>			
☒ PARTIAL INSPECTION - DESCRIPTION: <i>will leave gas tag @ BII Approval</i>			
☐ APPROVED		☐ PERMIT REQUIRED	
☐ REJECTED - CORRECTION		☐ STOP WORK	
NOTICE - REINSPECTION REQUIRED CALL 799-2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING
☐ B-8	EXTERIOR LATH/STUCCO		☐ E-1 UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL
☐ B-12	BUILDING FINAL		☐ E-3 LOW VOLTAGE ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH
		☐ E-4	SIGN INSPECTION
		☐ E-5	FINAL ELECTRICAL
		☐ E-6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C. of O ISSUANCE (Commercial Only)	

CITY OF LAS VEGAS, NEVADA

PERMIT NO. 90-005956

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR INSPECTIONS, CALL 799-2071

DEVELOPMENT PERMIT
FOR: Swimming Pool or Spa

66

440-542-037

LOG NO. & AREA _____ DATE _____ CONST. VAL. \$ 5620⁰⁰

ADDRESS OF CONSTRUCTION 9720 TERRACE GREEN OWNER JOE LA FOUR PHONE 363 1342

CONTRACTOR MISSION POOLS STATE LICENSE NO. WEST 3 LEV CITY LICENSE NO. R-PD6

LOT(S) _____ BLOCK _____ SUBDIVISION _____ ZONE _____

PLUMBING CONTRACTOR Mission Pools ELECTRICAL CONTRACTOR R.W. ELECTRONICS MIHOT

CIRCLE TYPE OF POOL THAT APPLIES: PRIVATE SEMI-PUBLIC PUBLIC SPA #33284

MATERIALS OF CONSTRUCTION. REINFORCED GUNITE REINFORCED CONCRETE OTHER _____

SQUARE FEET OF SURFACE POOL 4304 SPA 324 VOLUME IN GALLONS 13,000

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way.

I state that I am familiar with the effective ordinances of the City of Las Vegas, Nevada and the effective Statutes of the State of Nevada covering construction and use of the above type; I agree to perform said construction in conformity therewith. I further agree that issuance of a permit on the above application will not excuse me from conforming with the said Ordinances and Statutes despite any errors on the part of the building inspector or engineer in checking plans and application herewith.

All swimming pools must be fenced before the pool is filled with water. No electrical lines shall cross over a pool. Applicants must have separate plot plans showing location of power pole, proposed or existing fencing and location of swimming pool. I agree to repair any utility line, if damaged during excavation work. I have read and understand the contents of above application. I hereby state that the same are true and correct.

SIGNED Mission Pools CONTRACTOR
CPF J.E. L... AGENT/OWNER

PLANNING DEPT TB DATE 10-17-90

BUILDING DEPT DATE

1. Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
2. Re-Inspection fee during normal business hours assessed under provisions of TABLE 3-A of the Uniform Building Code = \$30.00 each
3. Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour).
4. Additional plan review required by changes, additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours)

DESCRIPTION			FEE	TOTAL
ISSUANCE FEE			10.00	10
SEWER CONNECTION FEE (to 30,000 GALLONS)			60.00	63
BUILDING PERMIT - POOL & OR SPA				68
PLUMBING PERMIT	PRIVATE POOL OR SPA	PREFORMED SPA	10.00	
		OTHERWISE	20.00	20
	PUBLIC OR SEMI-PUBLIC POOL OR SPA	PREFORMED SPA	20.00	
		OTHERWISE	30.00	10/17/90
	FUEL PIPING FOR POOL HEATER		6.00	40 y
ELECTRICAL PERMIT	SPA		8.00	
	SWIMMING POOL	RESIDENTIAL	20.00	20
		PUBLIC-SEMI-PUBLIC	30.00	
	ELECTRICAL SERVICE CHANGE		6.00	
MISC.				
TOTAL FEES				

RECEIPT

##0002##
 POOL 78.00
 SEWR 63.00
 PLRG 26.00
 ELEC 20.00
 CHEK 187.00
 3379A000 10:44

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

PERMIT NO.

90-00027

DEVELOPMENT PERMIT

FOR: Fence, Wall, Retaining Wall

LOG NO. & AREA M-6042FOR INFO
440DATE 11-20-90CONST. VAL. \$ 1012ADDRESS OF CONSTRUCTION 9720 TERRACE GREENOWNER Peggy Ann LaTourPHONE 363-1342CONTRACTOR OWNER

STATE LICENSE NO. _____

CITY LICENSE NO. _____

LOT(S) 358 BLOCK G SUBDIVISION LAKE WEST #3 LEWIS HOMES ZONE R-PDC6☐ CONSTRUCTION PLANS SUBMITTED BY OWNER/CONTRACTOR☒ CONSTRUCTION DESIGN BY CITY DESIGN SHEET.

ENGINEER _____

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

DESCRIPTION	TOTAL LIN FT	TOTAL SQ. FT.
CHAIN LINK OR WIRE MESH		
ORNAMENTAL IRON		
WOOD		
☒ MASONRY	<u>4</u>	<u>24</u>
☒ RETAINING	<u>268</u>	<u>272</u>

OTHER INSPECTIONS AND FEES


- 1 Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
- 2 Re-inspection fee during normal business hours assessed under provisions of TABLE 3-A of the Uniform Building Code = \$30.00 each
- 3 Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour)
- 4 Additional plan review required by changes, additions or revisions at approved plans = \$30.00 per hour (minimum charge two hours)

ID/OK

CONDITIONS OF THE PERMIT:

1. Any type of retaining wall must be engineered by a Civil or Structural Engineer.
2. If a home owner takes out the Building Permit and if the owner sublets the work to a Contractor, then the Contractor must take out the permit and pay for it.
3. No fence or wall can be built on City property or rights-of-way, but this is not intended to preclude construction within utility easements if utilities will not be damaged or made inaccessible.
4. The fence or wall shall not enclose any water meter, light standard, or fire alarm box and shall not come closer than 24" from the nearest fire hydrant outlet
5. Department Inspectors must approve footings before concrete is poured and block wall reinforcing before grouting is done.
6. Maximum height of any wall or fence is 6', side and rear yards; 4' maximum in front yard with the vertical surface above the height of 2' - 50% open.
7. I must not obstruct required onsite parking space (2 spaces for each dwelling unit) by the erection of this fence or wall.
8. By the signing of this application I herewith agree to the requirements outlined above

FOR INSPECTIONS, CALL 799-2071

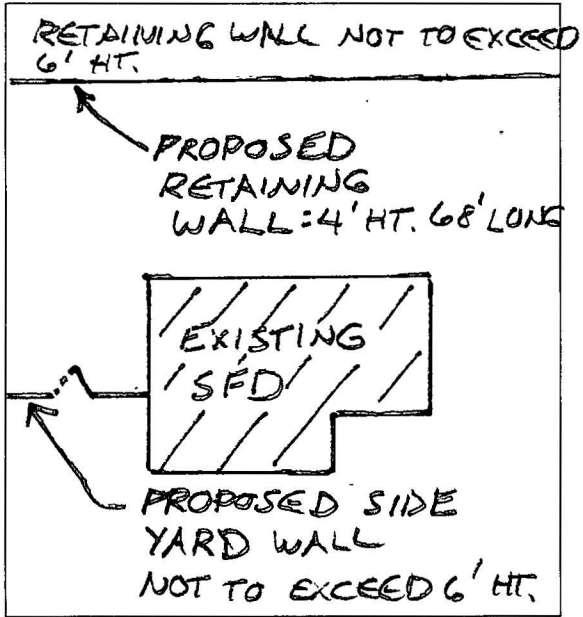

FRONT.

SIGNED Peggy Ann LaTour CONTRACTOR - AGENT - OWNER
[Signature] PLANNING DEPT. DATE 11/20/90

I hereby certify that I have reviewed this application and the proposed plans and have found that the proposed development meets the requirements of the City of Las Vegas Flood Hazard Reduction Ordinance for the issuance of this Development Permit.

RB 11/20/90
 LAND DEVELOPMENT AND FLOOD CONTROL ENGINEER DATE
RB 11-20-90
 BUILDING DEPT. DATE

PLAN REVIEW FEE _____

PERMIT FEE 23.00
2310-2401TOTAL FEES 23.00

RECEIPT

9001027
 WALL 23.00
 CHG 23.00
 TOTAL 46.00

11/20/90

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

CITY OF LAS VEGAS, NEVADA

PERMIT NO. 90-085956

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR

DEVELOPMENT PERMIT
FOR: Swimming Pool or Spa

LOG NO. & AREA

DATE

CONST. VAL. \$

562000

ADDRESS OF
CONSTRUCTION

9720 TERRACE GREEN

OWNER

JOE LA TOUR

PHONE

363 1342

CONTRACTOR

MISSION POOLS

STATE
LICENSE NO.CITY
LICENSE NO.

LOT(S)

BLOCK

G

SUBDIVISION

LAKES WEST 3 LAKES HOMES R-PD6

PLUMBING
CONTRACTOR

Mission Pools

ELECTRICAL
CONTRACTORR.W. ELECTRONICS MI467
Randy L. L. L.

CIRCLE TYPE OF POOL THAT APPLIES:

PRIVATE

SEMI-PUBLIC

PUBLIC

SPA

#33284

MATERIALS OF CONSTRUCTION:

REINFORCED GUNITE

REINFORCED CONCRETE

OTHER

SQUARE FEET OF SURFACE POOL

4307

SPA

327

VOLUME IN GALLONS

13,000

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way.

I state that I am familiar with the effective ordinances of the City of Las Vegas, Nevada and the effective Statutes of the State of Nevada covering construction and use of the above type; I agree to perform said construction in conformity therewith. I further agree that issuance of a permit on the above application will not excuse me from conforming with the said Ordinances and Statutes despite any errors on the part of the building inspector or engineer in checking plans and application herewith.

All swimming pools must be fenced before the pool is filled with water. No electrical lines shall cross over a pool. Applicants must have separate plot plans showing location of power pole, proposed or existing fencing and location of swimming pool. I agree to repair any utility line, if damaged during excavation work. I have read and understand the contents of above application. I hereby state that the same are true and correct.

SIGNED

CONTRACTOR

BY

AGENT/OWNER

PLANNING DEPT.

DATE

BUILDING DEPT.

DATE

1. Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours).
2. Re-Inspection fee during normal business hours assessed under provisions of TABLE 3-A of the Uniform Building Code = \$30.00 each.
3. Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour).
4. Additional plan review required by changes, additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours).

DESCRIPTION			FEE	TOTAL
ISSUANCE FEE			10.00	10
SEWER CONNECTION FEE (to 30,000 GALLONS)			60.00	63
BUILDING PERMIT - POOL & OR SPA.				68
PLUMBING PERMIT	PRIVATE POOL OR SPA	PREFORMED SPA	10.00	
		OTHERWISE	20.00	20
	PUBLIC OR SEMI-PUBLIC POOL OR SPA	PREFORMED SPA	20.00	
		OTHERWISE	30.00	10/17/90
	FUEL PIPING FOR POOL HEATER		6.00	16 y
ELECTRICAL PERMIT	SPA		8.00	
	SWIMMING POOL	RESIDENTIAL	20.00	20
		PUBLIC-SEMI-PUBLIC	30.00	
	ELECTRICAL SERVICE CHANGE		6.00	
MISC.				
TOTAL FEES				

RECEIPT

0002

POOL 78.00
SEWR 63.00
PLIG 26.00
ELEC 20.00
CHK 187.00
3379A000 10:44

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK
