



DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista Wy		PERMIT NO. 036694	
LOT NO	MAP NO	INSPECTOR 58	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 8/24/89
B-1 Please re-call and set up appointment with Conc. Cont.			
☐ PARTIAL INSPECTION - DESCRIPTION:			
☐ APPROVED		☐ PERMIT REQUIRED	☐ STOP WORK
☐ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING
☐ B-8	EXTERIOR LATH/STUCCO		
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL
☐ B-12	BUILDING FINAL		
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH
		☐ X-2	UNDERGROUND HYDRO
		☐ X-3	UNDERGROUND FINAL/FLOW
		☐ X-4	SPRINKLER SYSTEM HYDRO
		☐ X-5	FIRE ALARM
		☐ X-6	OTHER
		☐ X-7	FINAL FIRE
		☐ E-1	UNDERGROUND ELETRICAL
		☐ E-2	ROUGH ELECTRICAL
		☐ E-3	LOW VOLTAGE ELECTRICAL
		☐ E-4	SIGN INSPECTION
		☐ E-5	FINAL ELECTRICAL
		☐ E-6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)	


FOR ASSISTANCE -CALL: 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista			PERMIT NO. 036694
LOT NO.	MAP NO.	INSPECTOR 58	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 8/28/89

B-1 OK

UFR - 20' $\approx$ 4 Rebar

$\updownarrow$ 2' max

 18' min $\rightarrow$

☐ PARTIAL INSPECTION - DESCRIPTION.

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 793-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 393-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 TERRA VISTA			PERMIT NO 36694
LOT NO	MAP NO	INSPECTOR	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE DREW TO			INSPECTION DATE 9-7-89

UFR

I TALKED WITH YOUR BLDG INSPECTOR #58 ABOUT YOUR UFR. IT HAS TO BE 20 FT IN EARTH, (ONE PIECE) YOUR REBAR IS 6 FT OUT OF SLAB.

YOU ARE REQUIRED TO POUR A CONCRETE CUBE 2X2X2 FT WITH 20 FT OF # 1/0 COPPER COILED AT BOTTOM. CALL BEFORE YOU POUR.

☐ PARTIAL INSPECTION - DESCRIPTION:

ATTN BOB WAGNER

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED **(CORRECTION NOTICE)** REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER:
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☒ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista		PERMIT NO 036694	
LOT NO	MAP NO	INSPECTOR 58	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 	MDM		INSPECTION DATE 9/7/89

B-2

B-3

NOT Ready

Wire mesh missing

#4 cant.

Also UFER NOT installed properly,

7'-4" ABOVE concrete see sheet (inspector)

8/28/89

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ APPROVED	☐ PERMIT REQUIRED	☐ STOP WORK
☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 789-2071		

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☒ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☒ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION	BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)
--	--

FOR ASSISTANCE -CALL: 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terna Vista Wy			PERMIT NO. 036694
LOT NO	MAP NO	INSPECTOR 58	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE MDM			INSPECTION DATE 9/8/89

B-2
B-3 OK

U FPR OK

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☒ B-2	STEM WALL — FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☒ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	<u>POOL</u> PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	<u>POOL</u> PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. OF O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista Wy			PERMIT NO. 036694
LOT NO	MAP NO	INSPECTOR 58	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE			INSPECTION DATE 9/29/85

B-4 Dry inn only

**Re Check for preimeter
nailing**

- 1. Letter on Waffer Board.**
- 2. " on Staples instead
nails walls & Roof**

☐ PARTIAL INSPECTION - DESCRIPTION

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☒ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista			PERMIT NO. 036694
LOT NO	MAP NO	INSPECTOR SS	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE	MDM		INSPECTION DATE 10/24/88

B-4
B-8 OK

☐ PARTIAL INSPECTION - DESCRIPTION:

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL — FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☒ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER:
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☒ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 TERRA VISTA			PERMIT NO 36694-1	
LOT NO 3204	MAP NO	INSPECTOR	DATE	
SUBDIVISION NAME			PHONE	
INSPECTOR SIGNATURE D. M. W.			INSPECTION DATE 11-1-89	

- ADD 4-WAY TO GARAGE EXIT DOOR
- DINE RM SMALL APPLIANCE CKT
#12 4 # MAX
- WASHER H.R.
- 200 SUB / 3/0 ALUM/WIRE WILL HAVE
125 AMP BRKR. HAVE LOAD CALCS
- #6 ALUM UP TO 50 AMP
- NOOK SMALL APPLIANCE CKT
- 60 OW HOME RUN

OK D. M. W.

CORRECT BY 11-20-89

☐ PARTIAL INSPECTION - DESCRIPTION.

☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☒ E-2	ROUGH ELECTRICAL
☐ B-10	<u>POOL</u> PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	<u>POOL</u> PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE - CALL: 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista		PERMIT NO. 36694	
LOT NO.	MAP NO.	INSPECTOR 53	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 		INSPECTION DATE 11-20-89	

SFD

Dry wall - OK

Shear Wall Nailing - OK

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ APPROVED
☐ PERMIT REQUIRED
☐ STOP WORK

☐ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☒ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista		PERMIT NO. 036694	
LOT NO.	MAP NO. 18-5-48a	INSPECTOR 85	DATE 2-14
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE DZ			INSPECTION DATE 2-16-90
am - plug/AC p-6 p-7 m-3			
6507613			
☐ PARTIAL INSPECTION - DESCRIPTION			
☐ APPROVED		☐ PERMIT REQUIRED	☐ STOP WORK
☐ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST
☐ B-7	DRYWALL NAILING	☒ P-7	FINAL PLUMBING
☐ B-8	EXTERIOR LATH/STUCCO		
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD
☐ B-11	POOL PRE-PLASTER / FINAL	☒ M-3	FINAL MECHANICAL
☐ B-12	BUILDING FINAL		
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH
		☐ X-2	UNDERGROUND HYDRO
		☐ X-3	UNDERGROUND FINAL/FLOW
		☐ X-4	SPRINKLER SYSTEM HYDRO
		☐ X-5	FIRE ALARM
		☐ X-6	OTHER
		☐ X-7	FINAL FIRE
		☐ E-1	UNDERGROUND ELETTRICAL
		☐ E-2	ROUGH ELECTRICAL
		☐ E-3	LOW VOLTAGE ELECTRICAL
		☐ E-4	SIGN INSPECTION
		☐ E-5	FINAL ELECTRICAL
		☐ E-6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O. ISSUANCE (Commercial Only)	

FOR ASSISTANCE -CALL- 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Serra Vista			PERMIT NO. 36694
LOT NO	MAP NO 3-121 P	INSPECTOR 70	DATE 2-16
SUBDIVISION NAME			PHONE

INSPECTOR SIGNATURE ▶ Dan R. Ward	INSPECTION DATE 2-20-90
---	---

SCREW-IN FLORESCENT BULBS
NOT ACCEPTABLE. MUST BE
TUBE TYPE. HOOK GROUND
WIRE IN CLOSET LIGHTS
TO GROUND WIRE IN BOX,
NOT CORRECT TO WRAP
AROUND SCREW

30-DAY TEMP POWER OK

☐ PARTIAL INSPECTION - DESCRIPTION:

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☒ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER


☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 363-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS: 1891 Terra Vista		PERMIT NO: 36094	
LOT NO: . . .	MAP NO: 13-4:54a	INSPECTOR: 76	DATE: 2-21
SUBDIVISION NAME:			PHONE:
INSPECTOR SIGNATURE: David R. Marsh			INSPECTION DATE: 2-22-90

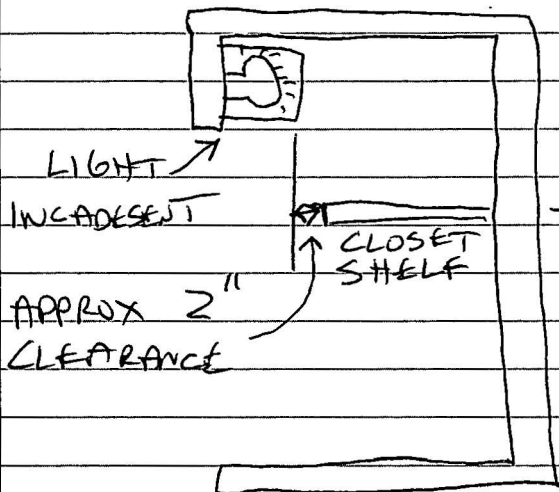

**YOU NEED
12" CLEARANCE
OR TUBE
TYPE
FLORESCENT
WITH COVER**

**CONTACT
BOB WAGNER
386-6657**

☐ PARTIAL INSPECTION - DESCRIPTION:

☐ APPROVED ☐ PERMIT REQUIRED ☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	☐ POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	☐ POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☒ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 393-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Serra Vista		PERMIT NO. 36694
LOT NO. 45-4258	MAP NO. 18-220p	INSPECTOR 68 55
SUBDIVISION NAME SFD		DATE 2-23
INSPECTOR SIGNATURE [Signature] J. Carson		PHONE 2-26-90
tag		
EL. meter		
TAG # 16327		

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ **APPROVED**

☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL — FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☒ X-6	OTHER <i>E, TAB</i>
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	<u>POOL</u> PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	<u>POOL</u> PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☐ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC.	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL- 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista		PERMIT NO. 36694	
LOT NO	MAP NO 18-220 P	INSPECTOR 75	DATE 2-23
SUBDIVISION NAME 45-42-56			PHONE
INSPECTOR SIGNATURE ▶ Dan R Ward			INSPECTION DATE 2-26-10

☐ PARTIAL INSPECTION - DESCRIPTION:

☒ **APPROVED**

 ☐ **PERMIT REQUIRED**

 ☐ **STOP WORK**

☐ **REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 793-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING		
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-1	UNDERGROUND ELETTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-2	ROUGH ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☐ E-4	SIGN INSPECTION
☐ B-12	BUILDING FINAL			☒ E-5	FINAL ELECTRICAL
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH	☐ E-6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C. of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL- 383-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista		PERMIT NO 036694	
LOT NO	MAP NO 17-5:02p	INSPECTOR 63	DATE 2-26
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 2/28/90
requested Thurs.			
☐ PARTIAL INSPECTION - DESCRIPTION:			
☒ APPROVED		☐ PERMIT REQUIRED	
☐ REJECTED - CORRECTION		☐ STOP WORK	
NOTICE - REINSPECTION REQUIRED CALL 793-2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER
☐ B-2	STEM WALL -- FORMS & REBAR	☐ P-2	ON SITE WATER
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING
☐ B-8	EXTERIOR LATH/STUCCO		
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL
☒ B-12	BUILDING FINAL		
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH
		☐ X-2	UNDERGROUND HYDRO
		☐ X-3	UNDERGROUND FINAL/FLOW
		☐ X-4	SPRINKLER SYSTEM HYDRO
		☒ X-5	FIRE ALARM
		☐ X-6	OTHER SINK OUT
		☐ X-7	FINAL FIRE
		☐ E-1	UNDERGROUND ELETRICAL
		☐ E-2	ROUGH ELECTRICAL
		☐ E-3	LOW VOLTAGE ELECTRICAL
		☐ E-4	SIGN INSPECTION
		☐ E-5	FINAL ELECTRICAL
		☐ E-6	TEMP POWER
☒ FINAL INSPECTION		BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C. of O ISSUANCE (Commercial Only)	

FOR ASSISTANCE -CALL- 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 1891 Terra Vista		PERMIT NO. 036694	
LOT NO.	MAP NO. 18-51489	INSPECTOR 70	DATE 2-14
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE David M. Lamb			INSPECTION DATE 2-16-90

PM -

PUT DEAD FRONT ON MAIN P.

NO-LOX ALL ACUM, INCLUDING GROUNDS

12" OR MORE OF KIT COUNTER GETS ~~✓~~

#4 CU BOND ON WATER SOFTNER

LABOR ALL PANELS

LIGHTS IN CLOSETS NEED 12" OF CLEARANCE, INSTALL FLUORESCENT FIXTURE WITH COVER

NOTICE WRITTEN ON 9-7-89, UTER NOT CORRECT, POUR 2X2X2 CURB, CALL

☐ PARTIAL INSPECTION - DESCRIPTION: for inspection

CALL BY 3-10-90

☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☒ REJECTED - CORRECTION NOTICE - REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B-1	FOOTING, LAYOUT, REBAR, ZONING	☐ P-1	ON SITE SEWER	☐ X-2	UNDERGROUND HYDRO
☐ B-2	STEM WALL - FORMS & REBAR	☐ P-2	ON SITE WATER	☐ X-3	UNDERGROUND FINAL/FLOW
☐ B-3	PRE-SLAB	☐ P-3	BUILDING SEWER (YARD LINES)	☐ X-4	SPRINKLER SYSTEM HYDRO
☐ B-4	ROOF SHEATHING	☐ P-4	UNDERSLAB PLUMBING	☐ X-5	FIRE ALARM
☐ B-5	FRAMING	☐ P-5	TOP OUT-WATER, GAS, WASTE	☐ X-6	OTHER
☐ B-6	INSULATION	☐ P-6	FINAL GAS TEST	☐ X-7	FINAL FIRE
☐ B-7	DRYWALL NAILING	☐ P-7	FINAL PLUMBING	☒ E-1	UNDERGROUND ELECTRICAL
☐ B-8	EXTERIOR LATH/STUCCO			☐ E-2	ROUGH ELECTRICAL
☐ B-9	WALL GROUT & STEEL	☐ M-1	ROUGH VENT	☐ E-3	LOW VOLTAGE ELECTRICAL
☐ B-10	POOL PRE-GUNITE	☐ M-2	HOOD	☐ E-4	SIGN INSPECTION
☐ B-11	POOL PRE-PLASTER / FINAL	☐ M-3	FINAL MECHANICAL	☒ E-5	FINAL ELECTRICAL
☐ B-12	BUILDING FINAL			☐ E-6	TEMP POWER
☐ B-13	CERT OF OCC	☐ X-1	KICKER / FLUSH		

☐ FINAL INSPECTION
 BRING HARD CARD WITH FIRE, QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O. ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL: 388-8251

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251FOR INSPECTIONS, CALL 799-2071
310 330 050

PERMIT NO. 89-036694

BUILDING PERMIT

FOR: Single Family Dwelling, Remodel,
Additions, Misc. Residential ConstructionLOG NO. & AREA 2153 DATE 7-14-89 CONST. VAL. \$ 113872.00ADDRESS OF CONSTRUCTION 1091 TERRA VISTA WAY OWNER Kyle Buhecker PHONE 363 0008LOT(s) 3 BLOCK PM 155-83 SUBDIVISION PM 155-83 ZONE R-EPROPOSED CONSTRUCTION SFD w/12 F.P.S USE THIS PERMIT FOR BLDG. ☐ A/C ☐ ELEC. ☐ PLBG ☐ OTHER PERMITS REQD: FENCE ☐ OFF SITE ☐ SWIM POOL ☐FLOOR AREA BSMT - 1ST 5883 2ND - GARAGE 902 PORCH 252 TOTAL 5037CONTRACTOR OWNER - Builder STATE LICENSE NO CITY LICENSE NO ARCHITECT PLACE - Arch ENGINEER MASTER PLUMBER/CONTRACTOR R. B. Plumbing MASTER ELECTRICIAN/CONTRACTOR

OTHER INSPECTIONS AND FEES

- 1 Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
- 2 Re-inspection fee during normal business hours assessed under provisions of TABLE 3-A of the Uniform Building Code = \$30.00 per hour
- 3 Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour)
- 4 Additional plan review required by changes, additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours)

CONDITIONS OF THE PERMIT:

1. I agree to call the City Building Department for inspections before concrete is poured, before rough wiring, electrical, plumbing, framing is covered. Also for air conditioning, drywall and sheathing inspection.
2. I agree that when the job is completed that I will call for final inspection before occupancy
3. I agree to perform all construction in accordance with City Ordinances and Building Codes
4. The Contractor's signature below denotes authority from the owner to sign in his behalf and that the owner is aware of all requirements of this application and permit. Separate permits must be taken out for work outlined above this agreement.
5. I have read and understand the contents of this application and permit, I hereby state that the information I have supplied on this application is true and correct.
6. Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way
7. 24 HOUR MINIMUM NOTICE REQUIRED FOR INSPECTIONS

BY [Signature] OWNERBY AGENT


I hereby certify that I have reviewed this application and the proposed plans and have found that the proposed development meets the requirements of the City of Las Vegas Flood Hazard Reduction Ordinance for the issuance of this Development Permit.

LAND DEVELOPMENT AND FLOOD CONTROL ENGINEER

PLANNING DEPT

BUILDING DEPT

SPECIAL CONDITIONS

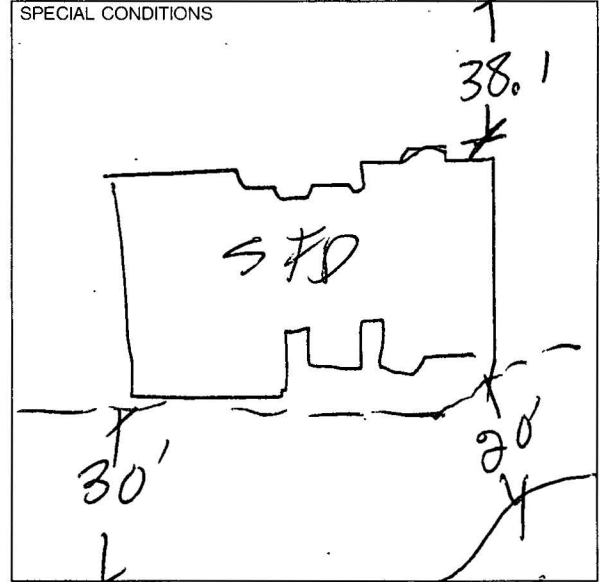

LAND DEVELOPMENT AND FLOOD CONTROL ENGINEER

PLANNING DEPT

BUILDING DEPT

PLUMBING		FEE	ELECTRICAL		FEE
WATER DISTRIBUTION	6.00	6.00	RECEPTACLE <u>88</u> SWITCH <u>45</u>	40	52.20
SEWER SYSTEM - NEW OR MODIFICATION	10.00	10.00	EACH LIGHT FIXTURE OR SOCKET <u>43</u>	30	12.90
FIXTURES - WATER SINK, TUB, HEATER	2.00	34.00	SPECIAL OUTLET, APPLIANCE ETC <u>48</u>	.70	58.99
GARBAGE DISPOSAL / WASHER	2.00	2.00	SERVICE/PANEL (SUB/300 - 200A/600 - 400A/1250)		13.50
FUEL PIPING	6.00		A.C. UNIT OR MOTORS <u>2</u>	3.00	6.00
IRRIGATION SYSTEM	8.00		2310 - 2402	TOTAL	87.60
MISC			MISC <u>Temp Pole</u>		6.00
2310 - 2403					
TOTAL		48.00			
AIR CONDITIONING		FEE	2310 - 2401 ISSUANCE FEE		
NEW UNIT - 3 TON = 9.00	16.50	33.00	7114 - 365 SEPT CONNECTION		58590-360
FURNACE TO 100,000/9.00 OVER/11.00			2310 - 2401 PLAN REVIEW FEE		562.00
VAPORATIVE COOLER	6.50		2310 - 2401 BLDG PERMIT FEE		740.00
VENTILATION FAN <u>4</u>	2.35	9.40	TOTAL FEES		740.00
2310 - 2405					
TOTAL		42.40			

RECEIPT

440002##
 PLBG 48.00
 ELEC 87.60
 A/C 42.40
 SFD 562.00
 CHEK 740.00
 0930A000 13:32

PERMIT NO.
MUST BE MACHINE VALIDATED

Permit Expires 180 Days After Abandonment of Work
