

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-088942

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

FOR INSPECTIONS CALL 799 2071

BUILDING PERMIT
FOR Single Family Dwelling Remodel
Additions Misc Residential Construction

LOG NO & AREA T-205 DATE OCT 8, 90 CONST VAL \$ 54,300

ADDRESS OF CONSTRUCTION 9428 Sierra Summit Ave OWNER Watt Nevada PHONE 369-2401

LOT(s) 109 BLOCK D SUBDIVISION LAS COLINAS Summerlin VIL #1 North ZONE P-C

PROPOSED CONSTRUCTION SFD with fireplace USE _____

THIS PERMIT FOR BLDG ☒ A/C ☐ ELEC ☐ PLBG ☐ OTHER PERMITS REQD FENCE ☐ OFF SITE ☐ SWIM POOL ☐

FLOOR AREA BSMT n/a 1ST 1054 2ND 820 GARAGE 380 PORCH 90 TOTAL 2344

CONTRACTOR Watt Nevada STATE LICENSE NO 0030439 CITY LICENSE NO C11-03409-

ARCHITECT Arlo Braun AIA ENGINEER J. C. Wallace Z-042316

MASTER PLUMBER/CONTRACTOR _____ MASTER ELECTRICIAN/CONTRACTOR _____

OTHER INSPECTIONS AND FEES

- Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
- Re inspection fee during normal business hours assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30.00 per hour
- Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour)
- Additional plan review required by changes additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours)

CONDITIONS OF THE PERMIT

- I agree to call the City Building Department for inspections before concrete is poured before rough wiring electrical plumbing framing is covered Also for air conditioning drywall and sheathing inspection
- I agree that when the job is completed that I will call for final inspection before occupancy
- I agree to perform all construction in accordance with City Ordinances and Building Codes
- The Contractor's signature below denotes authority from the owner to sign in his behalf and that the owner is aware of all requirements of this application and permit Separate permits must be taken out for work outlined above this agreement
- I have read and understand the contents of this application and permit I hereby state that the information I have supplied on this application is true and correct
- Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way
- 24 HOUR MINIMUM NOTICE REQUIRED FOR INSPECTIONS

BY Alan Swase 10-15-90 OWNER

BY _____ AGENT

I hereby certify that I have reviewed this application and the proposed plans and have found that the proposed development meets the requirements of the City of Las Vegas Flood Hazard Reduction Ordinance for the issuance of this Development Permit

LAND DEVELOPMENT AND FLOOD CONTROL ENGINEER Kent Nash 10-12-90 DATE

PLANNING DEPT C. R. 11/9/90 DATE

BUILDING DEPT Clone Hoesly 10/9/90 DATE

SPECIAL CONDITIONS

Model #11-2

PLUMBING		FEE	ELECTRICAL		FEE
WATER DISTRIBUTION	6 00		RECEPTACLE _____ SWITCH _____		40
SEWER SYSTEM NEW OR MODIFICATION	10 00		EACH LIGHT FIXTURE OR SOCKET _____		30
FIXTURES WATER SOFTENER H/W HEATER	2 00		SPECIAL OUTLET APPLIANCE ETC		70
GARBAGE DISPOSAL WASHER	2 00		SERVICE/PANEL SUB/3 00 200A/6 00 400A/12 50		
FUEL PIPING	6 00		A/C UNIT OR MOTORS	3 00	
IRRIGATION SYSTEM	8 00		2310 2432 TOTAL		
MISC			MISC		
2310 2433 TOTAL			2310 2431 ISSUANCE FEE		
AIR CONDITIONING		FEE	7143 2973 SEWER CONNECTION		
NEW UNIT 3 TON = 9 00 OVER = 16 50			2310 2431 PLAN REVIEW FEE		
FURNACE TO 100 000/9 00 OVER/11 00			2310 2431 BLDG PERMIT FEE		
VAPORATIVE COOLER	6 50		TOTAL FEES		
VENTILATION FAN	2 35				
2310 2435 TOTAL					

RECEIPT

0005

SEWR 12500 00

SFD 7253 00

CHEK 19753 00

4715A000 13 32

PERMIT NO _____


MUST BE MACHINE VALIDATED

Permit Expires 180 Days After Abandonment of Work

LAS COLINAS
FILE _____, PG _____

LOT 109, BLK "D"

ADDRESS 9428 Sierra Summit Avenue

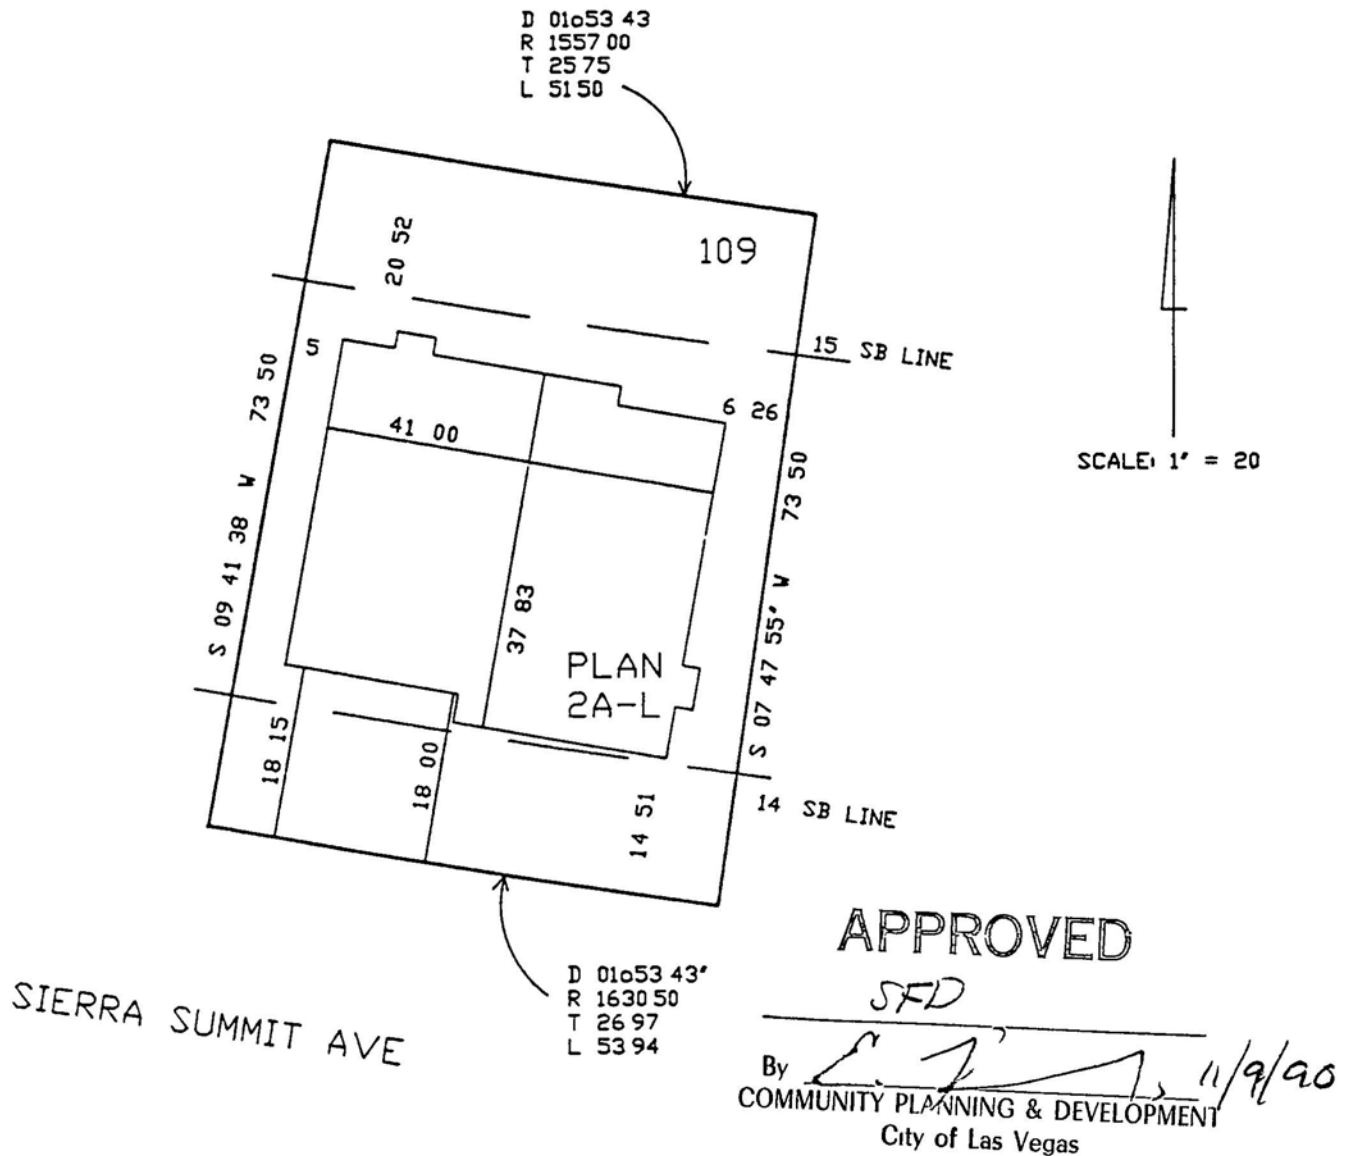

BRENNER & ASSOCIATES, INC.
LAND SURVEYORS

2915 W CHARLESTON BLVD., LAS VEGAS NEV 89102 / (702) 877-0317

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-089586

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

FOR INSPECTIONS CALL 799 2071

PLUMBING PERMIT

LOG NO & AREA P205 DATE 11/14/90 CONST VAL \$ADDRESS OF CONSTRUCTION 9428 Sierra Summit Avenue OWNER Daly Homes PHONE 642-9959CONTRACTOR Classic Plumbing, Inc. STATE LICENSE NO 016762 CITY LICENSE NO C 11 H 09201797LOT(s) 109 BLOCK D SUBDIVISION Las Colinas ZONEPROPOSED CONSTRUCTION Complete plumbing for new single family home USEPLUMBING
PERMIT NOApproval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10.00
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
10	Bathtub Shower Lavatory Toilet Urinal EA	2 00	20.00
1	Floor Drain Floor Sink Wash Tray Sink EA	2 00	2.00
1	Garbage Disposal Clothes Washer Dishwasher (residential) EA	2 00	2.00
	Garbage Disposal (commercial) EA	8 00	
	Clothes Washer Dishwasher (commercial) EA	2 00	
	Clothes Dryer (gas) (venting)	2 00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	2 00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
1	Hot Water Heater (Gas or Electric) EA	2 00	2.00
SEWER SYSTEM			
1	New Replacement Modification or Any Drainage Work	10 00	10.00
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
	Irrigation Single Family Dwelling	8 00	
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation		

UNITS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
	Medium Pressure System (Plan Check)	2 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Additional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTION

RECEIPT

FIXTURES X

FEE

2310 2403
PERMIT FEE 58 00

TOTAL FEES

PERMIT NO

MUST BE MACHINE VALIDATED

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED Diane M Byington 59
CONTRACTOR MASTER CARD NOBY Diane Hoesly Registered Master Plumber Spec Contractor or OwnerBUILDING DEPT 11/14/90 DATE

CITY OF LAS VEGAS, NEVADA

PERMIT NO 90-090975

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

FOR INSPECTIONS CALL 799-2071

AIR CONDITIONING PERMIT

LOG NO & AREA P205 DATE OCTOBER 16, 1990 CONST VAL \$ADDRESS OF CONSTRUCTION 9428 SIERRA SUMMIT AVENUE OWNER WATT NEVADA DEVELOPMENT PHONE 362-9878CONTRACTOR NEVCO AIR CONDITIONING & SHEET METAL STATE LICENSE NO 24377 CITY LICENSE NO C11023112033289LOT(s) 109 BLOCK D SUBDIVISION LAS COLINAS - SUMMERLIN ZONEPROPOSED CONSTRUCTION H V A C USE

UNITS	DESCRIPTION	FEE	TOTAL
1	PERMIT ISSUANCE		
1	For the issuance of each permit	15 00	15 00
	For issuing each supplemental permit	4 50	
	UNIT FEE SCHEDULE		
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance up to and including 100 000 Btu/h	9 00	
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance over 100 000 Btu/h	11 00	
	For the installation or relocation of each floor furnace including vent	9 00	
	For the installation or relocation of each suspended heater recessed wall heater or floor mounted unit heater	9 00	
	For the installation relocation or replacement of each appliance vent installed and not included in an appliance permit	4 50	
	For the repair of alteration of or addition to each heating appliance refrigeration unit cooling unit absorption unit or each heating cooling absorption or evaporative cooling system including installation of controls regulated by this code	9 00	
	For the installation or relocation of each boiler or compressor to and including three tons or each absorption system to and including 100 000 Btu/h	9 00	
1	For the installation or relocation of each boiler or compressor over three tons to and including 15 tons or each absorption system over 100 000 Btu/h and including 500 000 Btu/h	16 50	16 50
	For the installation or relocation of each boiler or compressor over 15 tons to and including 30 tons or each absorption system over 500 000 Btu/h to and including 1 000 000 Btu/h	22 50	
	For the installation or relocation of each boiler or compressor over 30 tons to and including 50 tons or for each absorption system over 1 000 000 Btu/h to and including 1 750 000 Btu/h	33 50	
	For the installation or relocation of each boiler or refrigeration compressor over 50 tons or each absorption system over 1 750 000 Btu/h	56 00	

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
	For each air handling unit to and including 10 000 cubic feet per minute including ducts attached thereto Note This fee shall not apply to an air handling unit which is a portion of a factory assembled appliance cooling unit evaporative cooler or absorption unit for which a permit is required elsewhere in this code	6 50	
	For each air handling unit over 10 000 cfm	11 00	
	For each evaporative cooler other than portable type	6 50	
	For each ventilation fan	COMMERCIAL 4 50 RESIDENTIAL 2 35	
	For each ventilation system which is not a portion of any heating or air conditioning system authorized by a permit	6 50	
	For the installation of each hood which is served by mechanical exhaust including the ducts for such hood	6 50	
	For each fire damper installed in an existing system	4 50	

OTHER INSPECTIONS AND FEES

	Inspections outside of normal business hours (minimum charge — three hours)	25 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code — \$15 00 EACH	15 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — two hours)	30 00 per hour	
	Mechanical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Gas piping which is directly related and necessary to the repair or replacement of heating air conditioning or refrigeration systems not exceeding 500 000 BTU H	6 00	

2310-2435

RECEIPT
0002

A/C 684 00

CHEK 684 00

5611A000 16 18

11/30/90

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED Julie Cullia CONTRACTOR NEVCO MASTER CARD NOBY Dona Hooley Spec Contr or OwnerBUILDING DEPT 4/29/90 DATEPERMIT FEE 1500TOTAL FEES 3150

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-091375

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

FOR INSPECTIONS CALL 799 2071

ELECTRICAL PERMIT

LOG NO & AREA T-205 DATE 11-28-90 CONST VAL \$ ADDRESS OF CONSTRUCTION 9428 SIERRA SUMMIT AVE. OWNER WATT-NEVADA DevelopmentCONTRACTOR HOLLAND & HOLLAND STATE LICENSE NO 021113 CITY LICENSE NO 021963(PRINT NAME OF MASTER ELECTRICIAN) BILL HOLLAND MASTER CARD NO 165 PHONE 362-6812PROPOSED CONSTRUCTION SINGLE FAMILY RES. 109/D USE ELECTRIC PERMIT NO

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
<u>1</u>	For Issuing Each Permit	10 00	<u>10-</u>
	Supplemental Fee	4 50	
APPLIANCE CHARGE			
	Residential or General Commercial		
<u>74</u>	Receptacle <u>51</u> Switch <u>23</u>	40	<u>29.60</u>
<u>25</u>	Each Light Fixture Socket or Exit Light Smoke Detector or Exhaust Fan	30	<u>7.50</u>
<u>6</u>	EACH OUTLET FOR SPECIAL PURPOSE Dishwasher Garbage Grinder Trash Compactor GFI Clothes Washer Dryer Electric Range Ovens Water Heater Space Heater Blast Coil Heater (PER KW) Mercury Lamp Quartz Lamp Sodium Lamp 20AMP Sign Circuit	70	<u>4.20</u>
	X Ray Unit	10 00	
	Area Lighting (First 3 000 Watts)	8 00	
	Each Additional 1 000 Watts	3 00	
MOTORS (1 H P AND OVER) TRANSFORMERS ELEVATORS WELDERS GENERATORS CHILLERS SIGNS AND A/C UNITS (OVER 5 TONS)			
	First H P or Ton For each Unit	3 00	
	First KVA For Each Unit	3 00	
	Each Additional H P Ton or KVA up to 50	50	
	Each Additional H P Ton or KVA over 50	35	
	Temporary power or Pole	6 00	
ELECTRIC SERVICE OR MAIN DISCONNECT			
<u>1</u>	Up to 200 AMP	6 00	<u>6-</u>
	400 AMP And 600 AMP	12 50	
	Over 600 AMP To 1200 AMP	25 00	
	Over 1200 AMP	50 00	
	Each Additional Meter Socket	50	
	Sub Panel Motor Control Center Disconnect Switch Transfer Switch (Each)	3 00	
	Swimming Pool (Residential)	20 00	
	Swimming Pool (Semi Public)	30 00	
	Spas	8 00	
	Recreational Vehicle Spaces (Each)	3 00	

UNITS	DESCRIPTION	FEE	TOTAL
	Busways Trolley or Plug in (Ea 100 Ft)	3 00	
	Gas Pumps Dispensers (Each)	3 00	
<u>2</u>	Permanent A/C Unit (5 Tons or Less)	3 00	<u>6-</u>
<u>2</u>	Each Air Handler	1 00	<u>2-</u>
RESIDENTIAL LOW VOLTAGE INSTALLATIONS			
	Speaker Outlets (Each)	30	
	Signal or Alarm Outlets (Each)	30	
	Amplifiers	2 00	
	Control Panel	50	
	TV Master System	30	
	Telephone or Computer Outlet	30	
OTHER INSPECTIONS AND FEES INCLUDES ISSUANCE FEES WHEN APPLICABLE			
	Inspections outside of normal business hours (minimum charge — three hours)	30 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30 00 EACH	30 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — one half hour) After work hours — \$30 00 per hour — minimum 1 hour	30 00 per hour	
	Starter Permit	50 00	
CONTRACT PRICE OR COST OF INSTALLATION			
	Commercial —Burglar Alarms		
	—Music Systems		
	—Data Processing		
	—Communication		
	Conduit Only—Contract Price		
	All Misc Electric		

Electrical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule

2310-2432

RECEIPT

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED HOMEOWNER CONTRACTOR

PERMIT FEE 6530LESS STARTER PERMIT TOTAL FEES PERMIT NO

MUST BE MACHINE VALIDATED

BUILDING DEPT

DATE

Permit Expires 180 Days After Abandonment of Work

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

IT NO 91-099702

PLUMBING PERMIT

LOG NO & AREA P-205 DATE 3-5-91 CONST VAL \$ _____ADDRESS OF CONSTRUCTION 9438 Sierra Summit Ave OWNER Watt Nevada PHONE 369-2401CONTRACTOR R & R Landscaping STATE LICENSE NO 0030153 CITY LICENSE NO C11-02189-2-
023628LOT(s) 109 BLOCK D SUBDIVISION Las Colinas ZONE _____

PROPOSED CONSTRUCTION _____ USE _____

PLUMBING
PERMIT NO _____Approval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
	Bathtub Shower Lavatory Toilet Urinal EA	2 00	
	Floor Drain Floor Sink Wash Tray Sink EA	2 00	
	Garbage Disposal Clothes Washer Dishwasher (residential) EA	2 00	
	Garbage Disposal (commercial) EA	8 00	
	Clothes Washer Dishwasher (commercial) EA	2 00	
	Clothes Dryer (gas) (venting)	2 00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	2 00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
	Hot Water Heater (Gas or Electric) EA	2 00	
SEWER SYSTEM			
	New Replacement Modification or Any Drainage Work	10 00	
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
	Single Family Dwelling	6 00	
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
1	Irrigation Single Family Dwelling	8 00	8
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation _____		

UNITS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
	Single Family Dwelling	6 00	
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
	Medium Pressure System (Plan Check)	12 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Additional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation _____		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTIONFIXTURES _____ X 03/08/91

FEE _____

2310 2403

PERMIT

FEE 18.00TOTAL
FEES _____

RECEIPT

0002

FLBG 360 00

CHEK 360 00

0369A000 11 44

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED

CONTRACTOR

MASTER CARD NO

BY

Registered Master Plumber Spec Contractor or Owner

BUILDING DEPT

DATE

PERMIT NO _____

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

PERMIT NO

90-039586

PLUMBING PERMIT

LOG NO & AREA

P205

DATE

11/14/90

CONST VAL \$

ADDRESS OF
CONSTRUCTION

9428 Sierra Summit Avenue

OWNER

Watt Nevada

PHONE 642-9959

CONTRACTOR

Classic Plumbing, Inc

STATE

LICENSE NO

016762

CITY

LICENSE NO

C 11 H 09201797

LOT(S)

109

BLOCK

D

SUBDIVISION

Las Colinas

ZONE

PROPOSED CONSTRUCTION Complete plumbing for new single family home

USE

PLUMBING
PERMIT NOApproval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10.00
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
10	Bathub Shower Lavatory Toilet Urinal EA	2 00	20.00
	Floor Drain Floor Sink Wash Tray Sink EA	2 00	2.00
1	Garbage Disposal Clothes Washer Dishwasher (residential) EA	2 00	2.00
	Garbage Disposal (commercial) EA	8 00	
	Clothes Washer Dishwasher (commercial) EA	2 00	
	Clothes Dryer (gas) (venting)	2 00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	2 00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
1	Hot Water Heater (Gas or Electric) EA	2 00	2.00
SEWER SYSTEM			
1	New Replacement Modification or Any Drainage Work	10 00	10.00
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
	Irrigation Single Family Dwelling	8 00	
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation		

UN TS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
	Medium Pressure System (Plan Check)	2 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Additional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTION

RECEIPT

FIXTURES X

FEE

2310 2403

PERMIT
FEE

58.00

TOTAL
FEES

PERMIT NO

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED

CONTRACTOR

MASTER CARD NO

BY

Registered Master Plumber Spec Contractor or Owner

BUILDING DEPT

DATE

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-091375

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FC



51209

ELECTRICAL PERMIT

LOG NO & AREA T-205 DATE 11-20-10 CONST VAL \$ADDRESS OF CONSTRUCTION 9428 SIERRA SUMMIT Ave. OWNER WATT-NEVADA DevelopmentCONTRACTOR HOLLAND & HOLLAND STATE LICENSE NO 021113 CITY LICENSE NO 021963(PRINT NAME OF MASTER ELECTRICIAN) BILL HOLLAND MASTER CARD NO 165 PHONE 362-6812PROPOSED CONSTRUCTION SINGLE FAMILY RES. 109/1D USE

ELECTRIC PERMIT NO

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10 -
	Supplemental Fee	4 50	
APPLIANCE CHARGE			
Residential or General Commercial			
74	Receptacle <u>51</u> Switch <u>23</u>	40	29 60
25	Each Light Fixture Socket or Exit Light Smoke Detector or Exhaust Fan	30	7 50
6	EACH OUTLET FOR SPECIAL PURPOSE Dishwasher Garbage Grinder Trash Compactor GFI Clothes Washer Dryer Electric Range Ovens Water Heater Space Heater Blast Coil Heater (PER KW) Mercury Lamp Quartz Lamp Sodium Lamp 20AMP Sign Circuit	70	4 20
	X Ray Unit	10 00	
	Area Lighting (First 3 000 Watts)	8 00	
	Each Additional 1 000 Watts	3 00	
MOTORS (1 H P AND OVER) TRANSFORMERS ELEVATORS WELDERS GENERATORS CHILLERS SIGNS AND A/C UNITS (OVER 5 TONS)			
	First H P or Ton For each Unit	3 00	
	First KVA For Each Unit	3 00	
	Each Additional H P Ton or KVA up to 50	50	
	Each Additional H P Ton or KVA over 50	35	
	Temporary power or Pole	6 00	
ELECTRIC SERVICE OR MAIN DISCONNECT			
1	Up to 200 AMP	6 00	6 -
	400 AMP And 600 AMP	12 50	
	Over 600 AMP To 1200 AMP	25 00	
	Over 1200 AMP	50 00	
	Each Additional Meter Socket	50	
	Sub Panel Motor Control Center Disconnect Switch Transfer Switch (Each)	3 00	
	Swimming Pool (Residential)	20 00	
	Swimming Pool (Semi Public)	30 00	
	Spas	8 00	
	Recreational Vehicle Spaces (Each)	3 00	

UNITS	DESCRIPTION	FEE	TOTAL
	Busways Trolley or Plug in (Ea 100 Ft)	3 00	
	Gas Pumps Dispensers (Each)	3 00	
2	Permanent A/C Unit (5 Tons or Less)	3 00	6 -
2	Each Air Handler	1 00	2 -
RESIDENTIAL LOW VOLTAGE INSTALLATIONS			
	Speaker Outlets (Each)	30	
	Signal or Alarm Outlets (Each)	30	
	Amplifiers	2 00	
	Control Panel	50	
	TV Master System	30	
	Telephone or Computer Outlet	30	
OTHER INSPECTIONS AND FEES INCLUDES ISSUANCE FEES WHEN APPLICABLE			
	Inspections outside of normal business hours (minimum charge -- three hours)	30 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30 00 EACH	30 00 each	
	Inspections for which no fee is specifically indicated (minimum charge -- one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge -- one half hour) After work hours -- \$30 00 per hour -- minimum 1 hour	30 00 per hour	
	Starter Permit	50 00	
CONTRACT PRICE OR COST OF INSTALLATION			
	Commercial --Burglar Alarms		
	--Music Systems		
	--Data Processing		
	--Communication		
	Conduit Only--Contract Price		
	All Misc Electric		

Electrical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule

2310-2432

RECEIPT

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED HOMEOWNER CONTRACTOR

PERMIT FEE 65-30

LESS STARTER PERMIT

TOTAL FEES

PERMIT NO

MUST BE MACHINE VALIDATED

BUILDING DEPT

DATE

Permit Expires 180 Days After Abandonment of Work

**Schuck COMPONENT SYSTEMS, INC.**

8205 NORTH 67TH AVENUE □ GLENDALE ARIZONA 85302 □ TELEPHONE (602) 931 • 3661

MARCH 21, 1991

TO WATT INDUSTRIES


RE. LOS COLINAS

SCHUCK COMPONENTS SYSTEMS WILL TAKE FULL RESPONSIBILITY FOR
THE LAMINATED GLASS IN LIEU OF TEMPERED GLASS IN THE
SIDELITES WE FURNISHED FOR THE FOLLOWING LOTS:

LOT 112	BLK D	9500 SIERRA SUMMIT AVE.
LOT 109	BLK D	9428 SIERRA SUMMIT AVE.
LOT 40	BLK B	9437 SIERRA SUMMIT AVE.
LOT 44	BLK B	9513 SIERRA SUMMIT AVE.
LOT 46	BLK B	9521 SIERRA SUMMIT AVE.

IF I MAY BE OF FURTHER ASSISTANCE, PLEASE CALL.

SINCERELY,


DEBBIE L. KASPRZAK
PURCHASING AGENT



CASHDAN

62

844 East Sahara Avenue, Las Vegas, Nevada 89104
(702) 735-7895
FAX (702) 735-3190

TO: City of Las Vegas Building Dept
City Hall
400 E Stewart
Las Vegas, Nevada 89101
In care of Pete White Concrete

RE: Epoxy Grouted All Thread Anchors

DATE	Dec 12, 1990	JOB NO	89-603-30
PROJECT	Los Colinas		
LOCATION	Del Webb Drive		
CONTRACTOR	Pete White	OWNER	
WEATHER	Cloudy	TEMP	50 ° at 11:00 AM ° at PM
PRESENT AT SITE	John Cannock - Pete White		

THE FOLLOWING WAS NOTED On December 12th I observed the preparation and installation on allthread bar for interior holdowns for the first 10 completed units at Los Colinas Development located off of Del Webb Dr, Las Vegas, Nevada The installation of the allthread bars appeared to follow the job specifications and ICBO recommendations, ie debris free drilled anchor bolt holes with correct diameters and embedment depths, and correct epoxying procedures The work in general followed good construction practices

* NEED ADDRESSES !

9428 9432 9436, 9500, 9504, 9508 9512 9516 9520
+ 9524 SIERRA Summit


SIGNED

[Signature]

COPIES TO Pete White, City of Las Vegas

REVIEWED BY

[Signature]



SPECIAL INSPECTION REPORT



Schuck COMPONENT SYSTEMS, INC.

8208 NORTH 67TH AVENUE □ GLENDALE, ARIZONA 85302 □ TELEPHONE (602) 931 • 3661

MARCH 21, 1991

TO: WATT INDUSTRIES


RE. LOS COLINAS

SCHUCK COMPONENTS SYSTEMS WILL TAKE FULL RESPONSIBILITY FOR THE LAMINATED GLASS IN LIEU OF TEMPERED GLASS IN THE SIDELITES WE FURNISHED FOR THE FOLLOWING LOTS:

LOT 112	BLK D	9500 SIERRA SUMMIT AVE.
LOT 109	BLK D	9428 SIERRA SUMMIT AVE.
LOT 40	BLK B	9437 SIERRA SUMMIT AVE.
LOT 44	BLK B	9513 SIERRA SUMMIT AVE.
LOT 46	BLK B	9521 SIERRA SUMMIT AVE.

IF I MAY BE OF FURTHER ASSISTANCE, PLEASE CALL.

SINCERELY,


DEBBIE L. KASPRZAK
PURCHASING AGENT

WATT NEVADA
DEVELOPMENT CORPORATION

Bob - Beeper

253-3533

MEMORANDUM

TO: All subcontractors, suppliers and Watt Nevada staff

FROM: Marc Stenzel 

DATE: October 15, 1990

SUBJECT: Las Colinas - Phase I - Addresses

<u>Lot</u>	<u>Block</u>	<u>Plan #</u>	<u>Elevation</u>	<u>Garage Hand</u>	<u>Address</u>
55	D	1	C	R	2124 Desert Pines Street
56	D	2	B	L	2128 Desert Pines Street
57	D	4	A	R	2132 Desert Pines Street
38	B	3	A	R	9429 Sierra Summit Avenue
39	B	4	A	R	9433 Sierra Summit Avenue
40	B	2	C	R	9437 Sierra Summit Avenue
41	C	4	B	R	9501 Sierra Summit Avenue
42	C	3	B	R	9505 Sierra Summit Avenue
43	C	1	C	R	9509 Sierra Summit Avenue
44	C	2	B	R	9513 Sierra Summit Avenue
45	C	3	C	R	9517 Sierra Summit Avenue
46	C	2	A	R	9521 Sierra Summit Avenue
47	C	4	C	R	9525 Sierra Summit Avenue
109	D	2	A	L	9428 Sierra Summit Avenue
110	D	1	B	L	9432 Sierra Summit Avenue
111	D	4	A	L	9436 Sierra Summit Avenue
112	D	2	B	L	9500 Sierra Summit Avenue
113	D	4	C	L	9504 Sierra Summit Avenue
114	D	3	A	L	9508 Sierra Summit Avenue
115	D	1	A	L	9512 Sierra Summit Avenue
116	D	4	B	L	9516 Sierra Summit Avenue
117	D	1	C	L	9520 Sierra Summit Avenue
118	D	3	B	L	9524 Sierra Summit Avenue



gale insulation of nevada, inc

5115 INDUSTRIAL ROAD SUITE 808
LAS VEGAS NEVADA 89118
(702) 739 6798



Installed Insulation Certificate

We certify insulation material listed herein meeting applicable federal state and local specifications has been installed at the following residence surrounding conditioned space

R FACTOR	AREA	TYPE	INCHES/BAGS (BLOWN)
R30	CEILING AREA	FIBERGLASS BATTS	9½"
R13	EXTERIOR WALL	FIBERGLASS BATTS	3 5/8 "
R30	CEILING AREA	CELLULOSE BLOW	8 7"

Certified by

Michelle Deano

Title

OFFICE MANAGER

LAS COLINAS BK D LOT 109

Address Lot Number

9428 SIERRA SUMMIT AVE

Date Installed

2-13-91

15

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7428 Sierra Summit		PERMIT NO. 88942
LOT NO.	MAP NO. S-104	INSPECTOR 60 th
SUBDIVISION NAME		DATE 11-19-90
INSPECTOR SIGNATURE S Van Patten		PHONE 11-20-90

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ PERMIT REQUIRED☐ **STOP WORK**☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☒ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☒ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	 PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	 PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

[illegible]

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9428 Sierra Summit		PERMIT NO 88942
LOT NO	MAP NO 9-246p	INSPECTOR 84
SUBDIVISION NAME		DATE 1-22-91
INSPECTOR SIGNATURE R Wund		PHONE
		INSPECTION DATE 1-23-91

- Shear - Nail all upper walls -
- ① HD-2 at south east corner at Front - no bolt
 - ② " " " " Kitchen on wrong walls - OK
 - ③ Install mud ring at wfer
 - ④ Stuff all holes at plates (Firestopping)
 - ⑤ Plumber req to read boring and notching at garage shear wall - stud shoes
 - ⑥ Plumbing going to second floor at family rm notched bottom corner of truss out get fix
 - ⑦ All red-heads + Quick-bolts must be tightened
 - ⑧ Get fix on truss at duct other side - at Kit

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☒ B 5	FRAMING / Shear	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT OK	☒ E 2	ROUGH ELECTRICAL OK
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9428 Sierra Summit		PERMIT NO 88942	
LOT NO	MAP NO 11-2.43P	INSPECTOR 84	DATE 1-30-91
SUBDIVISION NAME Las Colinas			PHONE
INSPECTOR SIGNATURE RW			INSPECTION DATE 1-31-91

① Hold Insulation below combustion Air Intake - Hold units 16" bottom cord

- Check All units -

All Corrections Made

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**
☐ **PERMIT REQUIRED**
☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☒ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☒ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☒ M 1	ROUGH VENT	☒ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS <i>9458 Sierra Summit</i>		PERMIT NO <i>88942</i>	
LOT NO	MAP NO <i>S-1020a</i>	INSPECTOR <i>84</i>	DATE <i>2-1-91</i>
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE <i>RWHL</i>			INSPECTION DATE <i>2-1-91</i>

bath nailing Incomplete
Drywall upstairs "

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☒ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☒ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9428 Sierra Summit Blvd		PERMIT NO. 88942	
LOT NO.	MAP NO. 5-247P	INSPECTOR 84	DATE 3-18-91
SUBDIVISION NAME Las Calinas			PHONE Bot
INSPECTOR SIGNATURE 			INSPECTION DATE 3-19-91

① Change disconnect to J-box
at condenser

② Grounds at panel - no clustering

Temp power only

Tag # 22479

Connect Above by Bld Final

Remove temp pde at near to Bld Final

☒ PARTIAL INSPECTION DESCRIPTION Temp only					
☒ APPROVED		☐ PERMIT REQUIRED		☐ STOP WORK	
☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071					
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION	BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)
---	--

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9428 Sierra Summit Ave		PERMIT NO 88942	
LOT NO	MAP NO 4-1229P	INSPECTOR 84	DATE 9-19-91
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 3-20-91

① Hood At Kit not sealed properly

② Water bond clamp loose

③ Repair window at Kit - sink

④ Repair & seat stucco at all piping etc

⑤ Grading at Front covering up drainage b/lks at well

⑥ Back yard swales not complete

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED
☐ PERMIT REQUIRED
☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☒ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	<u>POOL</u> PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	<u>POOL</u> PRE PLASTER / FINAL	☒ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 368-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9428 Sierra Summit			PERMIT NO 88942
LOT NO	MAP NO 9 2'54	INSPECTOR 84	DATE 3/20/91
SUBDIVISION NAME Las Colinas			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i>			INSPECTION DATE 3-21-91

Install GFI Recept at Kitchen counter - within 6" of sink
will ck 3-22-91

☐ PARTIAL INSPECTION DESCRIPTION

☒ APPROVED *
 ☐ PERMIT REQUIRED
 ☐ STOP WORK
☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☒ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☒ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY, CITY OF LAS VEGAS



**PERMIT
NUMBER**

88942

**INSPECTION
NUMBER**

JOB ADDRESS

9428 Sierra Summit Ave

LOT NO

BLOCK NO

SUBDIVISION NAME

FIRE DEPT MAP NO

JOB PHONE

CALL IN DATE

CALL IN TIME

SCHEDULE DATE

3 21 91

5 10 27A

INSPECTOR NO

INSPECTOR NAME

84

**INSPECTION
REQUESTED**

140- Final Bldg

240- Final Mechanical

340- F/Electrical

440- F/Plumbing

GFI Installed at Kit.

☐ PARTIAL
INSPECTION

☐ PARTIAL
APPROVAL (P)

PARTIAL DESCRIPTION

☐ APPROVED
(A)

☐ STOP
WORK (S)

☐ COMMENTS
(C)

☐ TEMPORARY
APPROVAL (T) - UNTIL

☐ HOLD
(H)

☐ REJECTED (R)

REINSPECTION REQUIRED CALL 799 2071

☐ REFEE (F)

REINSPECTION FEE REQUIRED PAY AT CITY HALL
3RD FLOOR 400 E STEWART STREET

☐ PERMIT
REQUIRED

**INSPECTOR
SIGNATURE**

RW

INSPECTION DATE

3-22-91

☐ **PROJECT
COMPLETE**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

IF YOU HAVE ANY QUESTIONS ON THIS INSPECTION YOU MAY
CALL THE INSPECTOR FROM 7 00 A M 7 15 A M OR 2 45 P M 3 00 P M AT

FOR ADDITIONAL ASSISTANCE CALL 386-6251
SEE REVERSE SIDE FOR INSPECTION TYPES

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

[illegible]☐ PARTIAL INSPECTION DESCRIPTION

APPROVED

☐ PERMIT REQUIRED☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL -- FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☒ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	NOT INSPECTED	NOT ON WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS <i>9428 Sierra Summit Av</i>		PERMIT NO <i>88942</i>	
LOT NO	MAP NO <i>12:09 p 84</i>	INSPECTOR	DATE <i>3/15/91</i>
SUBDIVISION NAME <i>Los Colinas</i>		PHONE	
INSPECTOR SIGNATURE <i>BWard</i>		INSPECTION DATE <i>3-18-91</i>	

gas pipe & final meter

Elect Incomplete -

Next Time Electrical
will be refee -

☒ PARTIAL INSPECTION DESCRIPTION

Gas Test only - Tag # 14350

☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL -- FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☒ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE -CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

[illegible]

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9428 Sierra Summit		PERMIT NO. 88942
LOT NO	MAP NO 11 1:48	INSPECTOR 62
SUBDIVISION NAME		DATE 12-6-90
INSPECTOR SIGNATURE [Signature]		PHONE [Blank]
INSPECTION DATE 12-7-90		

~~Sheet~~

☐ PARTIAL INSPECTION DESCRIPTION

☒ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL – FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☒ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	 PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	 PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9428 Sierra Summit		PERMIT NO 88942
LOT NO	MAP NO 20 252P	INSPECTOR 84
SUBDIVISION NAME Z-A-L		DATE 1-10-91
INSPECTOR SIGNATURE RW		PHONE
		INSPECTION DATE 1-11-91

- ① D1b 90° not allowed IN horizontal position
- ② All walls that are bearing when notched are drilled within 5/8" of edge or over 25% require stud-shoes
- ③ All F.H.A. straps at plates req #16's at each end when plates are notched out

Items 2 + 3 req on all house when notching or cutting ect occur

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY / CITY OF LAS VEGAS

JOB ADDRESS 6428 Sierra Summit			PERMIT NO 88194
LOT NO	MAP NO 14-553p	INSPECTOR JY	DATE 2-4-91
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE RWand			INSPECTION DATE 2-5-91

☐ PARTIAL INSPECTION DESCRIPTION			☐ PERMIT REQUIRED			☐ STOP WORK		
☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071								
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION			
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO			
☐ B 2	STEM WALL -- FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW			
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO			
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM			
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER			
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE			
☒ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING					
☒ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL			
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL			
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL			
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION			
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL			
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER			
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C OF O ISSUANCE (Commercial Only)						

FOR ASSISTANCE CALL 386-6251

UltraKote, Inc.

FIBER - REINFORCED STUCCO

2865 NW Grand Avenue Phoenix, AZ 85017 (602) 484-0320 FAX (602) 278-2699

Job Address

INSTALLATION CARD

ICBO Report No 4658

9428 Sierra Summit

Date of Job Completion 1/30

Plastering Contractor

Name

Norede Staro Plastering

Address

2442 Moose Rd

Telephone No

(22) 849 882

Above contractor is approved by UltraKote Inc

This is to certify that the exterior coating system on the building exterior at the above address has been installed in accordance with the evaluation report specified above and the manufacturer's instructions

Signature of authorized representative
of plastering contractor

Date

This installation card must be presented to the building inspector after completion of work and before final inspection
