

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

FOR INSPECTIONS CALL 799-2071

PERMIT NO

90-088944

BUILDING PERMIT

FOR Single Family Dwelling Remodel
Additions Misc Residential Construction

LOG NO & AREA T-205 DATE Oct 8, 90 CONST VAL \$ 46,000.00
ADDRESS OF CONSTRUCTION 9432 Suria Summit Ave OWNER Watt Nevada PHONE 309-2401
LOT(s) 110 BLOCK D SUBDIVISION LAS COLINAS Summerlin Village #1 North ZONE P/C
PROPOSED CONSTRUCTION STFD with fireplace USE _____
THIS PERMIT FOR BLDG ☒ A/C ☐ ELEC ☐ PLBG ☐ OTHER PERMITS REQD FENCE ☐ OFF SITE ☐ SWIM POOL ☐
FLOOR AREA BSMT n/a 1ST 1292 2ND 285 GARAGE 320 PORCH 90 TOTAL 1987
CONTRACTOR Watt Nevada Development Corp STATE LICENSE NO 0030439 CITY LICENSE NO C11-034092
ARCHITECT Arlo Brown, A.I.C. ENGINEER G.C. Wallace 042316
MASTER PLUMBER/CONTRACTOR _____ MASTER ELECTRICIAN/CONTRACTOR _____

OTHER INSPECTIONS AND FEES

- 1 Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
- 2 Re inspection fee during normal business hours assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30.00 per hour
- 3 Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour)
- 4 Additional plan review required by changes additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours)

CONDITIONS OF THE PERMIT

- 1 I agree to call the City Building Department for inspections before concrete is poured before rough wiring electrical plumbing framing is covered Also for air conditioning drywall and sheathing inspection
- 2 I agree that when the job is completed that I will call for final inspection before occupancy
- 3 I agree to perform all construction in accordance with City Ordinances and Building Codes
- 4 The Contractor's signature below denotes authority from the owner to sign in his behalf and that the owner is aware of all requirements of this application and permit Separate permits must be taken out for work outlined above this agreement
- 5 I have read and understand the contents of this application and permit I hereby state that the information I have supplied on this application is true and correct
- 6 Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way
- 7 24 HOUR MINIMUM NOTICE REQUIRED FOR INSPECTIONS

BY [Signature] 10-15-90
I HEREBY DECLARE THAT I AM THE LEGAL OWNER OF THE ABOVE PROPERTY OWNER
BY _____ AGENT

I hereby certify that I have reviewed this application and the proposed plans and have found that the proposed development meets the requirements of the City of Las Vegas Flood Hazard Reduction Ordinance for the issuance of this Development Permit

LAND DEVELOPMENT AND FLOOD CONTROL ENGINEER

PLANNING DEPT

BUILDING DEPT

10-12-90

DATE

11/9/90

DATE

10/9/90

DATE

SPECIAL CONDITIONS

Model #4-1

RECEIPT

PLUMBING		FEE	ELECTRICAL		FEE
WATER DISTRIBUTION	6.00		RECEPTACLE _____ SWITCH _____		40
SEWER SYSTEM NEW OR MODIFICATION	10.00		EACH LIGHT FIXTURE OR SOCKET _____		30
FIXTURES WATER SOFTENER HW HEATER	2.00		SPECIAL OUTLET APPLIANCE ETC		70
GARBAGE DISPOSAL WASHER	2.00		SERVICE/PANEL SUB/3.00 200A/6.00 400A/12.50		
FUEL PIPING	6.00		A/C UNIT OR MOTORS	3.00	
IRRIGATION SYSTEM	8.00		2310 2432 TOTAL		
MISC			MISC		
2310 2433 TOTAL			2310 2431 ISSUANCE FEE		
AIR CONDITIONING		FEE	7143 2973 SEWER CONNECTION		\$625
NEW UNIT 3 TON = 9.00 OVER = 16.50			2310 2431 PLAN REVIEW FEE		\$318
FURNACE TO 100 000/9.00 OVER/11.00			2310 2431 BLDG PERMIT FEE		\$943
VAPORATIVE COOLER	6.50		TOTAL FEES		
VENTILATION FAN	2.35				
2310 2435 TOTAL					


PERMIT NO _____
MUST BE MACHINE VALIDATED

Permit Expires 180 Days After Abandonment of Work

LAS COLINAS
FILE _____, PG _____

LOT 110, BLK 'D'

ADDRESS _____

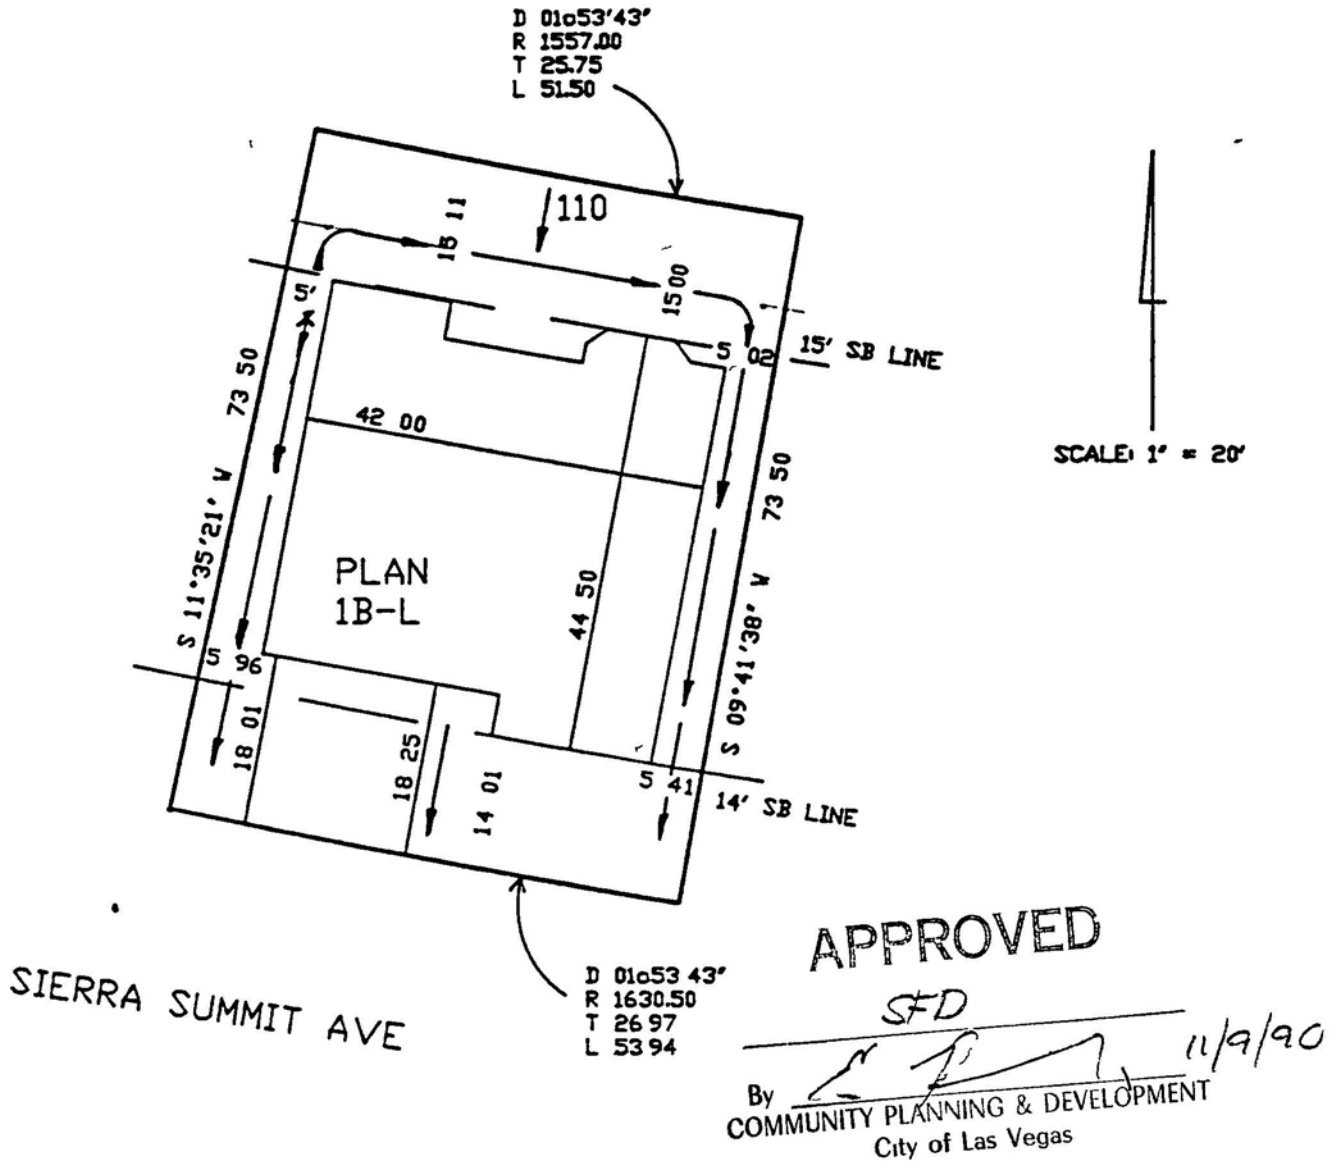

NOTE: 14' FRONT SB LINE
15' REAR SB LINE
5' SIDE SB LINE
15' SIDE SB LINE AT
CORNER LOTS

BRENNER & ASSOCIATES, INC
LAND SURVEYORS

2915 W CHARLESTON BLVD, LAS VEGAS NEV 89102 / (702) 877-0317

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-089568

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

FOR INSPECTIONS CALL 799 2071

PLUMBING PERMIT

LOG NO & AREA P205 DATE 11/14/90 CONST VAL \$ _____ADDRESS OF CONSTRUCTION 9432 Sierra Summit OWNER Watt Nevada PHONE 642-9959CONTRACTOR Classic Plumbing, Inc STATE LICENSE NO 016762 CITY LICENSE NO C 11 H 09201797LOT(s) 110 BLOCK D SUBDIVISION Las Colinas ZONE _____PROPOSED CONSTRUCTION Complete plumbing for new single family home USE _____
PLUMBING PERMIT NO _____

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10.00
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
8	Bathtub Shower Lavatory Toilet Urinal	EA 2 00	16.00
1	Floor Drain Floor Sink Wash Tray Sink	EA 2 00	2.00
1	Garbage Disposal Clothes Washer Dishwasher (residential)	EA 2 00	2.00
	Garbage Disposal (commercial)	EA 8 00	
	Clothes Washer Dishwasher (commercial)	EA 2 00	
	Clothes Dryer (gas) (venting)	2 00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	2 00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
1	Hot Water Heater (Gas or Electric)	EA 2 00	2.00
SEWER SYSTEM			
1	New Replacement Modification or Any Drainage Work	10 00	10.00
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
	Irrigation Single Family Dwelling	8 00	
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation _____		

UNITS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
	Medium Pressure System (Plan Check)	2 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Additional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation _____		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTION

RECEIPT

FIXTURES _____ X _____

FEE _____

2310 2403

PERMIT FEE 54.00TOTAL
FEES _____

PERMIT NO _____

MUST BE MACHINE VALIDATED

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

Diane M. Byington 59
 SIGNED _____ CONTRACTOR _____ MASTER CARD NO _____

BY _____ Registered Master Plumber Spec Contractor or Owner

Don Hooley 11/14/90
 BUILDING DEPT _____ DATE _____

CITY OF LAS VEGAS, NEVADA

PERMIT NO 90-090977

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR INSPECTIONS CALL 799-2071

AIR CONDITIONING PERMIT

LOG NO & AREA P205 DATE OCTOBER 16, 1990 CONST VAL \$ADDRESS OF CONSTRUCTION 9432 SIERRA SUMMIT AVENUE OWNER WATT NEVADA DEVELOPMENT PHONE 362-9878CONTRACTOR NEVCO AIR CONDITIONING & SHEET METAL STATE LICENSE NO 24377 CITY LICENSE NO C11023112033289LOT(S) 110 BLOCK D SUBDIVISION LAS COLINAS - SUMMERLIN ZONEPROPOSED CONSTRUCTION H V.A C USE

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For the issuance of each permit	15 00	1500
	For issuing each supplemental permit	4 50	
UNIT FEE SCHEDULE			
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance up to and including 100 000 Btu/h	9 00	
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance over 100 000 Btu/h	11 00	
	For the installation or relocation of each floor furnace including vent	9 00	
	For the installation or relocation of each suspended heater recessed wall heater or floor mounted unit heater	9 00	
	For the installation relocation or replacement of each appliance vent installed and not included in an appliance permit	4 50	
	For the repair of alteration of or addition to each heating appliance refrigeration unit cooling unit absorption unit or each heating cooling absorption or evaporative cooling system including installation of controls regulated by this code	9 00	
	For the installation or relocation of each boiler or compressor to and including three tons or each absorption system to and including 100 000 Btu/h	9 00	
1	For the installation or relocation of each boiler or compressor over three tons to and including 15 tons or each absorption system over 100 000 Btu/h and including 500 000 Btu/h	16 50	1650
	For the installation or relocation of each boiler or compressor over 15 tons to and including 30 tons or each absorption system over 500 000 Btu/h to and including 1 000 000 Btu/h	22 50	
	For the installation or relocation of each boiler or compressor over 30 tons to and including 50 tons or for each absorption system over 1 000 000 Btu/h to and including 1 750 000 Btu/h	33 50	
	For the installation or relocation of each boiler or refrigeration compressor over 50 tons or each absorption system over 1 750 000 Btu/h	56 00	

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
	For each air handling unit to and including 10 000 cubic feet per minute including ducts attached thereto Note This fee shall not apply to an air handling unit which is a portion of a factory assembled appliance cooling unit evaporative cooler or absorption unit for which a permit is required elsewhere in this code	6 50	
	For each air handling unit over 10 000 cfm	11 00	
	For each evaporative cooler other than portable type	6 50	
	For each ventilation fan	COMMERCIAL RESIDENTIAL	4 50 2 35
	For each ventilation system which is not a portion of any heating or air conditioning system authorized by a permit	6 50	
	For the installation of each hood which is served by mechanical exhaust including the ducts for such hood	6 50	
	For each fire damper installed in an existing system	4 50	

OTHER INSPECTIONS AND FEES

	Inspections outside of normal business hours (minimum charge — three hours)	25 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$15 00 EACH	15 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — two hours)	30 00 per hour	
	Mechanical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Gas piping which is directly related and necessary to the repair or replacement of heating air conditioning or refrigeration systems not exceeding 500 000 BTU H	6 00	

2310-2435

RECEIPT

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED Julie Cullina Nevco CONTRACTOR MASTER CARD NOBY Don Hooley Spec Contr or OwnerBUILDING DEPT 11/29/90 DATE

PERMIT FEE

TOTAL FEES

Permit Expires 180 Days After Abandonment of Work

MUST BE MACHINE VALIDATED

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-021376

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR INSPECTIONS CALL 799 2071

ELECTRICAL PERMIT

LOG NO & AREA P-205 DATE 11-28-90 CONST VAL \$ _____ADDRESS OF CONSTRUCTION 9432 SIERRA SUMMIT OWNER WATT-NEVADACONTRACTOR HOLLAND & HOLLAND STATE LICENSE NO 021113 CITY LICENSE NO 021963(PRINT NAME OF MASTER ELECTRICIAN) BILL HOLLAND MASTER CARD NO 165 PHONE 362-6812PROPOSED CONSTRUCTION SINGLE FAMILY RES 110/10 USE _____

ELECTRIC PERMIT NO _____

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
<u>1</u>	For Issuing Each Permit	10 00	<u>10 -</u>
	Supplemental Fee	4 50	
APPLIANCE CHARGE			
Residential or General Commercial			
<u>78</u>	Receptacle <u>47</u> Switch <u>31</u>	40	<u>31.20</u>
<u>30</u>	Each Light Fixture Socket or Exit Light Smoke Detector or Exhaust Fan	30	<u>9 -</u>
<u>7</u>	EACH OUTLET FOR SPECIAL PURPOSE Dishwasher Garbage Grinder Trash Compactor GFI Clothes Washer Dryer Electric Range Ovens Water Heater Space Heater Blast Coil Heater (PER KW) Mercury Lamp Quartz Lamp Sodium Lamp 20AMP Sign Circuit	70	<u>490</u>
	X Ray Unit	10 00	
	Area Lighting (First 3 000 Watts)	8 00	
	Each Additional 1 000 Watts	3 00	
MOTORS (1 H P AND OVER) TRANSFORMERS ELEVATORS WELDERS GENERATORS CHILLERS SIGNS AND A/C UNITS (OVER 5 TONS)			
	First H P or Ton For each Unit	3 00	
	First KVA For Each Unit	3 00	
	Each Additional H P Ton or KVA up to 50	50	
	Each Additional H P Ton or KVA over 50	35	
	Temporary power or Pole	6 00	
ELECTRIC SERVICE OR MAIN DISCONNECT			
<u>1</u>	Up to 200 AMP	6 00	<u>6 -</u>
	400 AMP And 600 AMP	12 50	
	Over 600 AMP To 1200 AMP	25 00	
	Over 1200 AMP	50 00	
	Each Additional Meter Socket	50	
	Sub Panel Motor Control Center Disconnect Switch Transfer Switch (Each)	3 00	
	Swimming Pool (Residential)	20 00	
	Swimming Pool (Semi Public)	30 00	
	Spas	8 00	
	Recreational Vehicle Spaces (Each)	3 00	

UNITS	DESCRIPTION	FEE	TOTAL
	Busways Trolley or Plug in (Ea 100 Ft)	3 00	
	Gas Pumps Dispensers (Each)	3 00	
<u>2</u>	Permanent A/C Unit (5 Tons or Less)	3 00	<u>6 -</u>
<u>2</u>	Each Air Handler	1 00	<u>2 -</u>
RESIDENTIAL LOW VOLTAGE INSTALLATIONS			
	Speaker Outlets (Each)	30	
	Signal or Alarm Outlets (Each)	30	
	Amplifiers	2 00	
	Control Panel	50	
	TV Master System	30	
	Telephone or Computer Outlet	30	
OTHER INSPECTIONS AND FEES INCLUDES ISSUANCE FEES WHEN APPLICABLE			
	Inspections outside of normal business hours (minimum charge — three hours)	30 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30 00 EACH	30 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — one half hour) After work hours — \$30 00 per hour — minimum 1 hour	30 00 per hour	
	Starter Permit	50 00	
CONTRACT PRICE OR COST OF INSTALLATION			
	Commercial —Burglar Alarms		
	—Music Systems		
	—Data Processing		
	—Communication		
	Conduit Only—Contract Price		
	All Misc Electric		

Electrical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule

2310-2432

RECEIPT

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED HOMEOWNER CONTRACTOR

PERMIT FEE 6910

LESS STARTER PERMIT _____

TOTAL FEES _____

PERMIT NO _____

MUST BE MACHINE VALIDATED

BUILDING DEPT

DATE

Permit Expires 180 Days After Abandonment of Work

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

30162

MIT NO 1-099704

071

PLUMBING PERMIT

LOG NO & AREA P-205 DATE 3-5-91 CONST VAL \$ _____ADDRESS OF CONSTRUCTION 9432 Sierra Summit Ave OWNER Watt Nevada PHONE 369-2401CONTRACTOR R & R Landscaping STATE LICENSE NO 0030153 CITY LICENSE NO C11-02189-2-
023628LOT(s) 110 BLOCK D SUBDIVISION Las Colinas ZONE _____PROPOSED CONSTRUCTION Irrigation USE _____PLUMBING
PERMIT NO _____Approval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
	Bathtub Shower Lavatory Toilet Urinal EA	2 00	
	Floor Drain Floor Sink Wash Tray Sink EA	2 00	
	Garbage Disposal Clothes Washer Dishwasher (residential) EA	2 00	
	Garbage Disposal (commercial) EA	8 00	
	Clothes Washer Dishwasher (commercial) EA	2 00	
	Clothes Dryer (gas) (venting)	2 00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	2 00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
	Hot Water Heater (Gas or Electric) EA	2 00	
SEWER SYSTEM			
	New Replacement Modification or Any Drainage Work	10 00	
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
	Single Family Dwelling	6 00	
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
1	Irrigation Single Family Dwelling	8 00	8
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation _____		

UNITS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
	Single Family Dwelling	6 00	
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
	Medium Pressure System (Plan Check)	2 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Additional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation _____		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTION

FIXTURES _____ X _____

FEE _____

2310 2403

PERMIT
FEE 18.00TOTAL
FEES _____

RECEIPT

PERMIT NO _____

MUST BE MACHINE VALIDATED

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED

CONTRACTOR

MASTER CARD NO

BY

Registered Master Plumber Spec Contractor or Owner

BUILDING DEPT

DATE

3/83

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-091376

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386 6251

FOR IN



51210

ELECTRICAL PERMIT

LOG NO & AREA

P-205

DA

CONST VAL \$

ADDRESS OF
CONSTRUCTION

9432 SIERRA SUMMIT

OWNER

WATT-NEVADA

CONTRACTOR

HOLLAND & HOLLAND

STATE
LICENSE NO

021113

CITY
LICENSE NO

021963

(PRINT NAME OF MASTER ELECTRICIAN)

BILL HOLLAND

MASTER CARD NO

165

PHONE 362-6812

PROPOSED CONSTRUCTION

SINGLE FAMILY RES

110/D USE

ELECTRIC
PERMIT NOApproval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10 -
	Supplemental Fee	4 50	
APPLIANCE CHARGE			
Residential or General Commercial			
78	Receptacle 47 Switch 31	40	3120
30	Each Light Fixture Socket or Exit Light Smoke Detector or Exhaust Fan	30	9 -
7	EACH OUTLET FOR SPECIAL PURPOSE Dishwasher Garbage Grinder Trash Compactor GFI Clothes Washer Dryer Electric Range Ovens Water Heater Space Heater Blast Coil Heater (PER KW) Mercury Lamp Quartz Lamp Sodium Lamp 20AMP Sign Circuit	70	490
	X Ray Unit	10 00	
	Area Lighting (First 3 000 Watts)	8 00	
	Each Additional 1 000 Watts	3 00	
MOTORS (1 H P AND OVER) TRANSFORMERS ELEVATORS WELDERS GENERATORS CHILLERS SIGNS AND A/C UNITS (OVER 5 TONS)			
	First H P or Ton for each Unit	3 00	
	First KVA For Each Unit	3 00	
	Each Additional H P Ton or KVA up to 50	50	
	Each Additional H P Ton or KVA over 50	35	
	Temporary power or Pole	6 00	
ELECTRIC SERVICE OR MAIN DISCONNECT			
1	Up to 200 AMP	6 00	6 -
	400 AMP And 600 AMP	12 50	
	Over 600 AMP To 1200 AMP	25 00	
	Over 1200 AMP	50 00	
	Each Additional Meter Socket	50	
	Sub Panel Motor Control Center Disconnect Switch Transfer Switch (Each)	3 00	
	Swimming Pool (Residential)	20 00	
	Swimming Pool (Semi Public)	30 00	
	Spas	8 00	
	Recreational Vehicle Spaces (Each)	3 00	

UNITS	DESCRIPTION	FEE	TOTAL
	Busways Trolley or Plug in (Ea 100 Ft)	3 00	
	Gas Pumps Dispensers (Each)	3 00	
2	Permanent A/C Unit (5 Tons or Less)	3 00	6 -
2	Each Air Handler	1 00	2 -
RESIDENTIAL LOW VOLTAGE INSTALLATIONS			
	Speaker Outlets (Each)	30	
	Signal or Alarm Outlets (Each)	30	
	Amplifiers	2 00	
	Control Panel	50	
	TV Master System	30	
	Telephone or Computer Outlet	30	
OTHER INSPECTIONS AND FEES INCLUDES ISSUANCE FEES WHEN APPLICABLE			
	Inspections outside of normal business hours (minimum charge — three hours)	30 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30 00 EACH	30 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — one half hour) After work hours — \$30 00 per hour — minimum 1 hour	30 00 per hour	
	Starter Permit	50 00	
CONTRACT PRICE OR COST OF INSTALLATION			
	Commercial —Burglar Alarms		
	—Music Systems		
	—Data Processing		
	—Communication		
	Conduit Only—Contract Price		
	All Misc Electric		

Electrical permit fees may be computed
the same as building permit fees by
using the cost of installation for valuation
amount when such work is not included
in the above schedule

2310 2432

RECEIPT

I hereby certify that I have carefully examined and read the above application that the
same is true and correct and that the work herein described is to be done in accordance
with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and
the State Laws whether herein specified or not

SIGNED HOMEOWNER CONTRACTOR

PERMIT
FEE

6910

LESS
STARTER PERMITTOTAL
FEES

PERMIT NO

MUST BE MACHINE VALIDATED

Permit Expires 180 Days After Abandonment of Work

WATT NEVADA
DEVELOPMENT CORPORATION

Bob - Beeper

253-3533

MEMORANDUM

TO: All subcontractors, suppliers and Watt Nevada staff

FROM: Marc Stenzel 

DATE: October 15, 1990

SUBJECT: Las Colinas - Phase I - Addresses

<u>Lot</u>	<u>Block</u>	<u>Plan #</u>	<u>Elevation</u>	<u>Garage Hand</u>	<u>Address</u>
55	D	1	C	R	2124 Desert Pines Street
56	D	2	B	L	2128 Desert Pines Street
57	D	4	A	R	2132 Desert Pines Street
38	B	3	A	R	9429 Sierra Summit Avenue
39	B	4	A	R	9433 Sierra Summit Avenue
40	B	2	C	R	9437 Sierra Summit Avenue
41	C	4	B	R	9501 Sierra Summit Avenue
42	C	3	B	R	9505 Sierra Summit Avenue
43	C	1	C	R	9509 Sierra Summit Avenue
44	C	2	B	R	9513 Sierra Summit Avenue
45	C	3	C	R	9517 Sierra Summit Avenue
46	C	2	A	R	9521 Sierra Summit Avenue
47	C	4	C	R	9525 Sierra Summit Avenue
109	D	2	A	L	9428 Sierra Summit Avenue
110	D	1	B	L	9432 Sierra Summit Avenue
111	D	4	A	L	9436 Sierra Summit Avenue
112	D	2	B	L	9500 Sierra Summit Avenue
113	D	4	C	L	9504 Sierra Summit Avenue
114	D	3	A	L	9508 Sierra Summit Avenue
115	D	1	A	L	9512 Sierra Summit Avenue
116	D	4	B	L	9516 Sierra Summit Avenue
117	D	1	C	L	9520 Sierra Summit Avenue
118	D	3	B	L	9524 Sierra Summit Avenue



gale insulation of nevada, inc

5115 INDUSTRIAL ROAD SUITE 808
LAS VEGAS NEVADA 89118
(702) 739 6798



Installed Insulation Certificate

We certify insulation material listed herein meeting applicable federal state and local specifications has been installed at the following residence surrounding conditioned space

R FACTOR	AREA	TYPE	INCHES/BAGS (BLOWN)
R30	CEILING AREA	CELLULOSE BLOW	8 7"
R30	CEILING AREA	FIBERGLASS BATTS	9 1/2"
R13	EXTERIOR WALL	FIBERGLASS BATTS	3 5/8"

Certified by

Michael Brown

Title

OFFICE MANAGER

Address or Lot Number LAS COLINAS LOT 110 BLK D

Address or Lot Number 9432 SIERRA SUMMIT AVE

Date Installed

3-7-91

UltraKote, Inc.

FIBER - REINFORCED STUCCO

2865 N W Grand Avenue Phoenix, AZ 85017 (602) 484-0320 FAX (602) 278-2699

Job Address

INSTALLATION CARD

ICBO Report No 4658

9432 Sierra Sunset

Date of Job Completion 1/20

Plastering Contractor

Name

Nevada State Plastering

Address

2442 Loosle Rd

Telephone No

(702) 649 8822

Above contractor is approved by UltraKote, Inc

This is to certify that the exterior coating system on the building exterior at the above address has been installed in accordance with the evaluation report specified above and the manufacturer's instructions

Signature of authorized representative
of plastering contractor

Ken Hatt

Date

1/20

This installation card must be presented to the building inspector after completion of work and before final inspection

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

[illegible]

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit Ave		PERMIT NO 88944	
LOT NO	MAP NO 14-252P	INSPECTOR 84	DATE 1-18-91
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE B Ward			INSPECTION DATE 1-22-91
Complete Shear nailing + recall			
☐ PARTIAL INSPECTION DESCRIPTION			
☐ APPROVED		☐ PERMIT REQUIRED	☐ STOP WORK
☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING
☒ B 5	FRAMING rough	☒ P 5	TOP OUT WATER GAS WASTE
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING
☐ B 8	EXTERIOR LATH/STUCCO		
☐ B 9	WALL GROUT & STEEL	☒ M 1	ROUGH VENT
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL
☐ B 12	BUILDING FINAL		
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH
		☐ X 2	UNDERGROUND HYDRO
		☐ X 3	UNDERGROUND FINAL/FLOW
		☐ X 4	SPRINKLER SYSTEM HYDRO
		☐ X 5	FIRE ALARM
		☐ X 6	OTHER
		☐ X 7	FINAL FIRE
		☐ E 1	UNDERGROUND ELETRICAL
		☒ E 2	ROUGH ELECTRICAL
		☐ E 3	LOW VOLTAGE ELECTRICAL
		☐ E 4	SIGN INSPECTION
		☐ E 5	FINAL ELECTRICAL
		☐ E 6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C OF O ISSUANCE (Commercial Only)	

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit #8944		PERMIT NO 88944
LOT NO	MAP NO 9-2460	INSPECTOR Jef
SUBDIVISION NAME		DATE 1-22-91
INSPECTOR SIGNATURE RWand		PHONE
		INSPECTION DATE 1-23-91

- ① Tighten all nuts & bolts on HDS (missing nuts & bolts)
- ② Replace 2x's At hddowns where split -
- ③ Fire stop plate at chimney needs work -
- ④ " all chases into Floor or Attic spaces
- ⑤ F4 truss are end bearing - now in hanger? (see later)
- ⑥ Switch duct at upstairs - large duct feeding kitchen area, to restricted - will remove Nailers

Complete Above by Insul

☐ PARTIAL INSPECTION DESCRIPTION

☒ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☒ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☒ M 1	ROUGH VENT	☒ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit		PERMIT NO 88944
LOT NO	MAP NO 11-2:43P	INSPECTOR 84
SUBDIVISION NAME Las Colinas		DATE 1-30-91
INSPECTOR SIGNATURE RWard		PHONE
		INSPECTION DATE 1-31-91

- ① Repair Firestop At chimney - **(Wires At Fire stop)**
- ② Tighten ~~out~~ **out** on 4" duct corner - **OK**
- ③ ~~Plumb~~ **Plumb** at attic access - **OK**

This is 3RD Notice no Attempt to correct - wiring holding Firestop plate from sealing Hole = move All wiring off vent piping

30⁰⁰ Re Fee Req before Inspection will be done

☐ PARTIAL INSPECTION DESCRIPTION


☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL -- FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☒ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION
 BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C. of O ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 SIERRA SUMMIT		PERMIT NO 83944	
LOT NO	MAP NO	INSPECTOR 62	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE 			INSPECTION DATE 2-1-91
FIRE BUK AT 1ST FLOOR FIRE PLACE OK (CORRECTION MADE) #30th RE-INSPECTION FEE ATTACHED			
☐ PARTIAL INSPECTION DESCRIPTION			
☒ APPROVED		☐ PERMIT REQUIRED	
☐ REJECTED CORRECTION		☐ STOP WORK	
☐ NOTICE REINSPECTION REQUIRED CALL 799-2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE
☒ B 6	INSULATION	☐ P 6	FINAL GAS TEST
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING
☐ B 8	EXTERIOR LATH/STUCCO		
☐ B 9	WALL GROUT & STEEL	☐ E 1	UNDERGROUND ELETRICAL
☐ B 10	 PRE GUNITE	☐ E 2	ROUGH ELECTRICAL
☐ B 11	 PRE PLASTER / FINAL	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 12	BUILDING FINAL	☐ E 4	SIGN INSPECTION
☐ B 13	CERT OF OCC	☐ E 5	FINAL ELECTRICAL
		☐ X 1	KICKER / FLUSH
		☐ E 6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)	

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS <i>9432 Sierra Summit</i>		PERMIT NO <i>88944</i>	
LOT NO	MAILING NO <i>5-1020a</i>	INSPECTOR <i>84</i>	DATE <i>2-1-91</i>
SUBDIVISION NAME <i>1 plan</i>			PHONE
INSPECTOR SIGNATURE <i>B Ward</i>			INSPECTION DATE <i>2-4-91</i>

Complete drawll + recall
Nail top plates per shear req
Tighten up all nailing

☒ PARTIAL INSPECTION DESCRIPTION
lath only (exterior)

☐ APPROVED ☐ PERMIT REQUIRED ☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☒ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☒ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit		PERMIT NO. 88744
LOT NO.	MAP NO. 14-553p	INSPECTOR 84
DATE 2-4-91		PHONE
SUBDIVISION NAME Las Colinas		INSPECTION DATE 2-5-91
INSPECTOR SIGNATURE RW		

[illegible]☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL – FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☒ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

☐ PERMIT NUMBER		88944		☐ INSPECTION NUMBER	
JOB ADDRESS 9432 Sierra Summit Ave					
LOT NO		BLOCK NO		SUBDIVISION NAME	
FIRE DEPT MAP NO		JOB PHONE		CALL IN DATE 3 21 91	CALL IN TIME 5 10 27A
INSPECTOR NO 84		INSPECTOR NAME			
INSPECTION REQUESTED 140 - F/Bldg					
240 - F/mech ① Seal duct at wall 340 - F/Elect ② of kitchen 440 - F/Plum ② No gas cock at Range ③ Seal holes under Kit. sink ④ Dead bolts not working properly ⑤ Set water closets					
☐ PARTIAL INSPECTION		☐ PARTIAL APPROVAL (P)		PARTIAL DESCRIPTION	
☐ APPROVED (A)		☐ STOP WORK (S)		☐ COMMENTS (C)	
☒ REJECTED (R)		☐ TEMPORARY APPROVAL (T)		— UNTIL	
☐ REFEE (F)		☐ HOLD (H)			
☐ REINSPECTION REQUIRED		CALL 799 2071		☐ PERMIT REQUIRED	
☐ REINSPECTION FEE REQUIRED		PAY AT CITY HALL			
☐ 3RD FLOOR		400 E STEWART STREET			
INSPECTOR SIGNATURE AWH				INSPECTION DATE 3-22-91	
☐ PROJECT COMPLETE		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)			
IF YOU HAVE ANY QUESTIONS ON THIS INSPECTION YOU MAY CALL THE INSPECTOR FROM 7 00 A M 7 15 A M OR 2 45 P M 3 00 P M AT					

FOR ADDITIONAL ASSISTANCE CALL 386-6251
SEE REVERSE SIDE FOR INSPECTION TYPES

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit Ave			PERMIT NO 88944
LOT NO	MAP NO 4-1229P	INSPECTOR 84	DATE 3-19-91
SUBDIVISION NAME Las Calinas			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 3-20-91

- ① Tighten water bond clamps
- ② Breaker at panel - condenser RQ 45 amp
breaker not 50 amp
- ③ IF NOT CORRECTED next Insp - refer
RQ -

☒ PARTIAL INSPECTION DESCRIPTION

Temp power Tag # 22484

☐ APPROVED ☐ PERMIT REQUIRED ☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388 6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit Ave		PERMIT NO. 88944
LOT NO	MAP NO 5 2:47p	INSPECTOR SY
SUBDIVISION NAME Los Colinas		DATE 3/26/91
INSPECTOR SIGNATURE > R. Ward		PHONE
		INSPECTION DATE 3-27-91

all final

- ① Holes at Range hood duct not sealed
- ② Kit sink clean-out not accessible -
- ③ Front dead bolt not corrected
- ④ Holes under Kit-sink not sealed - same as h.w.'s
- ⑤ " at water heater stub-outs need to be sealed

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B 6	INSULATION	☒ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☒ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☒ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☒ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit Ave		PERMIT NO 88944	
LOT NO	MAP NO 8-226 P.	INSPECTOR 84	DATE 3-27-91
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE RWard			INSPECTION DATE 3-28-91

- ① Seal around Range hood duct
- ② " " water lines under sink
- ③ Cut swale at Front

Approved provide above done

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**
☐ **PERMIT REQUIRED**
☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☒ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	☒ POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	☒ POOL PRE PLASTER / FINAL	☒ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☒ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Spring Summit		PERMIT NO. 88944	
LOT NO.	MAP NO. D-228p	INSPECTOR 62	DATE 11-18-90
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 11/16-90

☐ PARTIAL INSPECTION DESCRIPTION

☒ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL -- FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☒ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☒ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit		PERMIT NO 88944
LOT NO	MAP NO 20 252P	INSPECTOR 84
SUBDIVISION NAME 1-B-L		DATE 1-10-91
INSPECTOR SIGNATURE RWand		PHONE
		INSPECTION DATE 1-11-91

~~Shad~~

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ PERMIT REQUIRED

☐ STOP WORK

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION		INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING		☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL – FORMS & REBAR		☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB		☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING		☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING		☐ P 5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B 6	INSULATION		☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING		☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO				☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL		☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	☐ POOL	PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	☐ POOL	PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL				☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC		☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS <i>9432 Sierra Summit Dr</i>		PERMIT NO. <i>88944</i>	
LOT NO.	MAP NO. <i>1 12.09P</i>	INSPECTOR <i>84</i>	DATE <i>3/15/91</i>
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i>			INSPECTION DATE <i>3-18-91</i>

gas & final meter

Electrical Incomplete

☒ PARTIAL INSPECTION DESCRIPTION
Tag (Gas) 14349 Gas Final only

☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☒ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	☒ POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	☒ POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 SICKRA Summit		PERMIT NO 99704
LOT NO	MAP NO	INSPECTOR 84
SUBDIVISION NAME		DATE
INSPECTOR SIGNATURE [Signature]		PHONE
		INSPECTION DATE 3-20-81

[illegible]☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ PERMIT REQUIRED☐ STOP WORK

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL – FORMS & REBAR	☒ P 2	ON SITE WATER <i>Termination</i>	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9432 Sierra Summit			PERMIT NO 88944
LOT NO	MAP NO 11 1:48	INSPECTOR CS	DATE 12-6-90
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 12-7-90

① HO2A'S REQUIRE WASHERS ON MACHINE BOLTS THEN WOOD

② HO2A MISSING BY STAIRS

③ HO2A BY ~~6~~ FRONT DOOR MISLOCATED

ROOF SHEATHING OK

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**
☐ **PERMIT REQUIRED**
☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☒ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X-6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**
BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251
