

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR INSPECTIONS CALL 799-2071

PERMIT NO

90-088960

BUILDING PERMIT

FOR Single Family Dwelling Remodel
Additions, Misc Residential ConstructionLOG NO & AREA T-205 DATE Oct 8, 90 CONST VAL \$ 58,000.00ADDRESS OF CONSTRUCTION 9524 Sierra Summit Ave OWNER Watt Nevada PHONE 369-2401LOT(s) 118 BLOCK D SUBDIVISION LAS COLINAS Summerlin Village #1 ZONE P/CPROPOSED CONSTRUCTION SFD with fireplace USE _____THIS PERMIT FOR BLDG ☒ A/C ☐ ELEC ☐ PLBG ☐ OTHER PERMITS REQD FENCE ☐ OFF SITE ☐ SWIM POOL ☐FLOOR AREA BSMT n/a 1ST 1058 2ND 931 GARAGE 380 PORCH 100 TOTAL 2469CONTRACTOR Watt Nevada Development STATE LICENSE NO 0030439 CITY LICENSE NO CU-03409-ARCHITECT Arlo Braun, A.I.A. ENGINEER J C Wallace 2-042316

MASTER PLUMBER/CONTRACTOR _____ MASTER ELECTRICIAN/CONTRACTOR _____

OTHER INSPECTIONS AND FEES

- 1 Inspections outside of normal business hours = \$30.00 per hour (minimum charge three hours)
- 2 Re inspection fee during normal business hours assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30.00 per hour
- 3 Inspections during normal business hours for which no fee is specifically indicated = \$30.00 per hour (minimum charge one half hour)
- 4 Additional plan review required by changes additions or revisions to approved plans = \$30.00 per hour (minimum charge two hours)

CONDITIONS OF THE PERMIT

- 1 I agree to call the City Building Department for inspections before concrete is poured before rough wiring electrical plumbing framing is covered Also for air conditioning drywall and sheathing inspection
- 2 I agree that when the job is completed that I will call for final inspection before occupancy
- 3 I agree to perform all construction in accordance with City Ordinances and Building Codes
- 4 The Contractor's signature below denotes authority from the owner to sign in his behalf and that the owner is aware of all requirements of this application and permit Separate permits must be taken out for work outlined above this agreement
- 5 I have read and understand the contents of this application and permit I hereby state that the information I have supplied on this application is true and correct
- 6 Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way
- 7 24 HOUR MINIMUM NOTICE REQUIRED FOR INSPECTIONS

BY Alvin Swartz 10-15-90
I HEREBY DECLARE THAT I AM THE LEGAL OWNER OF THE ABOVE PROPERTY OWNER

BY _____ AGENT

I hereby certify that I have reviewed this application and the proposed plans and have found that the proposed development meets the requirements of the City of Las Vegas Flood Hazard Reduction Ordinance for the issuance of this Development Permit

LAND DEVELOPMENT AND FLOOD CONTROL ENGINEER Kent Nash 10-12-90PLANNING DEPT Don Hooley 11/9/90BUILDING DEPT Don Hooley 10/9/90

SPECIAL CONDITIONS

Model #4-3

RECEIPT

PLUMBING		FEE	ELECTRICAL		FEE
WATER DISTRIBUTION	6.00		RECEPTACLE _____ SWITCH _____		40
SEWER SYSTEM NEW OR MODIFICATION	10.00		EACH LIGHT FIXTURE OR SOCKET _____		30
FIXTURES WATER SOFTENER H/W HEATER	2.00		SPECIAL OUTLET APPLIANCE ETC		70
GARBAGE DISPOSAL WASHER	2.00		SERVICE/PANEL SUB/3.00 200A/6.00 400A/12.50		
FUEL PIPING	6.00		A.C. UNIT OR MOTORS	3.00	
IRRIGATION SYSTEM	8.00		2310 2432	TOTAL	
MISC			MISC		
2310 2433	TOTAL		2310 2431 ISSUANCE FEE		
AIR CONDITIONING		FEE	7143 2973 SEWER CONNECTION		
NEW UNIT 3 TON = 9.00 OVER = 16.50			2310 2431 PLAN REVIEW FEE		
FURNACE TO 100 000/9.00 OVER/11.00			2310 2431 BLDG PERMIT FEE		
VAPORATIVE COOLER	6.50				
VENTILATION FAN	2.35				
2310 2435	TOTAL				

TOTAL FEES

625-

369-

994-

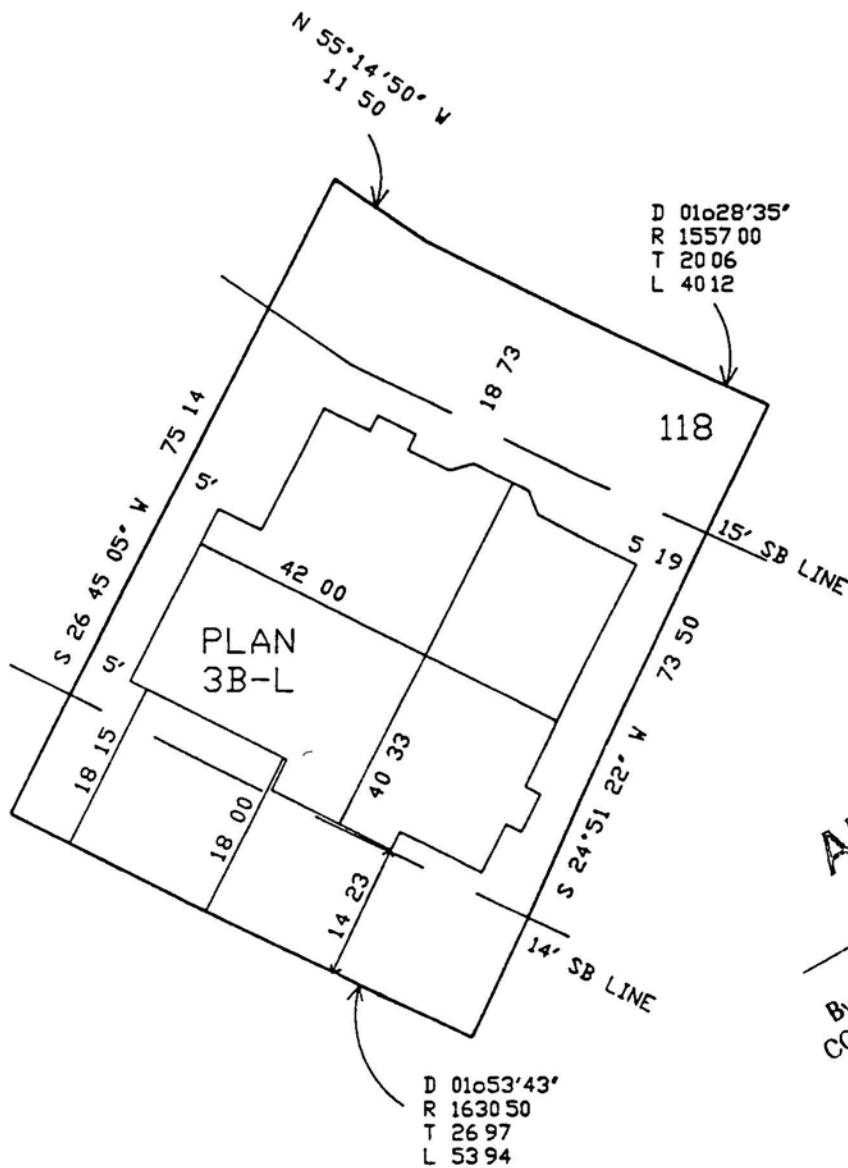
PERMIT NO _____
MUST BE MACHINE VALIDATED

Permit Expires 180 Days After Abandonment of Work

LAS COLINAS
FILE _____, PG. _____

LOT 118, BLK "D"

ADDRESS 9524 Sierra Summit Avenue



SCALE: 1" = 20'

APPROVED
SFD

By [Signature] 11/9/90
COMMUNITY PLANNING & DEVELOPMENT
City of Las Vegas

NOTE: 14' FRONT SB LINE
15' REAR SB LINE
5' SIDE SB LINE
15' SIDE SB LINE AT
CORNER LOTS

BRENNER & ASSOCIATES, INC.
LAND SURVEYORS

2915 W CHARLESTON BLVD., LAS VEGAS, NEV 89102 / (702) 877-0317

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-009584

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR INSPECTIONS CALL 799-2071

PLUMBING PERMIT

LOG NO & AREA P205 DATE 11/14/90 CONST VAL \$ _____ADDRESS OF CONSTRUCTION 9524 Sierra Summit Avenue OWNER Watt Nevada PHONE 642-9959CONTRACTOR Classic Plumbing, Inc STATE LICENSE NO 016762 CITY LICENSE NO C 11 H 09201797LOT(s) 118 BLOCK D SUBDIVISION Las Colinas ZONE _____PROPOSED CONSTRUCTION Complete plumbing for new single family home USE _____PLUMBING
PERMIT NO _____Approval for the work under this permit will be given only after refuse
and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10.00
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
11	Bathtub Shower Lavatory Toilet Urinal EA	2 00	22.00
1	Floor Drain Floor Sink Wash Tray Sink EA	2 00	2.00
1	Garbage Disposal Clothes Washer Dishwasher (residential) EA	2 00	2.00
	Garbage Disposal (commercial) EA	8 00	
	Clothes Washer Dishwasher (commercial) EA	2 00	
	Clothes Dryer (gas) (venting)	2 00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	2 00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
1	Hot Water Heater (Gas or Electric) EA	2 00	2.00
SEWER SYSTEM			
1	New Replacement Modification or Any Drainage Work	10 00	10.00
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
	Irrigation Single Family Dwelling	8 00	
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation _____		

UNITS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
1	Single Family Dwelling	6 00	6.00
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
	Medium Pressure System (Plan Check)	2 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Additional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation _____		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTION

RECEIPT

FIXTURES X

FEE _____

2310 2403

PERMIT
FEE 60.00TOTAL
FEES _____

PERMIT NO _____

MUST BE MACHINE VALIDATED

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

Diane M. Byington 59
SIGNED _____ CONTRACTOR _____ MASTER CARD NO _____

BY _____ Registered Master Plumber Spec Contractor or Owner

Diane Hoesly 11/14/90
BUILDING DEPT _____ DATE _____

CITY OF LAS VEGAS, NEVADA

PERMIT N90-090993

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR INSPECTIONS CALL 799-2071

AIR CONDITIONING PERMIT

LOG NO & AREA P205 DATE OCTOBER 16, 1990 CONST VAL \$ADDRESS OF CONSTRUCTION 9524 SIERRA SUMMIT AVENUE OWNER WATT NEVADA DEVELOPMENT PHONE 362-9878CONTRACTOR NEVCO AIR CONDITIONING & SHEET METAL STATE LICENSE NO 24377 CITY LICENSE NO C11023112033289LOT(S) 118 BLOCK D SUBDIVISION LAS COLINAS - SUMMERLIN ZONEPROPOSED CONSTRUCTION H.V.A.C. USE

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For the issuance of each permit	15 00	15 00
	For issuing each supplemental permit	4 50	
UNIT FEE SCHEDULE			
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance up to and including 100 000 Btu/h	9 00	
	For the installation or relocation of each forced air or gravity type furnace or burner including ducts and vents attached to such appliance over 100 000 Btu/h	11 00	
	For the installation or relocation of each floor furnace including vent	9 00	
	For the installation or relocation of each suspended heater recessed wall heater or floor mounted unit heater	9 00	
	For the installation relocation or replacement of each appliance vent installed and not included in an appliance permit	4 50	
	For the repair of alteration of or addition to each heating appliance refrigeration unit cooling unit absorption unit or each heating cooling absorption or evaporative cooling system including installation of controls regulated by this code	9 00	
	For the installation or relocation of each boiler or compressor to and including three tons or each absorption system to and including 100 000 Btu/h	9 00	
1	For the installation or relocation of each boiler or compressor over three tons to and including 15 tons or each absorption system over 100 000 Btu/h and including 500 000 Btu/h	16 50	16 50
	For the installation or relocation of each boiler or compressor over 15 tons to and including 30 tons or each absorption system over 500 000 Btu/h to and including 1 000 000 Btu/h	22 50	
	For the installation or relocation of each boiler or compressor over 30 tons to and including 50 tons or for each absorption system over 1 000 000 Btu/h to and including 1 750 000 Btu/h	33 50	
	For the installation or relocation of each boiler or refrigeration compressor over 50 tons or each absorption system over 1 750 000 Btu/h	56 00	

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
	For each air handling unit to and including 10 000 cubic feet per minute including ducts attached thereto Note This fee shall not apply to an air handling unit which is a portion of a factory assembled appliance cooling unit evaporative cooler or absorption unit for which a permit is required elsewhere in this code	6 50	
	For each air handling unit over 10 000 cfm	11 00	
	For each evaporative cooler other than portable type	6 50	
	For each ventilation fan	COMMERCIAL RESIDENTIAL	4 50 2 35
	For each ventilation system which is not a portion of any heating or air conditioning system authorized by a permit	6 50	
	For the installation of each hood which is served by mechanical exhaust including the ducts for such hood	6 50	
	For each fire damper installed in an existing system	4 50	
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge — three hours)	25 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$15 00 EACH	15 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — two hours)	30 00 per hour	
	Mechanical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Gas piping which is directly related and necessary to the repair or replacement of heating air conditioning or refrigeration systems not exceeding 500 000 BTUH	6 00	

2310-2435

RECEIPT

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED Julie Cellina CONTRACTOR MASTER CARD NOBY Wanda Hoesly Spec Contr or OwnerBUILDING DEPT 11/29/90 DATE

PERMIT FEE

TOTAL FEES

Permit Expires 180 Days After Abandonment of Work

MUST BE MACHINE VALIDATED

CITY OF LAS VEGAS, NEVADA

PERMIT NO

90-091374

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251

FOR INSPECTIONS CALL 799-2071

ELECTRICAL PERMIT

LOG NO & AREA P-205 DATE 11-28-90 CONST VAL \$ADDRESS OF CONSTRUCTION 9524 SIERRA SUMMIT Ave. OWNER WATT-NEVADA DEVELOPMENTCONTRACTOR HOLLAND & HOLLAND STATE LICENSE NO 021113 CITY LICENSE NO 021963(PRINT NAME OF MASTER ELECTRICIAN) BILL HOLLAND MASTER CARD NO 165 PHONE 362-6812PROPOSED CONSTRUCTION SINGLE FAMILY RES 118/D USE

ELECTRIC PERMIT NO

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10 -
	Supplemental Fee	4 50	
APPLIANCE CHARGE			
Residential or General Commercial			
82	Receptacle <u>54</u> Switch <u>28</u>	40	32.80
28	Each Light Fixture Socket or Exit Light Smoke Detector or Exhaust Fan	30	8.40
8	EACH OUTLET FOR SPECIAL PURPOSE Dishwasher Garbage Grinder Trash Compactor GFI Clothes Washer Dryer Electric Range Ovens Water Heater Space Heater Blast Coil Heater (PER KW) Mercury Lamp Quartz Lamp Sodium Lamp 20AMP Sign Circuit	70	560
	X Ray Unit	10 00	
	Area Lighting (First 3 000 Watts)	8 00	
	Each Additional 1 000 Watts	3 00	
MOTORS (1 H P AND OVER) TRANSFORMERS ELEVATORS WELDERS GENERATORS CHILLERS SIGNS AND A/C UNITS (OVER 5 TONS)			
	First H P or Ton For each Unit	3 00	
	First KVA For Each Unit	3 00	
	Each Additional H P Ton or KVA up to 50	50	
	Each Additional H P Ton or KVA over 50	35	
	Temporary power or Pole	6 00	
ELECTRIC SERVICE OR MAIN DISCONNECT			
1	Up to 200 AMP	6 00	6 -
	400 AMP And 600 AMP	12 50	
	Over 600 AMP To 1200 AMP	25 00	
	Over 1200 AMP	50 00	
	Each Additional Meter Socket	50	
	Sub Panel Motor Control Center Disconnect Switch Transfer Switch (Each)	3 00	
	Swimming Pool (Residential)	20 00	
	Swimming Pool (Semi Public)	30 00	
	Spas	8 00	
	Recreational Vehicle Spaces (Each)	3 00	

UNITS	DESCRIPTION	FEE	TOTAL
	Busways Trolley or Plug in (Ea 100 Ft)	3 00	
	Gas Pumps Dispensers (Each)	3 00	
1	Permanent A/C Unit (5 Tons or Less)	3 00	3 -
1	Each Air Handler	1 00	1 -
RESIDENTIAL LOW VOLTAGE INSTALLATIONS			
	Speaker Outlets (Each)	30	
	Signal or Alarm Outlets (Each)	30	
	Amplifiers	2 00	
	Control Panel	50	
	TV Master System	30	
	Telephone or Computer Outlet	30	
OTHER INSPECTIONS AND FEES INCLUDES ISSUANCE FEES WHEN APPLICABLE			
	Inspections outside of normal business hours (minimum charge — three hours)	30 00 per hour	
	Reinspection fee assessed under provisions of TABLE 3 A of the Uniform Building Code = \$30 00 EACH	30 00 each	
	Inspections for which no fee is specifically indicated (minimum charge — one half hour)	30 00 per hour	
	Additional plan review required by changes additions or revisions to approved plans (minimum charge — one half hour) After work hours — \$30 00 per hour — minimum 1 hour	30 00 per hour	
	Starter Permit	50 00	
CONTRACT PRICE OR COST OF INSTALLATION			
	Commercial —Burglar Alarms		
	—Music Systems		
	—Data Processing		
	—Communication		
	Conduit Only—Contract Price		
	All Misc Electric		

Electrical permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule

2310-2432

RECEIPT

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED HOMEOWNER CONTRACTOR

PERMIT FEE 666.80LESS
STARTER PERMITTOTAL
FEES

PERMIT NO

MUST BE MACHINE VALIDATED

BUILDING DEPT

DATE

Permit Expires 180 Days After Abandonment of Work

CITY OF LAS VEGAS, NEVADA

DEPARTMENT OF BUILDING AND SAFETY
PHONE 386-6251NO 91-099720
PLUMBING PERMITLOG NO & AREA P-205 DATE 3-5-91 CONST VAL \$ _____ADDRESS OF CONSTRUCTION 9524 Shennar Summit Ave OWNER Watt Nevada PHONE 369-2401CONTRACTOR R & R Landscaping STATE LICENSE NO 0030153 CITY LICENSE NO C11-02189-27
023628LOT(s) 118 BLOCK D SUBDIVISION Las Colinas ZONE _____PROPOSED CONSTRUCTION Irrigation USE _____

PLUMBING PERMIT NO _____

Approval for the work under this permit will be given only after refuse and debris have been removed from job site and public right of way

UNITS	DESCRIPTION	FEE	TOTAL
PERMIT ISSUANCE			
1	For Issuing Each Permit	10 00	10
	For Issuing Each Supplemental Permit	4 50	
FIXTURE CHARGE			
	Bathtub Shower Lavatory Toilet Urinal EA	2 00	
	Floor Drain Floor Sink Wash Tray Sink EA	2 00	
	Garbage Disposal Clothes Washer Dishwasher (residential) EA	2 00	
	Garbage Disposal (commercial) EA	8 00	
	Clothes Washer Dishwasher (commercial) EA	2 00	
	Clothes Dryer (gas) (venting)	2 00	
	Dental Unit	8 00	
	Drinking Fountain	2 00	
	Refrigerator Ice Maker Water Dispenser	2 00	
	Any other water using equipment Attached Coffee Makers Ice Makers	2 00	
	Hot Water Heater (Gas or Electric) EA	2 00	
SEWER SYSTEM			
	New Replacement Modification or Any Drainage Work	10 00	
	Grease or Sand Trap or Interceptor	2 00	
	Trailer Trap (rental parks)	5 00	
WATER SOFTENERS			
	Non Permanent Type (rental)	2 00	
	Permanent Type (connected to drain)	2 00	
WATER DISTRIBUTION SYSTEM			
	Single Family Dwelling	6 00	
	Multi Family Dwelling	6 00	
	Plus Each Dwelling Unit	3 00	
	Commercial Building per floor	3 00	
	Plus Each Unit (leased space or office)	2 00	
	Hotel or Motel	8 00	
	Plus Each Unit	3 00	
	Trailer Park	30 00	
	Plus Each Space	2 00	
1	Irrigation Single Family Dwelling	8 00	8
	Irrigation Commercial Fee Based on Building Code Valuation Chart Construction Valuation _____		

UNITS	DESCRIPTION	FEE	TOTAL
FUEL PIPING SYSTEM			
	Single Family Dwelling	6 00	
	Multi Family Dwelling	10 00	
	Plus Each Unit	2 00	
	Commercial Building (per floor)	6 00	
	Plus Each Unit (leased space or office)	6 00	
	Medium Pressure System (Plan Check)	2 00	
	Each Gas Appliance (Any Type)	2 00	
	Steam Boilers	5 00	
SOLAR ENERGY SYSTEMS			
	Collectors (including piping) (per collector)	5 00	
	Storage Tanks (each)	5 00	
PIPELINE CONTRACT			
	For Onsite Sewer Gas or Water Contract Value Fee based on Building Code Permit Valuation Chart		
OTHER INSPECTIONS AND FEES			
	Inspections outside of normal business hours (minimum charge—three hours)	25 00 per hour	
	Under provisions of Table 3 A of the Uniform Building Code work which has been inspected once and not approved may be subject to a Reinspection Fee not less than \$30 00 per each inspection during business hours	30 00 each	
	Additional plan review required by changes Additions to or revisions to approved plans (minimum charge two hours)	30 00 per hour	
	Plumbing permit fees may be computed the same as building permit fees by using the cost of installation for valuation amount when such work is not included in the above schedule		
	Construction Valuation _____		

FOR INSPECTIONS
CALL 799-2071SEWER # 7114 3654
CONNECTION

RECEIPT

FIXTURES _____ X _____

FEE _____

2310 2403

PERMIT
FEE 18.00TOTAL
FEES _____

PERMIT NO _____

I hereby certify that I have carefully examined and read the above application that the same is true and correct and that the work herein described is to be done in accordance with all the provisions of the applicable Ordinances of the City of Las Vegas Nevada and the State Laws whether herein specified or not

SIGNED

CONTRACTOR

MASTER CARD NO

BY

Registered Master Plumber Spec Contractor or Owner

BUILDING DEPT

DATE

3/63

MUST BE MACHINE VALIDATED

PERMIT EXPIRES 180 DAYS AFTER ABANDONMENT OF WORK



gale insulation of nevada, inc.

5115 INDUSTRIAL ROAD SUITE 808
LAS VEGAS NEVADA 89118
(702) 739 6798



Installed Insulation Certificate

We certify insulation material listed herein meeting applicable federal state and local specifications has been installed at the following residence surrounding conditioned space

R FACTOR	AREA	TYPE	INCHES/BAGS (BLOWN)
R30	CEILING AREA	FIBERGLASS BATTS	9 1/2"
R30	CEILING AREA	CELLULOSE BLOW	8 7"
R13	EXTERIOR WALL	FIBERGLASS BATTS	3 5/8"

Certified by

Michele Arano

Title

OFFICE MANAGER

LAS COLINAS LOT 117 BK D

Address or Lot Number

9520 SIERRA SUMMIT

Date Installed

3 7 91

UltraKote 1

FIBER - REINFORCED STUCCO

INSTALLATION CARD

#88961(54)

Job Site Location

9525 Serra Summit

ICBO Report No 4658 (issued 8/28/89)

Job Completion Date 1/28

Contractor

Business Name

Nevada State Plastering

Address

CITY

2442 Lowe Rd

STATE

ZIP

Telephone ()

649 8822

UltraKote Assigned License Number

A-247

State Contractor License Number

This is to certify that UltraKote 1 and the lath system has been installed in accordance with the evaluation report No 4685 and the UltraKote 1, Inc instructions

Signature of authorized representatives of plastering contractor

Nevada State Plastering

Date

1/28

Installation card must be presented to the building inspector after completion of work and before final inspection

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS <i># 9524 King Summit 88960</i>		PERMIT NO. <i>88960</i>	
LOT NO.	MAP NO. <i>B-228p</i>	INSPECTOR <i>62</i>	DATE <i>11-18-90</i>
SUBDIVISION NAME <i>Los Colinas</i>			PHONE
INSPECTOR SIGNATURE <i>Jm Bara</i>			INSPECTION DATE <i>11-16-90</i>

☐ PARTIAL INSPECTION DESCRIPTION

☒ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☒ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☒ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☒ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit		PERMIT NO 88960
LOT NO	MAP NO 8-235P	INSPECTOR 62
SUBDIVISION NAME Las Colinas		DATE 11-16-90
INSPECTOR SIGNATURE S Van Patton		INSPECTION DATE 11-18-90
Post Tension		AM

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED** ☐ **PERMIT REQUIRED** ☐ **STOP WORK**

☐ REJECTED ☐ CORRECTION NOTICE ☐ REINSPECTION REQUIRED CALL 799 2071




INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☒ B 2	STEM WALL – FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☒ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit		PERMIT NO 88960
LOT NO	MAP NO 1/48	INSPECTOR 62
SUBDIVISION NAME Las Colinas		DATE 12-6-90
INSPECTOR SIGNATURE 		PHONE
		INSPECTION DATE 12-7-90
 		

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071.**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☒ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☒ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	 PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	 PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit		PERMIT NO. 88960	
LOT NO.	MAP NO. 7-2500	INSPECTOR 62	DATE 1-3-91
SUBDIVISION NAME Las Vegas			PHONE
INSPECTOR SIGNATURE Am. Baker			INSPECTION DATE 1-4-99

- ① 1" CLEAR FROM WOOD
ON H.W. VENT
- ② STRAP GAS LINE AT F.P.
- ③ SEAL OUTSIDE PLATES (FLOOR)
- ④ ~~CHANGE OUTLET IN KIT TO~~
~~KICKER & OUTLETS ON CIRCUIT~~
- ⑤ FIRE BULK FIRE PLATE 3/4" PLY OR
5/8" D.W.
- ⑥ FIRE STOP TOP PLATES

OK TO LOAD ROOF

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 793-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☒ B 5	FRAMING	☒ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☒ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☒ M 1	ROUGH VENT	☒ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 383-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit Ave			PERMIT NO 88960
LOT NO	MAP NO 2 - 1:07P	INSPECTOR 62 84	DATE 1-7-91
SUBDIVISION NAME Las Cienas - 3 plan			PHONE
INSPECTOR SIGNATURE R. Wood			INSPECTION DATE 1-9-91

P.M. - Did not give inspection type

① 3 way at rear door on plans not installed - (Room ? to install)

② - RELESED CANS TO BE I.C. RATED -

③ - LIGHTS OVER TUBS & SHOWERS TO BE G.F.E. PROTECTED -

④ Truss top - cord bearing - notched at east side above window - Get engineering approval

⑤ Provide letter - to match as built truss & wall above master bath - Engineering -

⑥ Rat pack all exterior wall

Approved pending Above done by Insulation

☐ PARTIAL INSPECTION - DESCRIPTION

Plb + Meck select - OK

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 793-2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☒ B 5	FRAMING	☒ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☒ M 1	ROUGH VENT	☒ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit		PERMIT NO 88960	
LOT NO	MAP NO	INSPECTOR 84	DATE
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE Rwand			INSPECTION DATE 1-10-91

⑦ Fire stop pop-outs at Front entry - ceiling line

⑧ " top plate at water heater vent

⑨ Verify HVAC units are Dry night as per plan

⑩ Install HDSAs top & Bottom per plan

☐ PARTIAL INSPECTION DESCRIPTION

☒ APPROVED
☐ PERMIT REQUIRED
☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☒ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS <i>9514 Sierra Summit</i>		PERMIT NO. <i>88960</i>	
LOT NO <i>118</i>	MAP NO <i>13-250p</i>	INSPECTOR <i>84</i>	DATE <i>1-23-91</i>
SUBDIVISION NAME <i>Los Colinas</i>			PHONE
INSPECTOR SIGNATURE <i>R Ward</i>			INSPECTION DATE <i>1-24-91</i>

- ① BIK trusses
- ② Get letter showing AS built
- ③ Firestop water heater vent
- ④ Insul to be 6' from all corner of unit
- ⑤ Attic access - At master bath closet
- ⑥ Tighten up Insulation behind tubs, walls corners ect.

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED
 ☐ PERMIT REQUIRED
 ☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☒ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit		PERMIT NO 88960	
LOT NO	MAP NO 7-2:31P	INSPECTOR 84	DATE 1-28-91
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i>			INSPECTION DATE 1-29-91
<i>Closet + bath at bedroom #2 not nailed -</i> <i>Drywall rejected</i>			
☒ PARTIAL INSPECTION - DESCRIPTION <i>Exterior Lath OK</i>			
☐ APPROVED		☐ PERMIT REQUIRED	
☐ STOP WORK			
☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST
☒ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING
☒ B 8	EXTERIOR LATH/STUCCO		
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL
☐ B 12	BUILDING FINAL		
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH
		☐ X 2	UNDERGROUND HYDRO
		☐ X 3	UNDERGROUND FINAL/FLOW
		☐ X 4	SPRINKLER SYSTEM HYDRO
		☐ X 5	FIRE ALARM
		☐ X 6	OTHER
		☐ X 7	FINAL FIRE
		☐ E 1	UNDERGROUND ELECTRICAL
		☐ E 2	ROUGH ELECTRICAL
		☐ E 3	LOW VOLTAGE ELECTRICAL
		☐ E 4	SIGN INSPECTION
		☐ E 5	FINAL ELECTRICAL
		☐ E 6	TEMP POWER
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C OF O ISSUANCE (Commercial Only)	

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 24 9512 Sierra Summit Ave		PERMIT NO 60 88954	
LOT NO	MAP NO 8-2:42P	INSPECTOR 84	DATE 1-24-91
SUBDIVISION NAME Las Colinas			PHONE
INSPECTOR SIGNATURE Reward			INSPECTION DATE 1-25-91

A.M.

Approved pending better match's truss above master bath wall - as built

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**
☐ **PERMIT REQUIRED**
☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 798-2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☒ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit Ave		PERMIT NO 88960	
LOT NO	MAP NO 12-248P	INSPECTOR 84	DATE 1-29-91
SUBDIVISION NAME Las Colinas			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 1-30-91

- OK to rock provided latter match's construction & Hanger's Installer AT close + (will check 1-31-91)

☐ PARTIAL INSPECTION - DESCRIPTION

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit			PERMIT NO 88960
LOT NO 118	MAP NO	INSPECTOR 84	DATE
SUBDIVISION NAME Los Colinas - Watt Homes, NV			PHONE
INSPECTOR SIGNATURE <i>[Signature]</i>			INSPECTION DATE 2-5-91

Corrections made - As built to
letter from Engineer of Feb 1, 1991
in file onsite (letter stamped by Eng)

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**
☐ **PERMIT REQUIRED**
☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 7324 <i>Sierra Summit Dr</i>	PERMIT NO 889000
LOT NO 9250P	MAP NO 84
INSPECTOR 84	DATE 3/4/91
SUBDIVISION 9250P	PHONE 3-5-91

**INSPECTOR
SIGNATURE**

P Ward

INSPECTION DATE

3-5-91

Am final meter & gasoline

*GT # 14337
Elect # 22467*

- ① Wire nut off at stair lights
- ② Complete touch at Kit counter recept

☐ PARTIAL INSPECTION DESCRIPTION

☒ **APPROVED**

☐ **PERMIT REQUIRED**

☐ **STOP WORK**

☐ **REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071**

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL -- FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☐ P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	☐ POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	☐ POOL PRE PLASTER / FINAL	☐ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☐ B 12	BUILDING FINAL			☐ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ **FINAL
INSPECTION**

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 368-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit Ave.		PERMIT NO. 88960 88954	
LOT NO	MAP NO	INSPECTOR 4 2:40p 5784	DATE 3/11/91
SUBDIVISION NAME Los Colinas			PHONE
INSPECTOR SIGNATURE [Signature]			INSPECTION DATE 3/12/91

Ref
complete insp. card dated 3/5/91

☐ PARTIAL INSPECTION DESCRIPTION

☐ APPROVED

☐ PERMIT REQUIRED

☐ STOP WORK

☒ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL — FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	☒ B 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELECTRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	☒ M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
☒ B 12	BUILDING FINAL			☒ E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☐ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
 SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 388-8251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit Av		PERMIT NO 88960	
LOT NO	MAP NO 6 2:54P	INSPECTOR 84	DATE 3/6/91
SUBDIVISION NAME			PHONE
INSPECTOR SIGNATURE RWand			INSPECTION DATE 3-8-91
all building finals (am)			
① Complete grade at rear - clean up + lot swales			
② Remove Flex at hood + install hard duct			
③ Complete condenser pad			
☒ PARTIAL INSPECTION DESCRIPTION 30 Day Temp Final (Int.) 3-8-91			
☐ APPROVED		☐ PERMIT REQUIRED	
☐ STOP WORK			
☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071			
INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER
☐ B 2	STEM WALL - FORMS & REBAR	☐ P 2	ON SITE WATER
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST
☐ B 7	DRYWALL NAILING	☒ P 7	FINAL PLUMBING
☐ B 8	EXTERIOR LATH/STUCCO		
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD
☐ B 11	POOL PRE PLASTER / FINAL	☒ M 3	FINAL MECHANICAL
☒ B 12	BUILDING FINAL		
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH
☐ FINAL INSPECTION		BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS SIGNED OFF TO BLDG & SAFETY FOR C OF O ISSUANCE (Commercial Only)	

FOR ASSISTANCE CALL 388-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

JOB ADDRESS 9524 Sierra Summit Ave.		PERMIT NO 88960
LOT NO	MAP NO 10 1.30p	INSPECTOR 84
SUBDIVISION NAME Los Colinas		DATE 3/14/91
INSPECTOR SIGNATURE R Ward		PHONE 3-15-91

☐ PARTIAL INSPECTION - DESCRIPTION☒ APPROVED☐ PERMIT REQUIRED

☐ STOP WORK

☐ REJECTED CORRECTION NOTICE REINSPECTION REQUIRED CALL 799 2071

INSPECT	DESCRIPTION	INSPECT	DESCRIPTION	INSPECT	DESCRIPTION
☐ B 1	FOOTING LAYOUT REBAR ZONING	☐ P 1	ON SITE SEWER	☐ X 2	UNDERGROUND HYDRO
☐ B 2	STEM WALL – FORMS & REBAR	☐ P 2	ON SITE WATER	☐ X 3	UNDERGROUND FINAL/FLOW
☐ B 3	PRE SLAB	☐ P 3	BUILDING SEWER (YARD LINES)	☐ X 4	SPRINKLER SYSTEM HYDRO
☐ B 4	ROOF SHEATHING	☐ P 4	UNDERSLAB PLUMBING	☐ X 5	FIRE ALARM
☐ B 5	FRAMING	☐ P 5	TOP OUT WATER GAS WASTE	☐ X 6	OTHER
☐ B 6	INSULATION	☐ P 6	FINAL GAS TEST	☐ X 7	FINAL FIRE
☐ B 7	DRYWALL NAILING	X P 7	FINAL PLUMBING		
☐ B 8	EXTERIOR LATH/STUCCO			☐ E 1	UNDERGROUND ELETRICAL
☐ B 9	WALL GROUT & STEEL	☐ M 1	ROUGH VENT	☐ E 2	ROUGH ELECTRICAL
☐ B 10	POOL PRE GUNITE	☐ M 2	HOOD	☐ E 3	LOW VOLTAGE ELECTRICAL
☐ B 11	POOL PRE PLASTER / FINAL	X M 3	FINAL MECHANICAL	☐ E 4	SIGN INSPECTION
X B 12	BUILDING FINAL			X E 5	FINAL ELECTRICAL
☐ B 13	CERT OF OCC	☐ X 1	KICKER / FLUSH	☐ E 6	TEMP POWER

☒ FINAL INSPECTION

BRING HARD CARD WITH FIRE QUALITY CONTROL & PLANNING APPROVALS
SIGNED OFF TO BLDG & SAFETY FOR C of O ISSUANCE (Commercial Only)

FOR ASSISTANCE CALL 386-6251

DEPARTMENT OF BUILDING & SAFETY CITY OF LAS VEGAS

[illegible]

FOR ASSISTANCE CALL 386-6251
