


JOB NO. 620.222

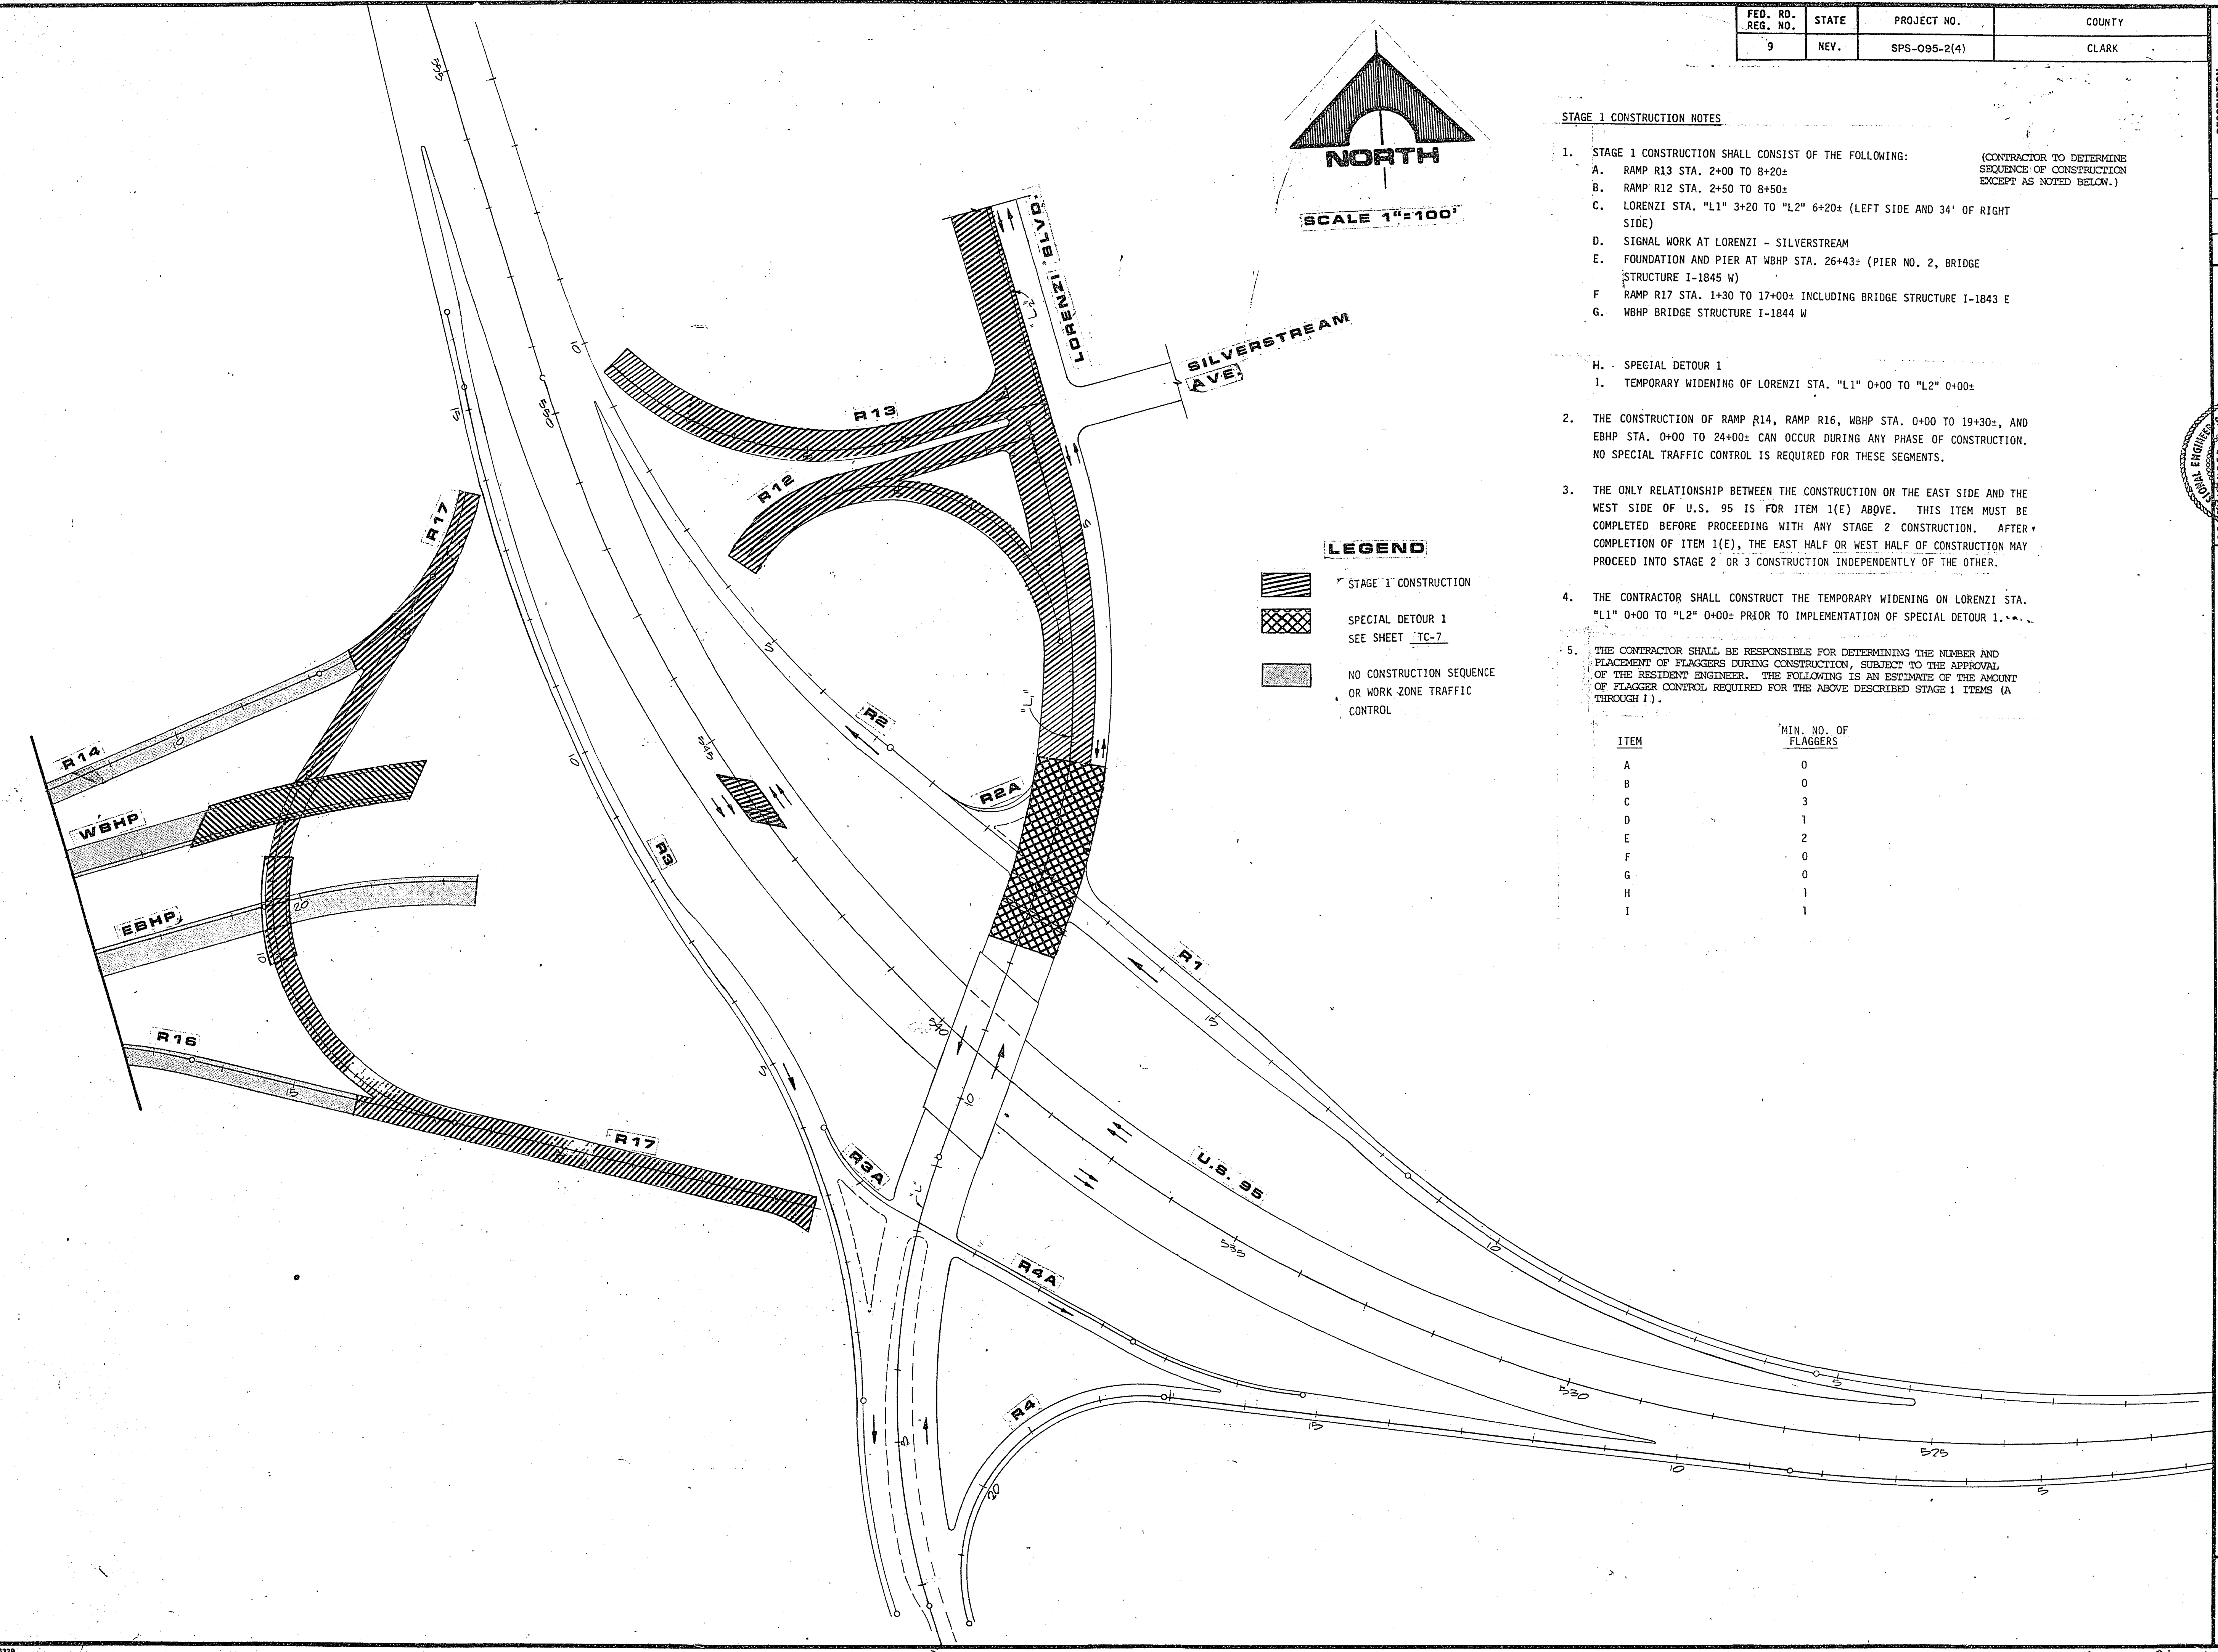

LEGEND

- [Hatched Box] STAGE 1 CONSTRUCTION
- [Cross-hatched Box] SPECIAL DETOUR 1
SEE SHEET TC-7
- [Solid Grey Box] NO CONSTRUCTION SEQUENCE
OR WORK ZONE TRAFFIC
CONTROL

FED. RD. REG. NO.	STATE	PROJECT NO.	COUNTY
9	NEV.	SPS-095-2(4)	CLARK


STAGE 1 CONSTRUCTION NOTES

- STAGE 1 CONSTRUCTION SHALL CONSIST OF THE FOLLOWING:
A. RAMP R13 STA. 2+00 TO 8+20±
B. RAMP R12 STA. 2+50 TO 8+50±
C. LORENZI STA. "L1" 3+20 TO "L2" 6+20± (LEFT SIDE AND 34' OF RIGHT SIDE)
D. SIGNAL WORK AT LORENZI - SILVERSTREAM
E. FOUNDATION AND PIER AT WBHP STA. 26+43± (PIER NO. 2, BRIDGE STRUCTURE I-1845 W)
F. RAMP R17 STA. 1+30 TO 17+00± INCLUDING BRIDGE STRUCTURE I-1843 E
G. WBHP BRIDGE STRUCTURE I-1844 W

(CONTRACTOR TO DETERMINE SEQUENCE OF CONSTRUCTION EXCEPT AS NOTED BELOW.)

- SPECIAL DETOUR 1
1. TEMPORARY WIDENING OF LORENZI STA. "L1" 0+00 TO "L2" 0+00±
- THE CONSTRUCTION OF RAMP R14, RAMP R16, WBHP STA. 0+00 TO 19+30±, AND EBHP STA. 0+00 TO 24+00± CAN OCCUR DURING ANY PHASE OF CONSTRUCTION. NO SPECIAL TRAFFIC CONTROL IS REQUIRED FOR THESE SEGMENTS.
- THE ONLY RELATIONSHIP BETWEEN THE CONSTRUCTION ON THE EAST SIDE AND THE WEST SIDE OF U.S. 95 IS FOR ITEM 1(E) ABOVE. THIS ITEM MUST BE COMPLETED BEFORE PROCEEDING WITH ANY STAGE 2 CONSTRUCTION. AFTER COMPLETION OF ITEM 1(E), THE EAST HALF OR WEST HALF OF CONSTRUCTION MAY PROCEED INTO STAGE 2 OR 3 CONSTRUCTION INDEPENDENTLY OF THE OTHER.
- THE CONTRACTOR SHALL CONSTRUCT THE TEMPORARY WIDENING ON LORENZI STA. "L1" 0+00 TO "L2" 0+00± PRIOR TO IMPLEMENTATION OF SPECIAL DETOUR 1.
- THE CONTRACTOR SHALL BE RESPONSIBLE FOR DETERMINING THE NUMBER AND PLACEMENT OF FLAGGERS DURING CONSTRUCTION, SUBJECT TO THE APPROVAL OF THE RESIDENT ENGINEER. THE FOLLOWING IS AN ESTIMATE OF THE AMOUNT OF FLAGGER CONTROL REQUIRED FOR THE ABOVE DESCRIBED STAGE 1 ITEMS (A THROUGH I).

ITEM	MIN. NO. OF FLAGGERS
A	0
B	0
C	3
D	1
E	2
F	0
G	0
H	1
I	1

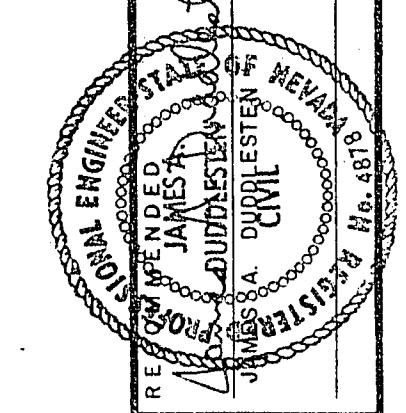

G.C. WALLACE, INC.
Engineering/Architecture
1555 SOUTH RAINBOW BLVD., LAS VEGAS, NEVADA 89102

HOWARD HUGHES PROPERTIES
HUSITE PARKWAY INTERCHANGE
TRAFFIC CONTROL PLAN
STAGE 1

26-3-81 107-07652
