



Department of Parks & Recreation

Park & Facility Construction Update September 2018

❖ **Bill Briare Family Park**

- Completed

❖ **Bob Baskin Park**

- Completed

❖ **Rafael Rivera Soccer Fields**


- Existing soccer field
- LED sports lighting will be installed
- Bid in 4th quarter of 2018
- Estimated completion late 2019

❖ **Lieburn Senior Center**

- New room addition
- In construction
- Estimated completion end of November 2018

❖ **Doolittle Community Center**

- Adding 3 pre-school classrooms
- In design
- Timeline: Bid Dec. 2018 – NTP March 2019 – Completion Sept/Oct 2019

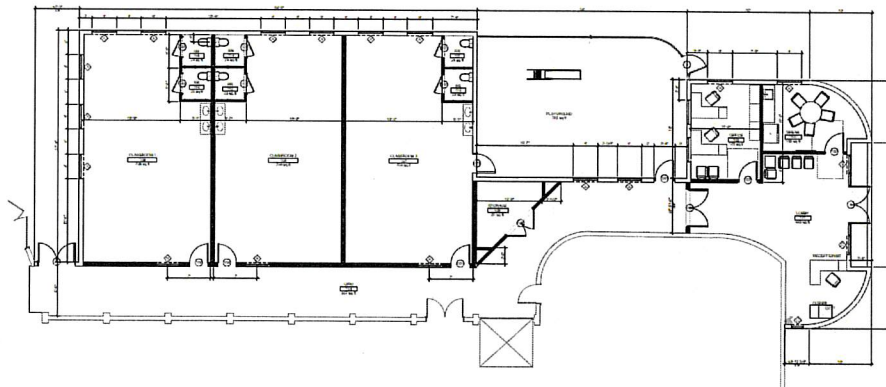

❖ Skye Canyon

- Allyn Beck Memorial Park – 2 soccer fields – natural turf
- In design
- Timeline: too early to determine



❖ Teton Trails

- Installing 3rd soccer field with lights
- In design
- Timeline: too early to determine

❖ Las Vegas Senior Center

- Two Phases - New HVAC and ADA/Front desk improvements
- In construction – HVAC
- HVAC complete Oct/Nov 2018
- ADA improvements will start 2nd quarter 2019
- Estimated ADA Completion: too early to determine


❖ Las Vegas Wash Park

- Artificial Turf Soccer Field, basketball court, picnic pavilions, great playground units
- Bid in 4th quarter of 2018
- Estimated completion early 2020



❖ Baker Park and Pool

- Existing park and pool with major improvements
- Artificial turf soccer fields, water play area, new restrooms, soccer theme
- Projected to start 4th quarter of 2018
- Estimated completion 2019/2020

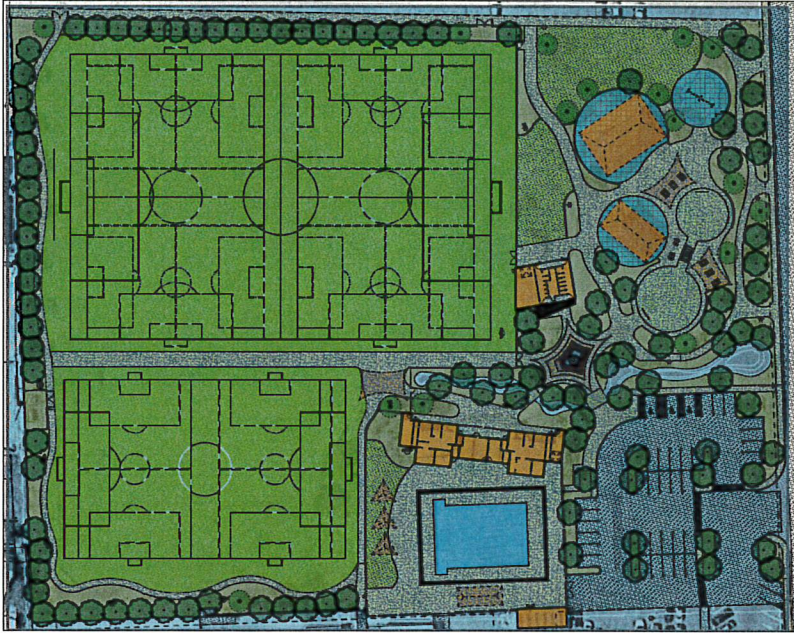

❖ Gilmore Cliff Shadows

- New park – terrain at this location allowed for unique design
- Walking path, great playground units, Movie In The Park stations
- Projected to start in 1st quarter of 2019
- Estimated completion 2020



❖ **Harris Marion Park**

- New park
- Small soccer fields with an equestrian elements
- In design
- Estimated completion 2019/2020

❖ **Woofter Park**

- Existing park with dog areas
- Redesign Dog Areas
- Bid in 4th quarter of 2018
- Estimated completion late 2019/early 2020

❖ **Charleston Heights Park**

- Possible community center and park improvements
- Community Workshop in February 2019
- Timeline: too early to determine

❖ **Cimarron Rose**

- Room addition
- Addition will have two classrooms - AA is 15 additional parking stalls
- In design
- Timeline: too early to determine
