



JOB NO. 520.222

FED. RD. REG. NO.	STATE	PROJECT NO.	COUNTY
9	NEV.	SPS-095-2(4)	CLARK

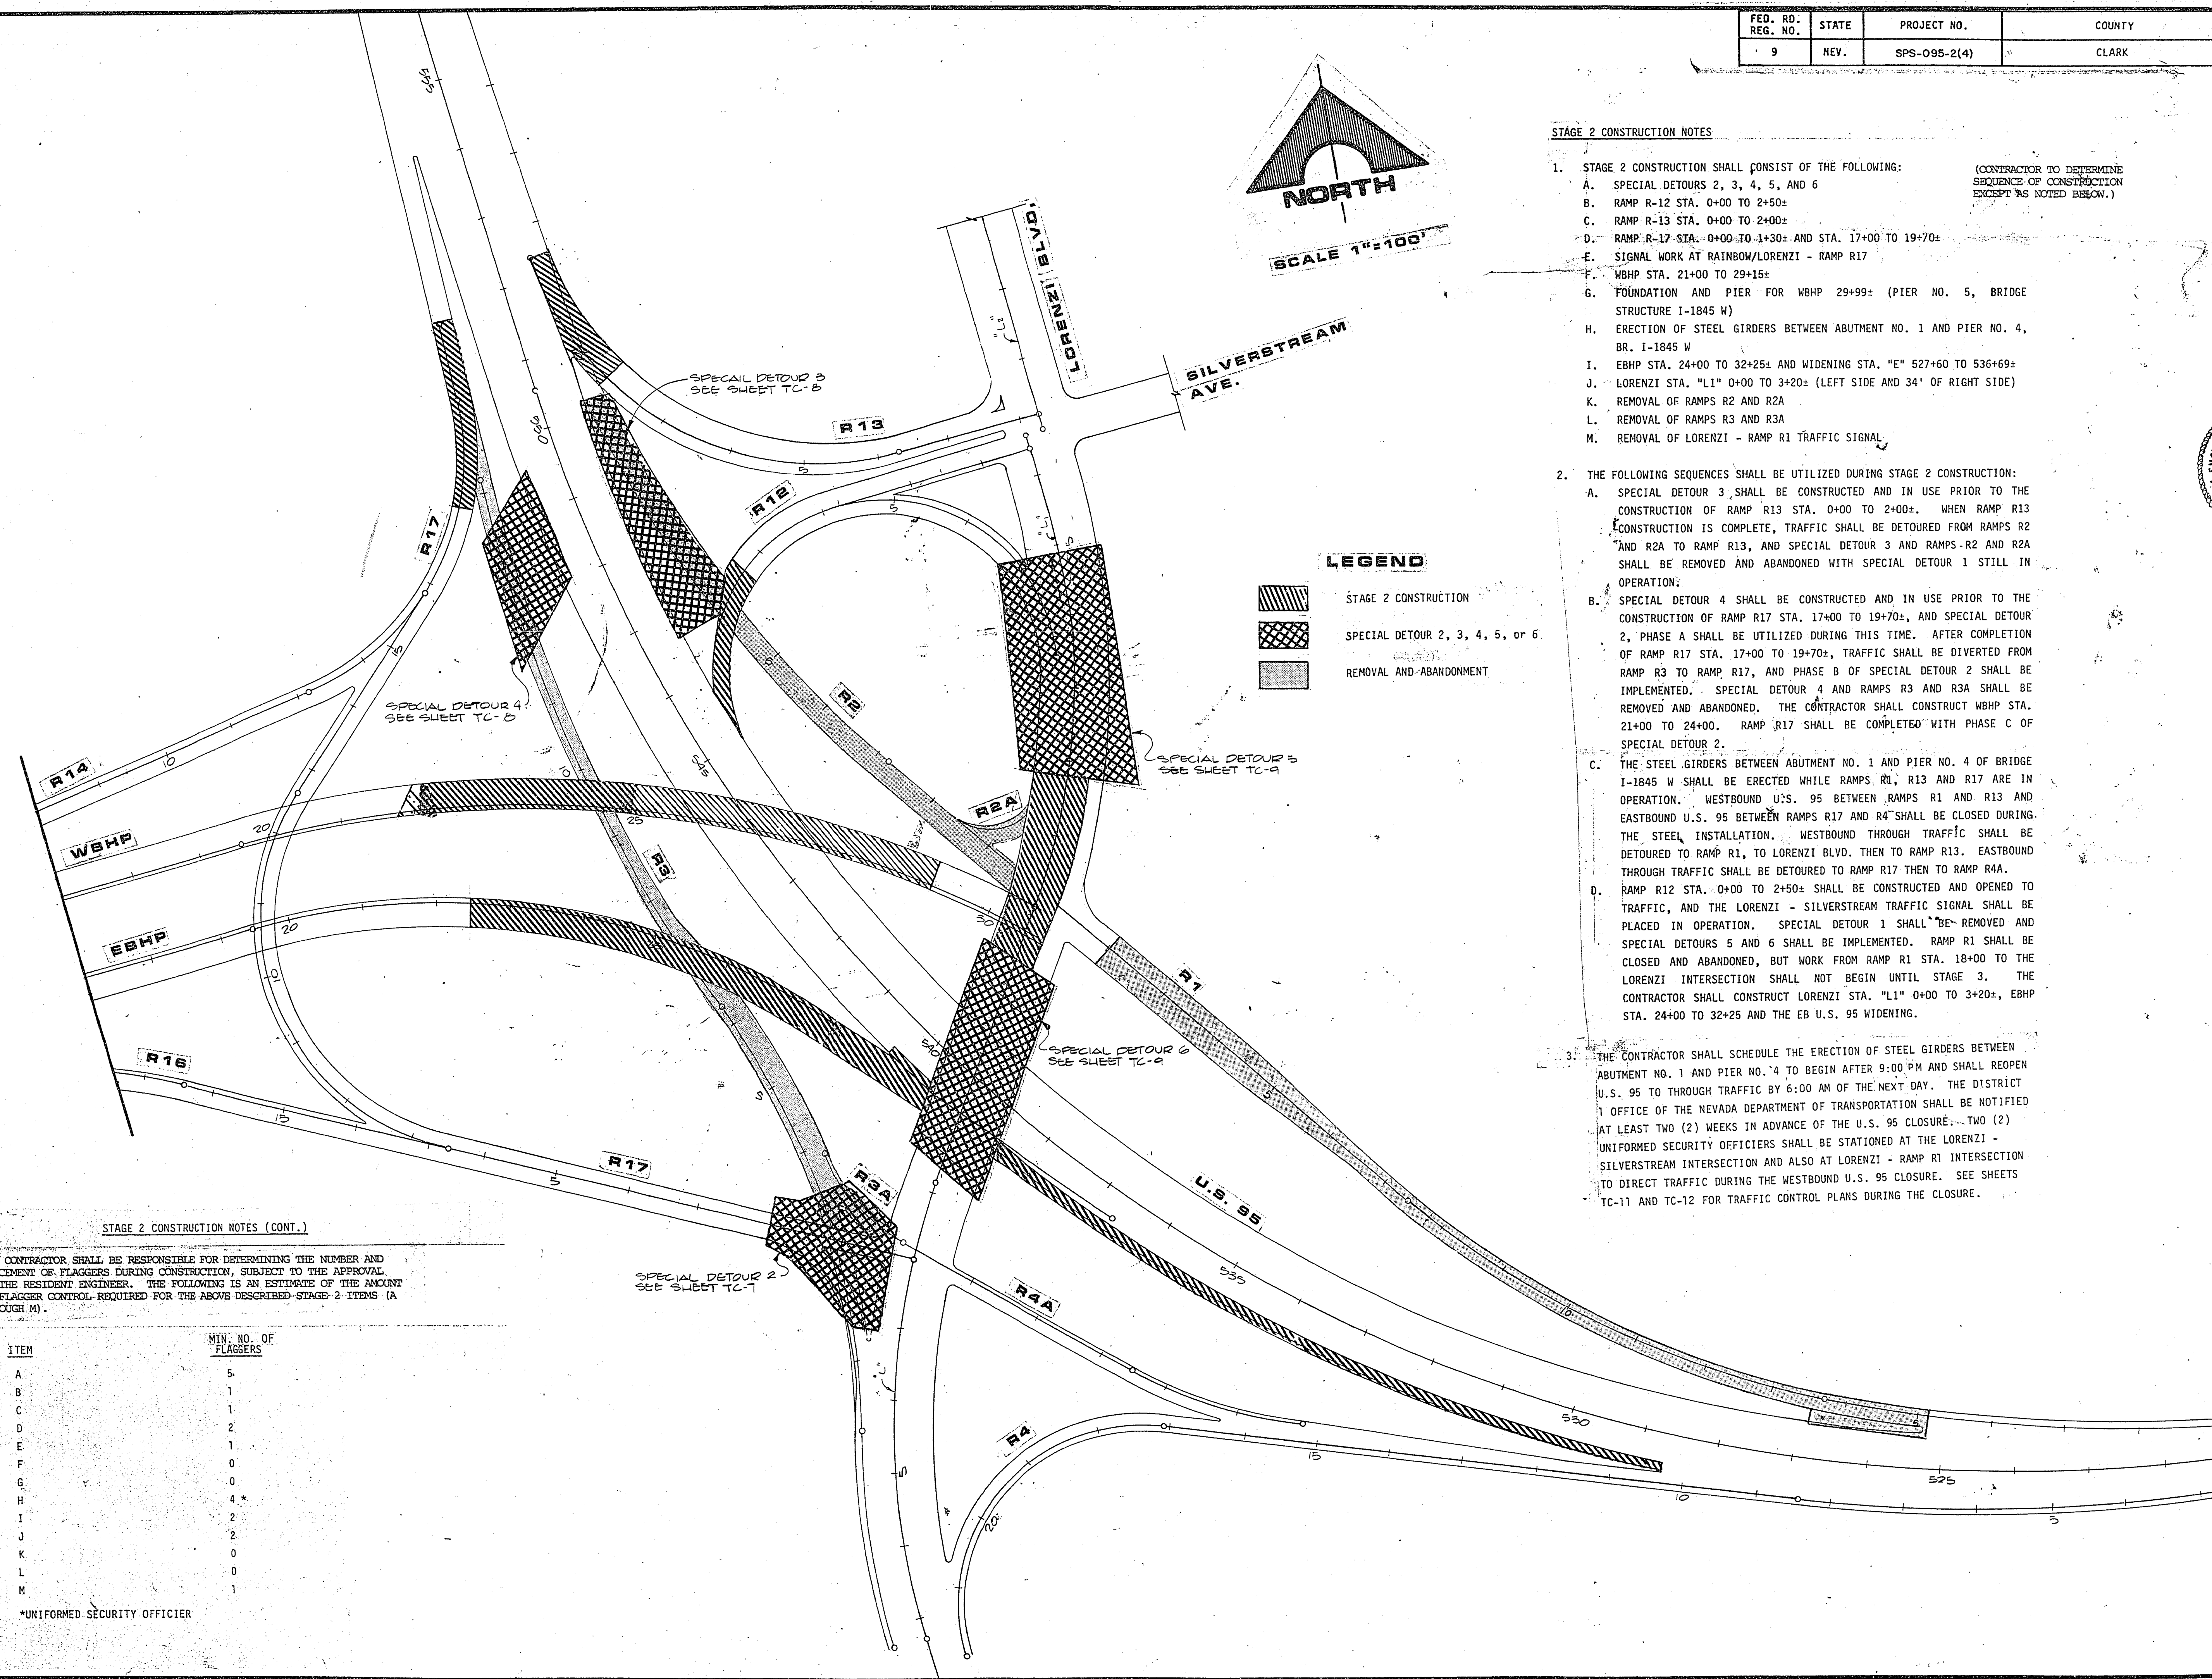

LEGEND

- [Hatched Box] STAGE 2 CONSTRUCTION
- [Cross-hatched Box] SPECIAL DETOUR 2, 3, 4, 5, or 6
- [Solid Grey Box] REMOVAL AND ABANDONMENT

STAGE 2 CONSTRUCTION NOTES

- STAGE 2 CONSTRUCTION SHALL CONSIST OF THE FOLLOWING: (CONTRACTOR TO DETERMINE SEQUENCE OF CONSTRUCTION EXCEPT AS NOTED BELOW.)
 - SPECIAL DETOURS 2, 3, 4, 5, AND 6
 - RAMP R-12 STA. 0+00 TO 2+50±
 - RAMP R-13 STA. 0+00 TO 2+00±
 - RAMP R-17 STA. 0+00 TO 1+30± AND STA. 17+00 TO 19+70±
 - SIGNAL WORK AT RAINBOW/LORENZI - RAMP R17
 - WBHP STA. 21+00 TO 29+15±
 - FOUNDATION AND PIER FOR WBHP 29+99± (PIER NO. 5, BRIDGE STRUCTURE I-1845 W)
 - ERECTION OF STEEL GIRDERS BETWEEN ABUTMENT NO. 1 AND PIER NO. 4, BR. I-1845 W
 - EBHP STA. 24+00 TO 32+25± AND WIDENING STA. "E" 527+60 TO 536+69±
 - LORENZI STA. "L1" 0+00 TO 3+20± (LEFT SIDE AND 34' OF RIGHT SIDE)
 - REMOVAL OF RAMPS R2 AND R2A
 - REMOVAL OF RAMPS R3 AND R3A
 - REMOVAL OF LORENZI - RAMP R1 TRAFFIC SIGNAL
- THE FOLLOWING SEQUENCES SHALL BE UTILIZED DURING STAGE 2 CONSTRUCTION:
 - SPECIAL DETOUR 3 SHALL BE CONSTRUCTED AND IN USE PRIOR TO THE CONSTRUCTION OF RAMP R13 STA. 0+00 TO 2+00±. WHEN RAMP R13 CONSTRUCTION IS COMPLETE, TRAFFIC SHALL BE DETOURED FROM RAMPS R2 AND R2A TO RAMP R13, AND SPECIAL DETOUR 3 AND RAMPS R2 AND R2A SHALL BE REMOVED AND ABANDONED WITH SPECIAL DETOUR 1 STILL IN OPERATION.
 - SPECIAL DETOUR 4 SHALL BE CONSTRUCTED AND IN USE PRIOR TO THE CONSTRUCTION OF RAMP R17 STA. 17+00 TO 19+70±, AND SPECIAL DETOUR 2, PHASE A SHALL BE UTILIZED DURING THIS TIME. AFTER COMPLETION OF RAMP R17 STA. 17+00 TO 19+70±, TRAFFIC SHALL BE DIVERTED FROM RAMP R3 TO RAMP R17, AND PHASE B OF SPECIAL DETOUR 2 SHALL BE IMPLEMENTED. SPECIAL DETOUR 4 AND RAMPS R3 AND R3A SHALL BE REMOVED AND ABANDONED. THE CONTRACTOR SHALL CONSTRUCT WBHP STA. 21+00 TO 24+00. RAMP R17 SHALL BE COMPLETED WITH PHASE C OF SPECIAL DETOUR 2.
 - THE STEEL GIRDERS BETWEEN ABUTMENT NO. 1 AND PIER NO. 4 OF BRIDGE I-1845 W SHALL BE ERECTED WHILE RAMPS R1, R13 AND R17 ARE IN OPERATION. WESTBOUND U.S. 95 BETWEEN RAMPS R1 AND R13 AND EASTBOUND U.S. 95 BETWEEN RAMPS R17 AND R4 SHALL BE CLOSED DURING THE STEEL INSTALLATION. WESTBOUND THROUGH TRAFFIC SHALL BE DETOURED TO RAMP R1, TO LORENZI BLVD. THEN TO RAMP R13. EASTBOUND THROUGH TRAFFIC SHALL BE DETOURED TO RAMP R17 THEN TO RAMP R4A.
 - RAMP R12 STA. 0+00 TO 2+50± SHALL BE CONSTRUCTED AND OPENED TO TRAFFIC, AND THE LORENZI - SILVERSTREAM TRAFFIC SIGNAL SHALL BE PLACED IN OPERATION. SPECIAL DETOUR 1 SHALL BE REMOVED AND SPECIAL DETOURS 5 AND 6 SHALL BE IMPLEMENTED. RAMP R1 SHALL BE CLOSED AND ABANDONED, BUT WORK FROM RAMP R1 STA. 18+00 TO THE LORENZI INTERSECTION SHALL NOT BEGIN UNTIL STAGE 3. THE CONTRACTOR SHALL CONSTRUCT LORENZI STA. "L1" 0+00 TO 3+20±, EBHP STA. 24+00 TO 32+25 AND THE EB U.S. 95 WIDENING.
- THE CONTRACTOR SHALL SCHEDULE THE ERECTION OF STEEL GIRDERS BETWEEN ABUTMENT NO. 1 AND PIER NO. 4 TO BEGIN AFTER 9:00 PM AND SHALL REOPEN U.S. 95 TO THROUGH TRAFFIC BY 6:00 AM OF THE NEXT DAY. THE DISTRICT OFFICE OF THE NEVADA DEPARTMENT OF TRANSPORTATION SHALL BE NOTIFIED AT LEAST TWO (2) WEEKS IN ADVANCE OF THE U.S. 95 CLOSURE. TWO (2) UNIFORMED SECURITY OFFICERS SHALL BE STATIONED AT THE LORENZI - SILVERSTREAM INTERSECTION AND ALSO AT LORENZI - RAMP R1 INTERSECTION TO DIRECT TRAFFIC DURING THE WESTBOUND U.S. 95 CLOSURE. SEE SHEETS TC-11 AND TC-12 FOR TRAFFIC CONTROL PLANS DURING THE CLOSURE.

STAGE 2 CONSTRUCTION NOTES (CONT.)

4. THE CONTRACTOR SHALL BE RESPONSIBLE FOR DETERMINING THE NUMBER AND PLACEMENT OF FLAGGERS DURING CONSTRUCTION, SUBJECT TO THE APPROVAL OF THE RESIDENT ENGINEER. THE FOLLOWING IS AN ESTIMATE OF THE AMOUNT OF FLAGGER CONTROL REQUIRED FOR THE ABOVE DESCRIBED STAGE 2 ITEMS (A THROUGH M).

ITEM	MIN. NO. OF FLAGGERS
A	5
B	1
C	1
D	2
E	1
F	0
G	0
H	4*
I	2
J	2
K	0
L	0
M	1

*UNIFORMED SECURITY OFFICIER

REVISIONS

REV	DATE	DESCRIPTION
1	8/12/87	ISSUE FOR GMP
2	8/12/87	ISSUE FOR CONSTRUCTION

REGISTERED PROFESSIONAL ENGINEER

JAMES A. DUDLEY

CIVIL

1555 SOUTH RAINBOW BLVD. LAS VEGAS, NEVADA 89102

HOWARD HUGHES PROPERTIES

HUBITE PARKWAY INTERCHANGE

TRAFFIC CONTROL PLAN

STAGE 2

SHEET 31

TC-4

OF 130 SHEETS

76-3 83 107-V1882
