
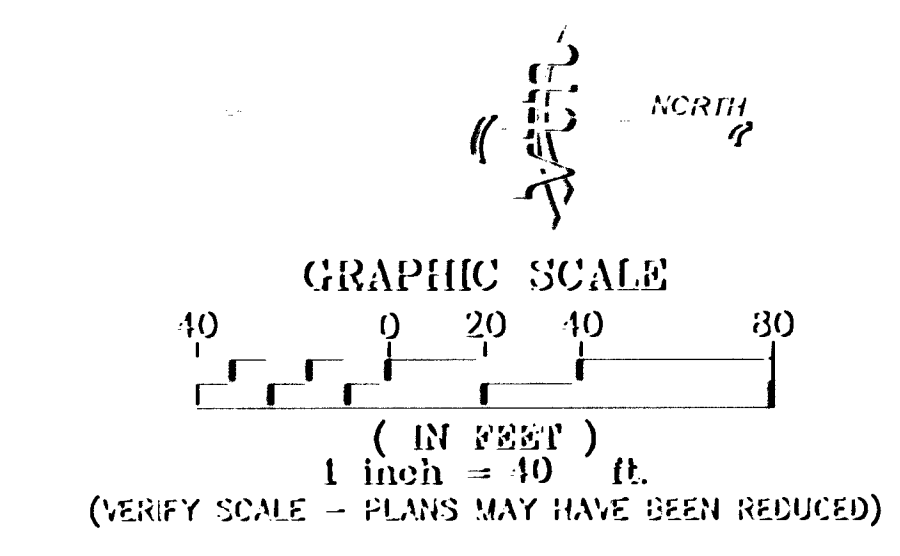


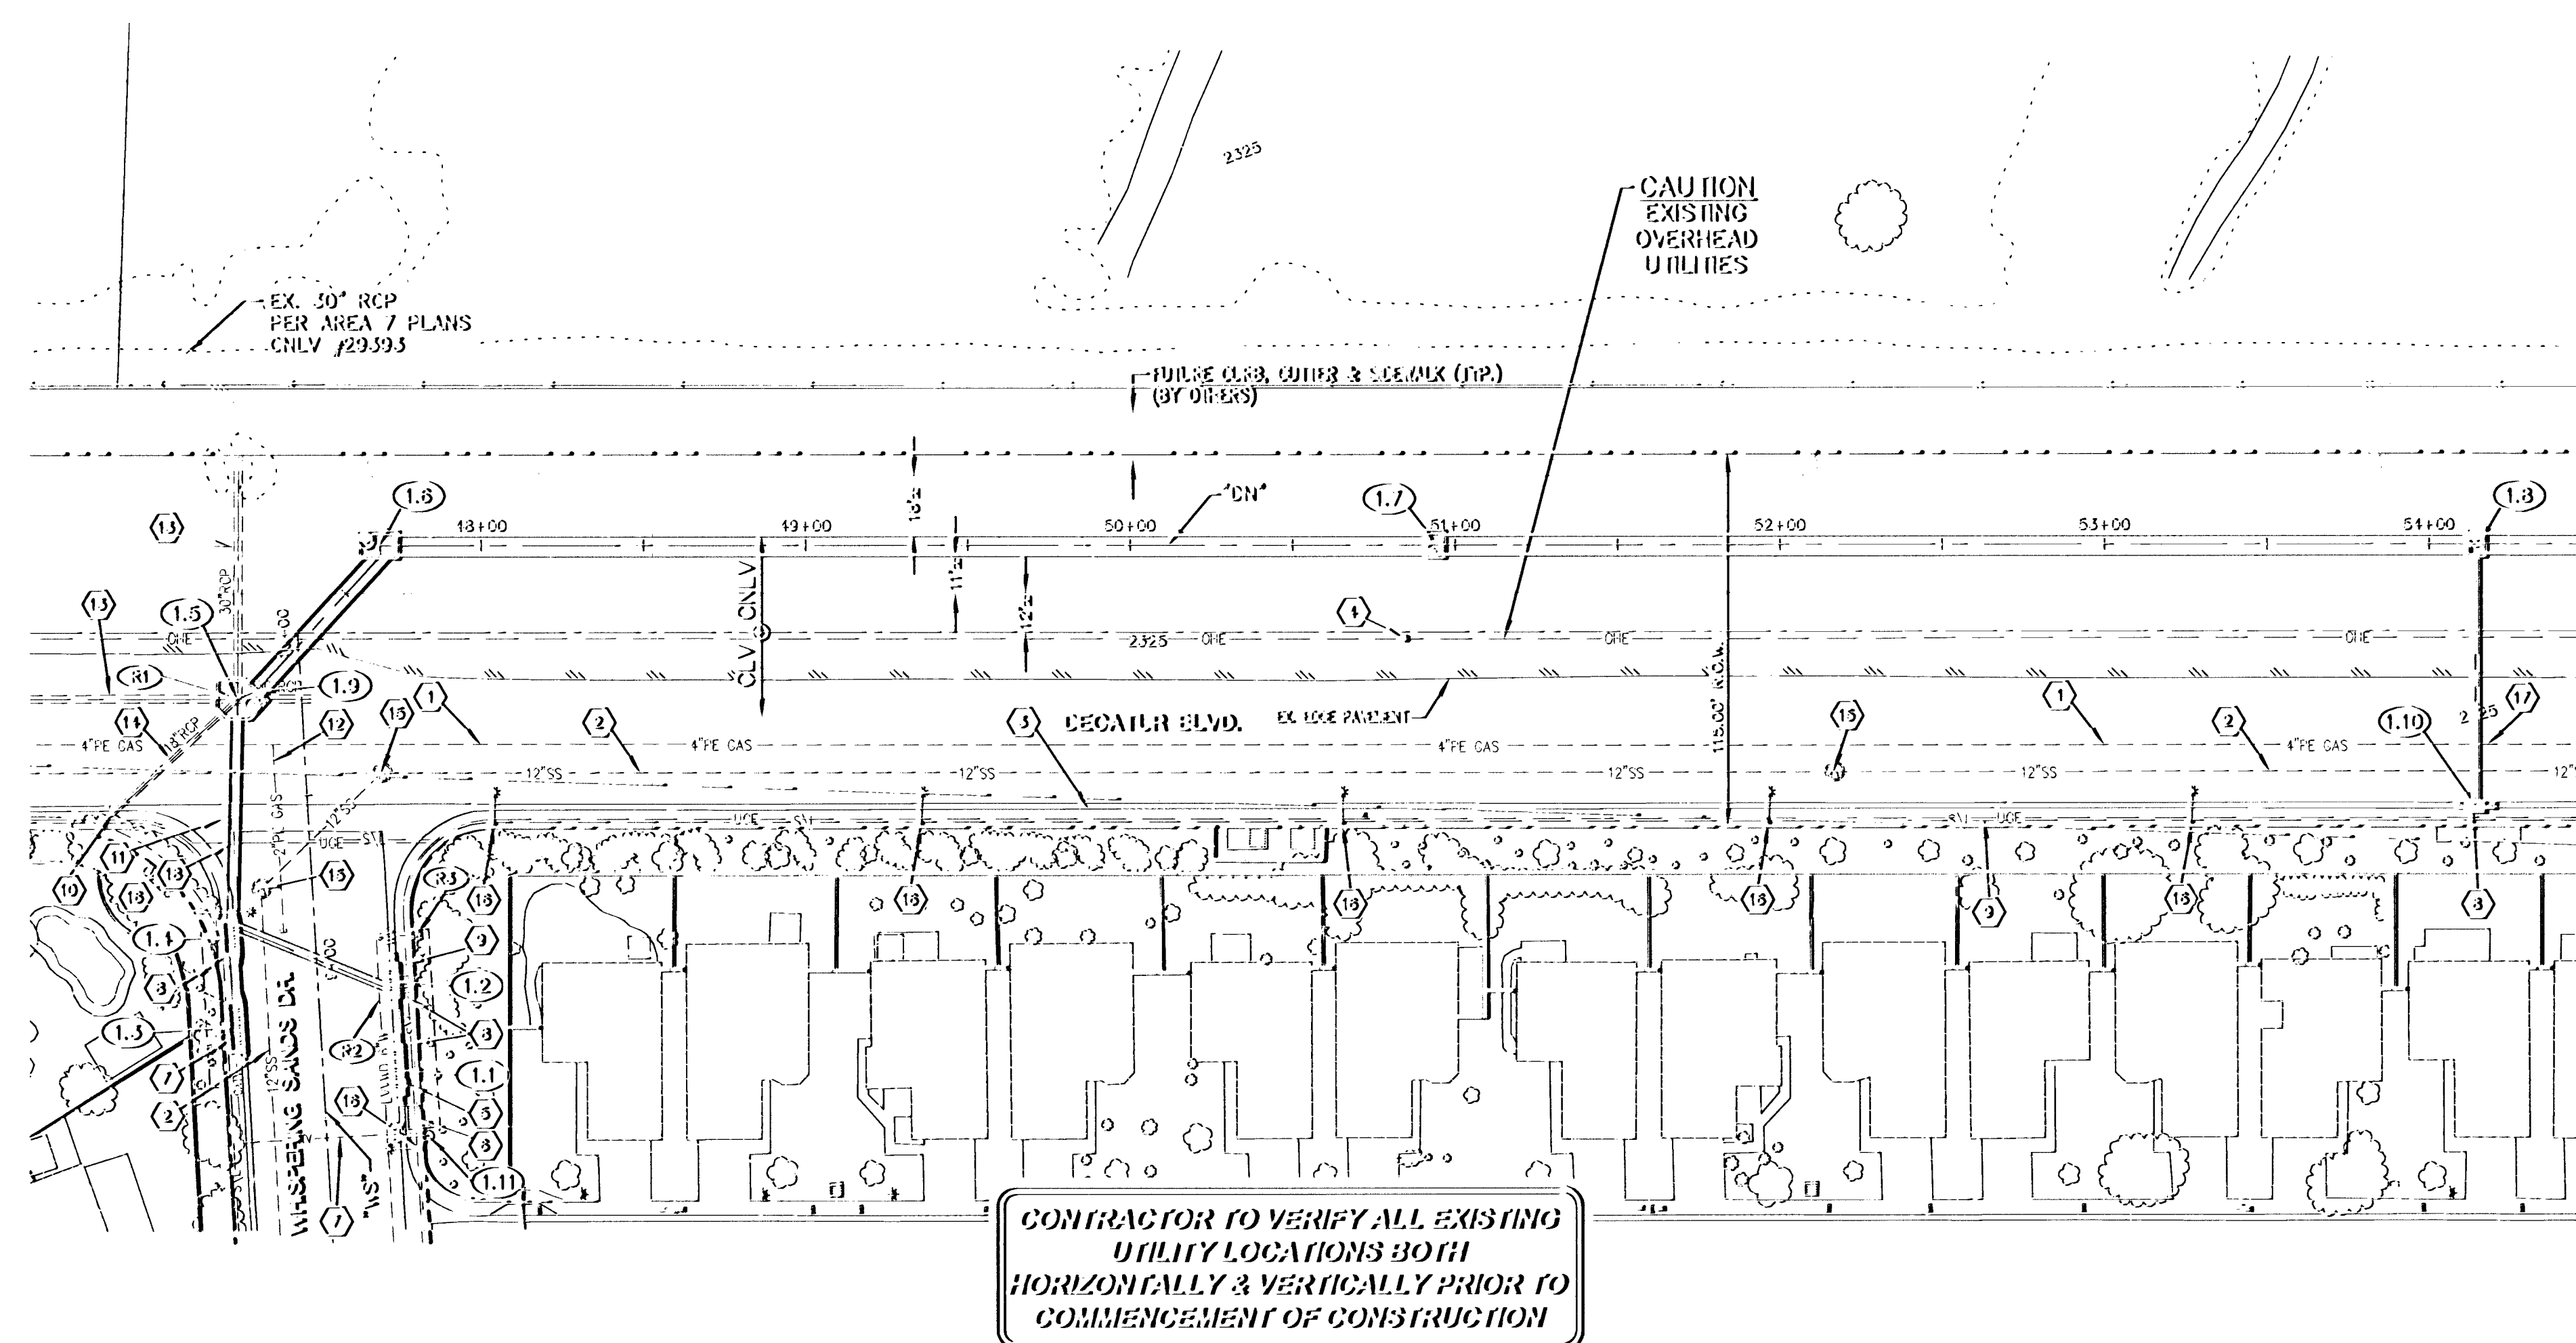

STORM DRAIN CONSTRUCTION NOTES

- (1.1) "WS" 3+83.90, 25.00' RT
INSTALL 15" TYPE "DM28" D.I.
PER DETAIL CN SHEET D2
PLACE SANDBAGS AROUND D.I.
PER DETAIL CN SHEET D1
INSTALL 15.50 L.F. 30" RCP
SEE PROFILE 2 SHEET SD1
- (1.2) "WS" 3+91.10, 25.00' RT
INSTALL 10" TYPE "DM28" D.I.
PER DETAIL CN SHEET D2
PLACE SANDBAGS AROUND D.I.
PER DETAIL CN SHEET D1
INSTALL 50.25 L.F. 30" RCP
SEE PROFILE 2 SHEET SD1
- (1.3) "WS" 3+99.93, 25.00' LT
INSTALL 15" TYPE "DM28" D.I.
PER DETAIL CN SHEET D2
PLACE SANDBAGS AROUND D.I.
PER DETAIL CN SHEET D1
INSTALL 15.50 L.F. 30" RCP
SEE PROFILE 1 SHEET SD1
- (1.4) "WS" 3+07.13, 25.00' LT
INSTALL 10" TYPE "DM28" D.I.
PER DETAIL CN SHEET D2
PLACE SANDBAGS AROUND D.I.
PER DETAIL CN SHEET D1
INSTALL 83.28 L.F. 30" RCP
SEE PROFILE 1&2 SHEET SD1
- (1.5) "DN" 47+03.18
INSTALL JUNCTION STRUCTURE
FOR STRUCTURAL DETAIL REFER
TO SHEET S4
INSTALL 58.28 L.F. 88" RCP
- (1.6) "DN" 47+88.90
INSTALL MOD. NDOT TYPE 4 SCMH
FOR STRUCTURAL DETAIL REFER
TO SHEET S5
INSTALL 318.21 L.F. 88" RCP
- (1.7) "DN" 50+94.82
INSTALL NDOT TYPE 4 SCMH
PER NDOT SID. DWG. R-4.3.2
INSTALL 318.58 L.F. 88" RCP
- (1.8) "DN" 51+15.13
INSTALL NDOT TYPE 4 SCMH
PER NDOT SID. DWG. R-4.3.2
INSTALL 318.58 L.F. 88" RCP
- (1.9) "DN" 47+09.38
INSTALL RCP END CAP
PER DETAIL CN SHEET D1
- (1.10) "DN" 51+15.13, 79.75' RT
INSTALL 5" TYPE "DM28" D.I.
PER DETAIL CN SHEET D2
PLACE SANDBAGS AROUND D.I.
PER DETAIL CN SHEET D1
INSTALL 78.18 L.F. 18" RCP
SEE PROFILE 3 SHEET SD3
- (1.11) INSTALL FIRE HYDRANT SEE
SHEET U2

REMOVAL NOTES

- (R1) REMOVE EX. SCMH
- (R2) ABANDON AND/OR REMOVE EX. 8" PVC WIR SEE SHEET U2
- (R3) REMOVE EX. FIRE HYDRANT ASSEMBLY
SEE SHEET U2

MECHANICAL CONSTRUCTION NOTES

- (1) EX. 4" PE GAS - PROTECT IN PLACE
- (2) EX. 12" SANITARY SEWER - PROTECT IN PLACE
- (3) EX. CURB, CUTTER, SIDEWALK & UTILS. - PROTECT IN-PLACE
- (4) EX. POWER POLE - PROTECT IN-PLACE
- (5) EX. ELEC. BOX - TO BE RELOCATED BY NPC
- (6) EX. ELEC. VAULT - PROTECT IN-PLACE
- (7) EX. UNDERGROUND CATV - TO BE RELOCATED BY COX
- (8) REMOVE AND REPLACE CURB, CUTTER AND SIDEWALK AS REQUIRED
FOR D.I. CONSTRUCTION, PROTECT EX. DRY UTILITIES IN PLACE.
- (9) EX. UNDERGROUND ELEC - PROTECT IN PLACE
- (10) EX. CRCP INLET - PROTECT IN PLACE
FOR LATERAL CONSTRUCTION
- (11) REMOVE AND REPLACE VALLEY CUTTER AS NEEDED
- (12) EX. 2" PE GAS - PROTECT IN PLACE
- (13) EX. 30" RCP SD - PROTECT IN PLACE
- (14) EX. 18" RCP SD - PROTECT IN PLACE
- (15) EX. SANITARY SEWER MH - PROTECT IN PLACE
- (16) EX. STREET LIGHT - PROTECT IN PLACE
- (17) EX. 4" PE GAS - TO BE RELOCATED BY SWG
- (18) EX. UNDERGROUND ELEC - TO BE
RELOCATED BY NPC

THE ONLY 4" W IS INTENDED TO BE
USED FOR IRRIGATION PURPOSES
ONLY. DOMESTIC CONNECTIONS
WILL NOT BE ALLOWED

NOTE:
1. FINISHED GROUND ABOVE RCP
AND STORM DRAIN STRUCTURES
SHALL BE EXISTING GROUND OR
TWO FEET OF COVER, WHICHEVER
IS GREATER.
2. FOR FIRE HYDRANT RELOCATION
SEE SHEET U2


APPROVED
[Signature] 8-13-03
Las Vegas Valley Water District

AND WHENEVER POWER LINE
CONTACT, IT'S COSTLY

Call
before you
Overhead

1-702-227-2929
24 HOURS A DAY
SERVICES DEPENDENT

Call
811
1-800-227-2929
1-800-227-2929

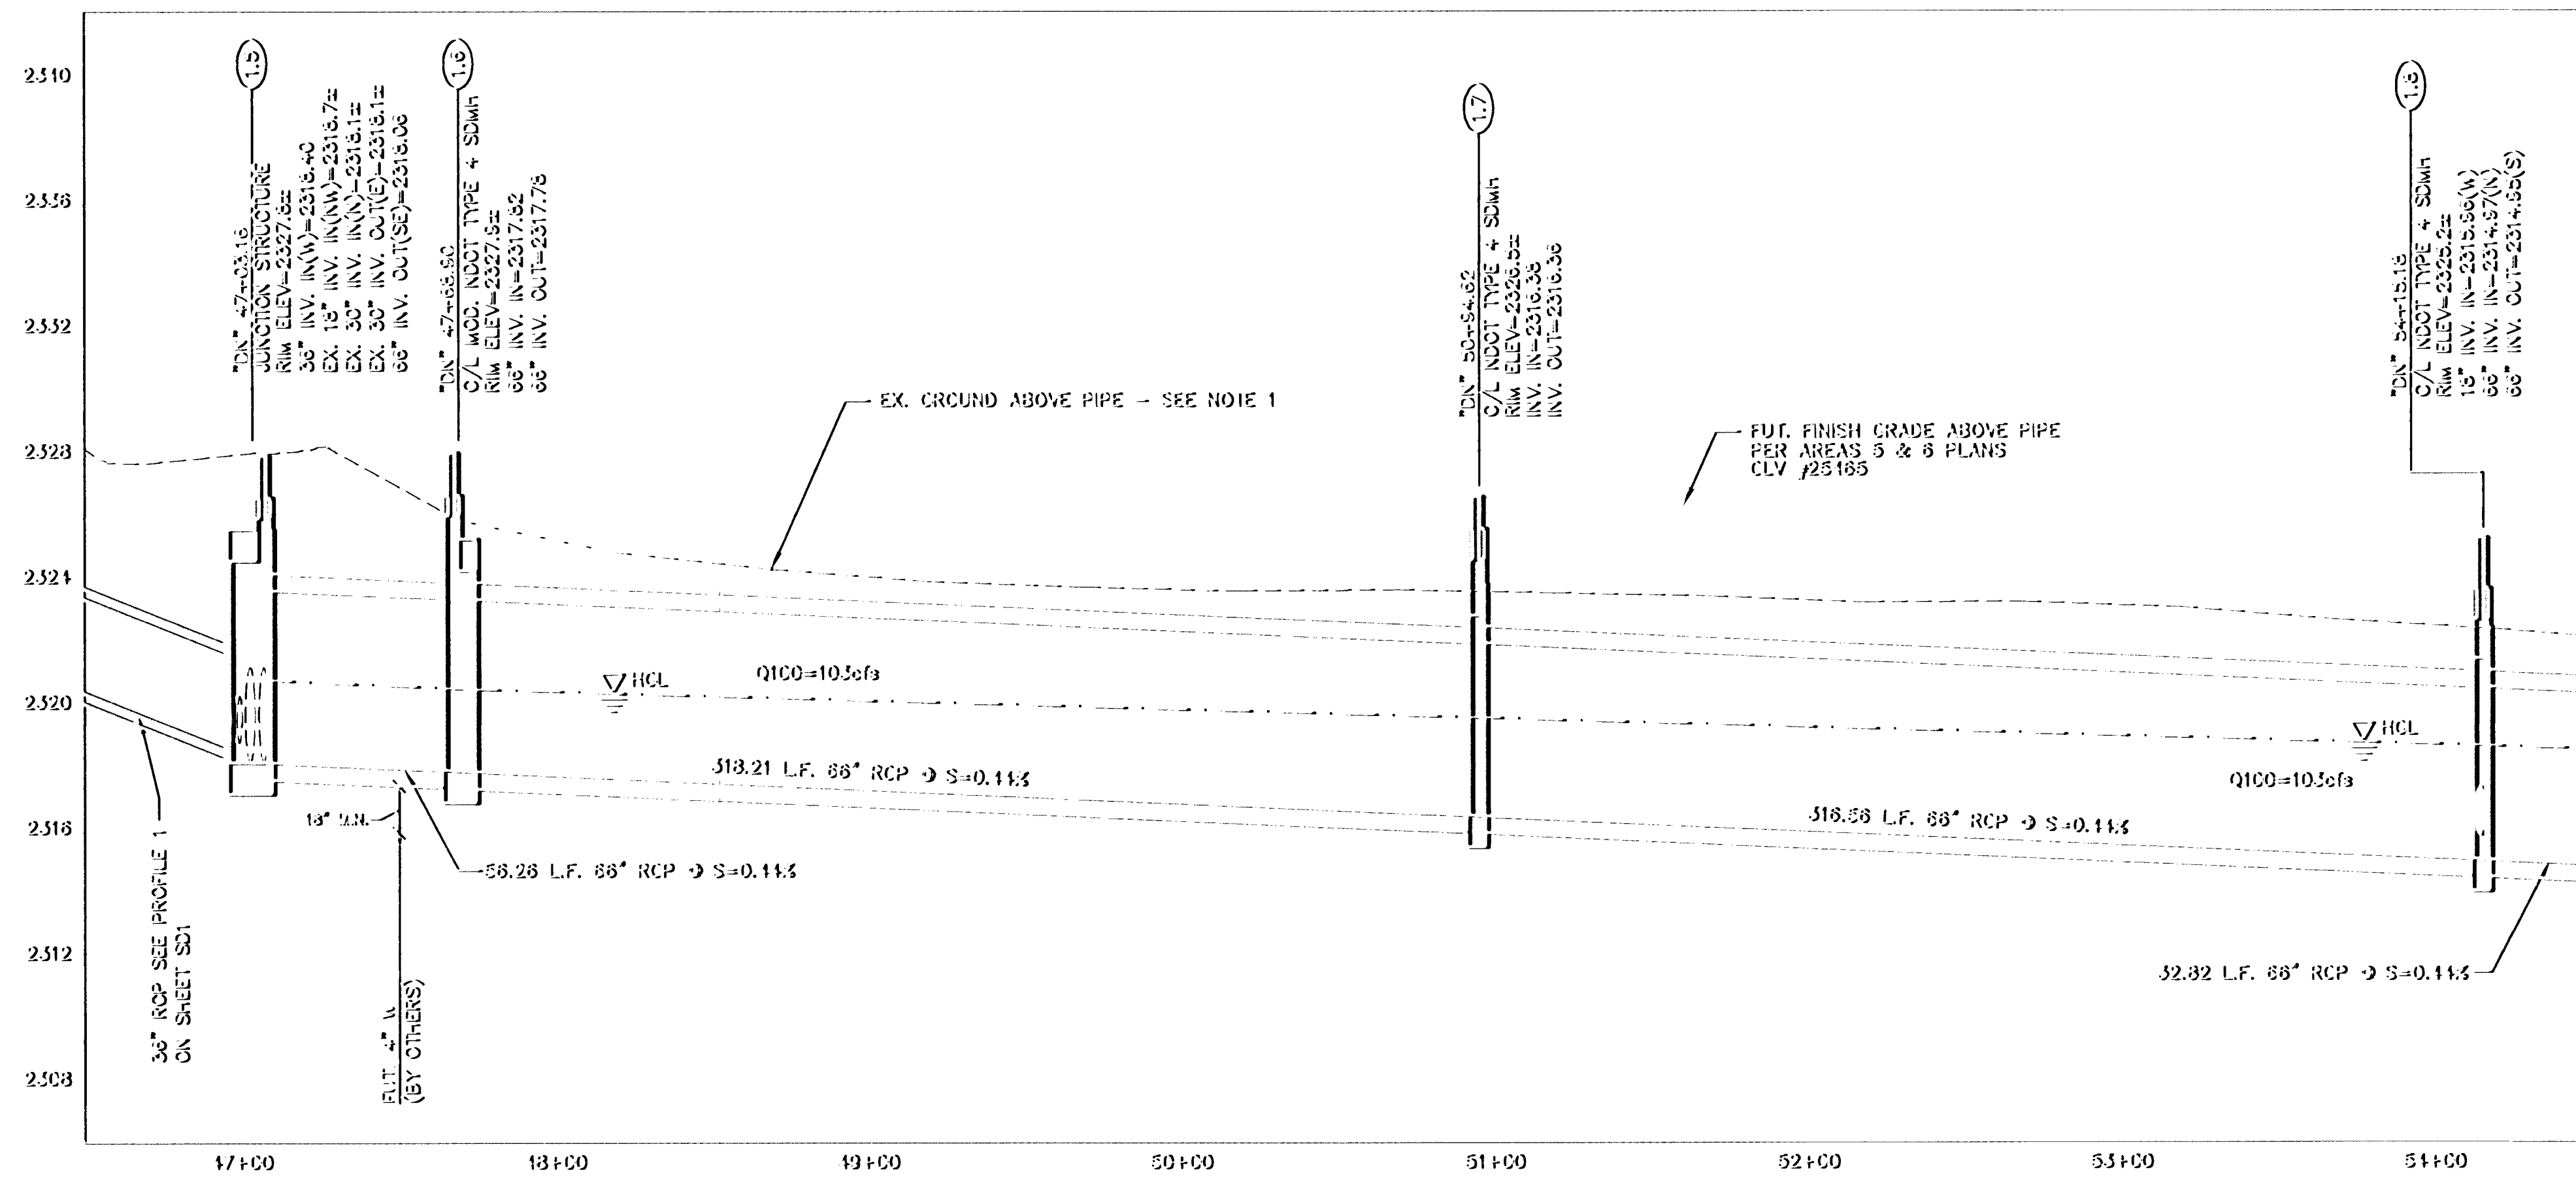

113755

PUBLIC WORKS DEPARTMENT 222 SOUTH BURNING WOODS AVENUE LAS VEGAS, NV 89101 TEL: (702) 227-2929 FAX: (702) 227-2929 WEB SITE: WWW.LVWPD.COM		DATE: _____ BY: _____ REV: _____
CONSTRUCTION PLAN & PROFILE "DN" 43+00 TO "DN" 54+00 LAS VEGAS WASH MIDDLE BRANCH DECREE BOULEVARD EL CAMINO ROAD TO WASHINGTON SAUS DRIVE		DRAWN BY: _____ DESIGNED BY: _____ CHECKED BY: _____ PROJECT NO: _____ SCALE: HORIZ. 1"=40' VERT. 1"=4' SHEET 1 OF 25 SHEETS DRAWING NO. 731-37-1
